

Job Name: 26-3221 - Ulta Gateway Commons
Job Location: Owensboro, KY
Contractor: Winwater Hartford KY Co.

Plant: 100

9/25/2026 11:46:08 AM

Tech: Jared - F

PC: A.Chambers



Structure ID: I-1 SS-MH

P4 GR4CDARED

GRADE RING w/ConBlock-CDA Red F/F

P5) 24" - CASTING HEIGHT - 7"
P4) 24" - GRADE RING w/ConBlock-CDA Red F/F - 4"
P3) 48" - ECC CONE w/ 24" HOLE, w/ConBlock-CDA Red F/G - 42"
P2) 48" - MH RISER w/ConBlock-CDA Red T/G - 72"
P1) 48" - MH BASE w/FLANGE (08F/08EF) w/ConBlock-CDA Red T/n - 24"
1) JOINT WRAP - 0.065"x6"x50' CONSEAL CS212
1) 48" - MH INVERT CHANNEL w/ConBlock-CDA Red - FULL HEIGHT
1) JOINT WRAP PRIMER - CONSEAL CS-75 (1 gal.)
1) ADMIXTURE CONBLOCK CDA RED
1) CASTING - HOE MC-315 F/C RWRA
2) 48" - Conseal CS-102 1.00" (Double)
2) 24" - Conseal CS-102 1.00" (Double)
2) PSX - 12-08 NYLO
1) PSX - 12-06 NYLO
12) MH Step ML-10-TDS-NCR - 10"

0 lb
270 lb
3116 lb
5030 lb
4420 lb
0 lb
1440 lb
0 lb
0 lb
258 lb
0 lb
0 lb
16 lb
8 lb
0 lb


Structure Total: 14558 lb

Structure Notes:


1. PER ASTM C478 SPECIFICATIONS.
 2. CONCRETE = 4,000 PSI AT 28 DAYS.
 3. ADMIXTURE = CONBLOCK CDA RED.
 4. CASTING BY ICAST (HOE MC-315 F/C RWRA SANITARY).
- REINFORCING PER ASTM A615 (GRADE 60).
- CONE (As .12)
 - RISER/WALLS (As .12)
 - FLOOR (As .31) #5 BARS AT 12" C.C.E.W.

NOTES:

1. GRADE RINGS MEET OR EXCEED THE FOLLOWING SPECIFICATIONS:
 - CONCRETE: 4,000 PSI @ 28 DAYS.
 - REINFORCING: (1) #3 HOOP CENTERED (GRADE 60)
2. WEIGHT: 4" 270 LBS.
3. ADMIXTURE: CONBLOCK CDA RED

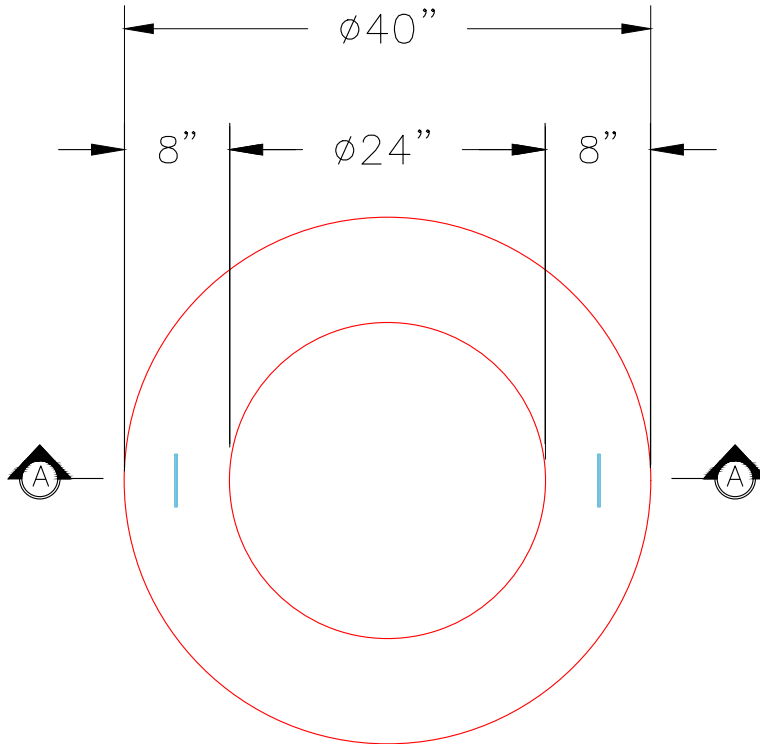


PLAN VIEW

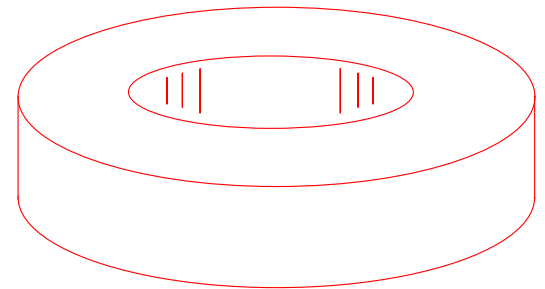

ISOMETRIC VIEW

2X CONAC WRA016 WIRE
ROPE LIFTING ANCHORS

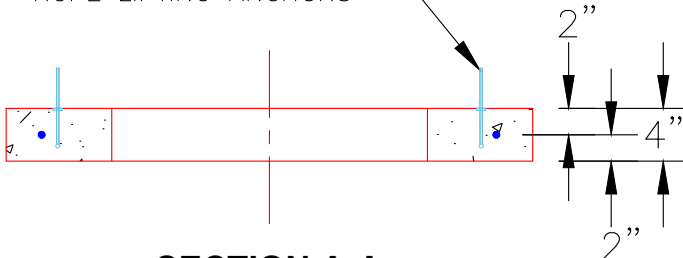

SECTION A-A

Coating (Int):
Coating (Ext):

Seam Up: Flat
Seam Dn: Flat

Wall Thickness: 8"

Height (Ext): 4"

Weight (Net): 270 lb
Volume (Net): 0.07cu.yd
