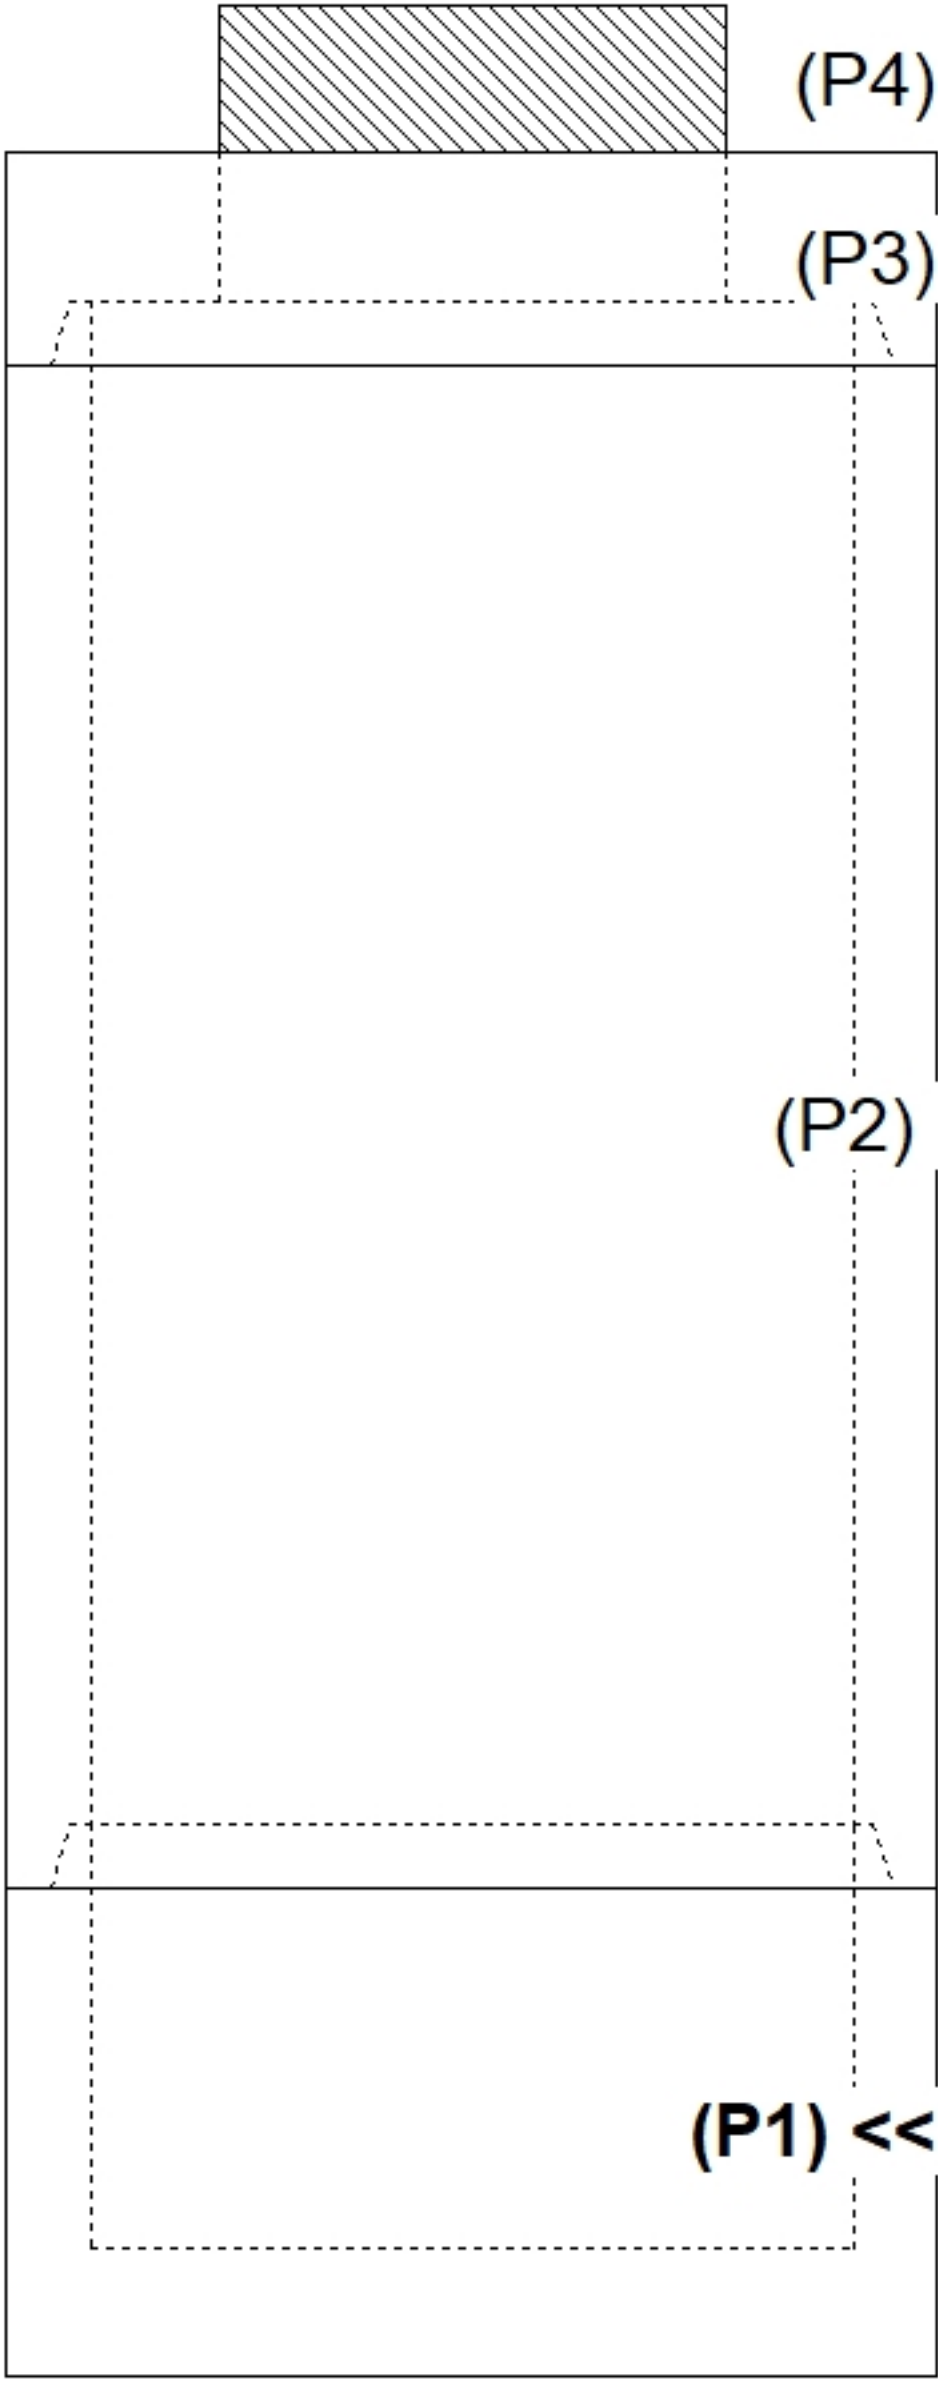
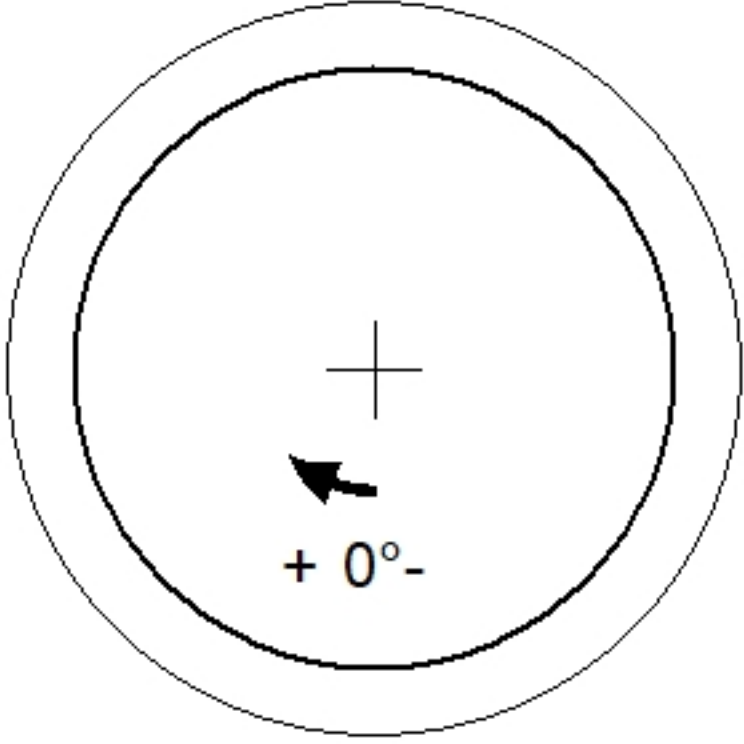
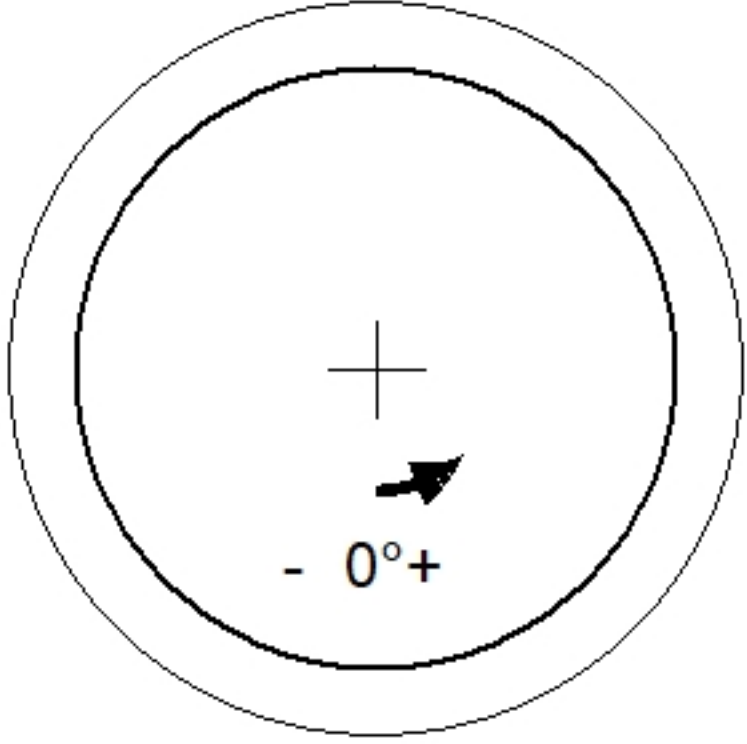
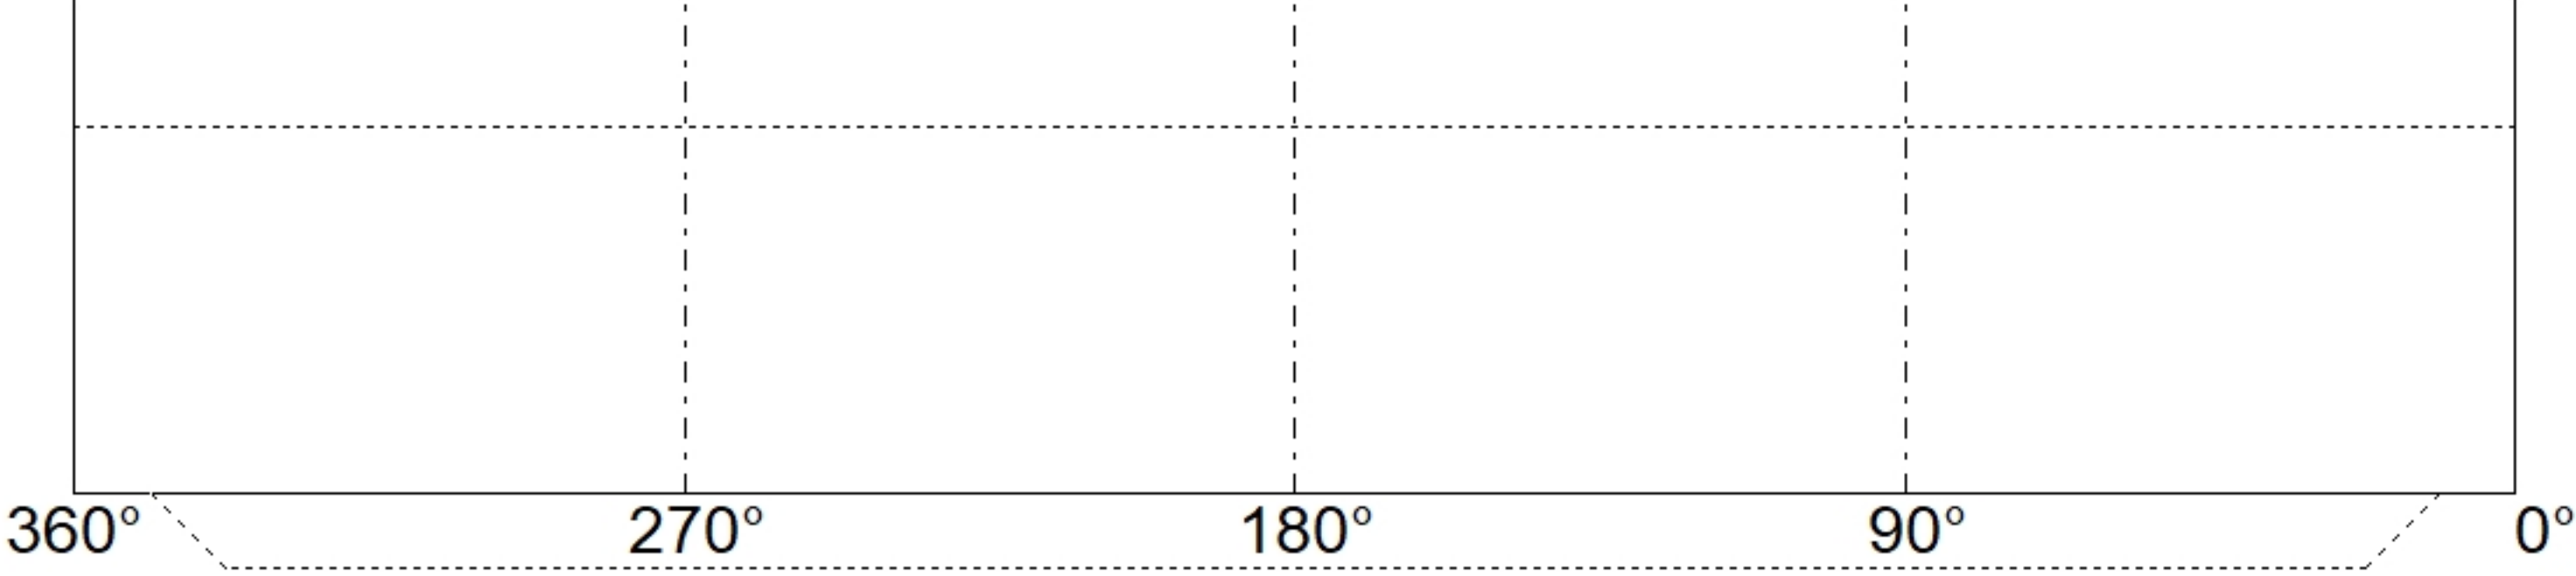



Job Name: 26-3263 ADS Hickory Commerce Center Job Location: Whites Creek, TN 37189 Contractor: ADS Advanced Drainage Systems, Inc.					Plant: Beaver Dam 10/8/2026 3:30:58 PM		Tech: J. Coppage PC:				
Structure ID: WQU C4											
P1 MH036BAVF			MH BASE Custom Ht T/n								
P4) 24" - CASTING HEIGHT - 7" P3) 36" - MH FLAT TOP w/ 24" Ctr. Hole F/G - 10" P2) 36" - MH RISER T/G - 72" P1) 36" - MH BASE Custom Ht T/n - 17" 1) JOINT WRAP - 0.065"x6"x50' CONSEAL CS212 1) JOINT WRAP PRIMER - CONSEAL CS-75 (1 gal.) 1) ASSEMBLY REQUIRED 1) CASTING - JBS 1150 F/C STORM 2) 36" - Conseal CS-102 1.00" 1) 24" - Conseal CS-102 1.00" 2) Hole - 26						0 lb 896 lb 2647 lb 1483 lb 0 lb 0 lb 0 lb 250 lb 0 lb 0 lb 0 lb ----- 5276 lb		Structure Notes: . 1. PER ASTM C478 SPECIFICATIONS. 2. CONCRETE = 4,000 PSI AT 28 DAYS. 3. CASTING BY ICAST (JBS 1150 F/C "STORM"). 4. LIFTING ANCHORS TO BE INSTALLED ON THE OUTSIDE OF THE STRUCTURE. 5. ASSEMBLY REQUIRED. . REINFORCING PER ASTM A615 (GRADE 60). - TOP SLAB (As .62) #5 BARS AT 6" C.C.E.W. - RISER/WALLS (As .12) - FLOOR (As .31) #5 BARS AT 12" C.C.E.W.			
Rim: 514.32' Rim to Invert: 4.29' Slack: 0.44" Sump: 54.96" Step Position:											
Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up ()	Offset	
Invert 1											
Invert 2											
Invert 3											
Invert 4											
Invert 5											
Invert 6											
Invert 7											
Invert 8											
RIGHT-SIDE UP VIEW (int. dimensions)						UPSIDE-DOWN VIEW (int. dimenions)					
											
INSIDE WALL DIMENSIONS											
											
Coating (Int): Coating (Ext):			Seam Up: Tongue Seam Dn: n/a		Wall Thickness: 4" Floor Height: 6"		Height (Int): 17" Height (Ext): 23"		Weight (Net): 1483 lb Volume (Net): 0.38cu.yd		
