




Job Name: 26-3270 - German American Bank Access Roadway Job Location: Bowling Green, KY Contractor: Scott & Ritter, Inc.				Plant: 100 9/16/2026 10:22:05 AM		Tech: Jared - F PC: M. Sullivan				
Structure ID: CBI 1 ST-CI										
P1 MH048BAVF		MH BASE Custom Ht T/n								
P3) 24" x 34" - CASTING HEIGHT - 6.5" P2) 48" - MH FLAT TOP w/24"x34" Hole F/G - 12" P1) 48" - MH BASE Custom Ht T/n - 40" 1) CASTING - JBS 3080 SET (F/G/H) 1) 48" - Conseal CS-102 1.00" 1) Hole - 30 1) Hole - 24 3) MH Step ML-10-TDS-NCR - 10"					0 lb 1839 lb 3659 lb 500 lb 0 lb 0 lb 0 lb 0 lb ----- Structure Total: 5997 lb		Structure Notes: . 1. PER ASTM C478 SPECIFICATIONS. 2. CONCRETE = 4,000 PSI AT 28 DAYS. 3. NO INVERT CHANNEL. 4. CASTING BY ICAST (JBS 3080 SET (F/G/H)). REINFORCING PER ASTM A615 (GRADE 60). - TOP SLAB (As .62) #5 BARS AT 6" C.C.E.W.. - RISER/WALLS (As .12) - FLOOR (As .31) #5 BARS AT 12" C.C.E.W.			
Rim: 527.33' Rim to Invert: 4.72' Slack: 0.09" Sump: 1.95" Step Position: 136°										
Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up ()	Offset
Invert 1	522.61'	0°	0"	24" HP STORM	28"	Hole 30	30"	32.406"	0"	0"
Invert 2	522.61'	272°	137.625"	18" HP STORM	21.4"	Hole 24	24"	25.133"	0.375"	0"
Invert 3										
Invert 4										
Invert 5										
Invert 6										
Invert 7										
Invert 8										

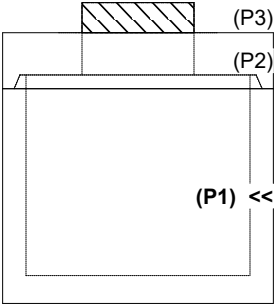


RIGHT-SIDE UP VIEW (int. dimensions)

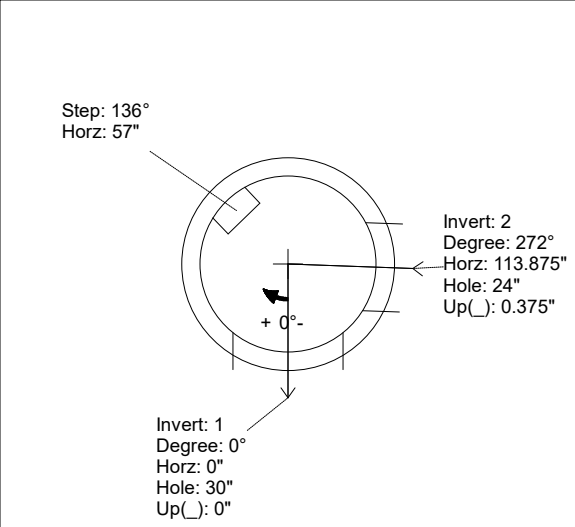

UPSIDE-DOWN VIEW (int. dimensions)

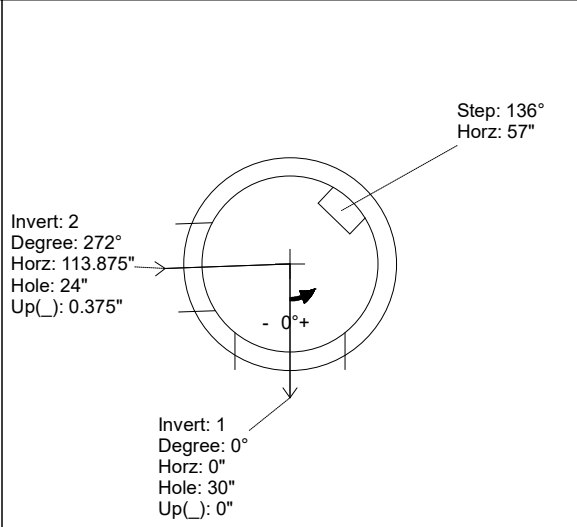

INSIDE WALL DIMENSIONS

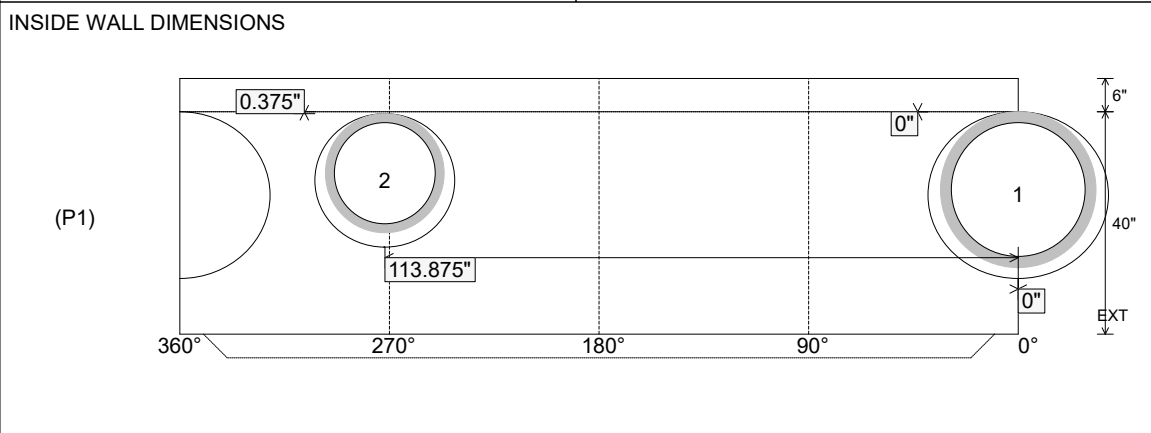

Coating (Int): Coating (Ext):	Seam Up: Tongue Seam Dn: n/a	Wall Thickness: 5" Floor Height: 6"	Height (Int): 40" Height (Ext): 46"	Weight (Net): 3659 lb Volume (Net): 0.94cu.yd
----------------------------------	---------------------------------	--	--	--
