





Job Name: 26-3280 - G.N. Miles Estates Subdivision Ph.4 Job Location: Nicholasville, KY Contractor: PECCO, Inc.					Plant: 100 8/24/2026 11:00:43 AM		Tech: Jared - F PC: A. Chambers			
Structure ID: CI101 CBIA										
P1 BX2436-08BA48 BOX BASE 8inW, 8inF T/n										
P4) 24" x 120" - CB INLET KY A 10' TOP RIGHT F/G - 10" P3) 24" x 120" - CB INLET KY A 10' BOTTOM RIGHT T/G - 18" P2) 24" x 36" - BOX RISER 8inW T/G - 48" P1) 24" x 36" - BOX BASE 8inW, 8inF T/n - 48" 1) CASTING - HOE KY-206 F/C (KY CBI A) 2) 24" x 36" - Conseal CS-102 1.00" 1) Hole - 24 2) Hole - 20					3398 lb 5270 lb 4389 lb 6066 lb 206 lb 0 lb 0 lb 0 lb ----- 19329 lb		Structure Notes: . 1. PER KYTC CBI TYPE A / ASTM C913 SPEC'S. 2. CONCRETE = 4,000 PI AT 28 DAYS. 3. CASTING BY ICAST (HOE KY-206 F/C (KY CBI A)). REINFORCING PER ASTM A615 (GRADE 60). - TOP PHASE (As .62) #5 BARS AT 6" C.C.E.W. - WALLS/RISER (As .31) #5 BARS AT 12" C.C.E.W. - FLOOR (As .31) #5 BARS AT 12" C.C.E.W.			
Rim: 946.36' Rim to Invert: 10.34' Slack: 0.08" Sump: 0" Step Position:										
Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up ()	Offset
Invert 1	936.02'	0°	20"	18" HDPE	21.2"	Hole 24	24"	24"	-1.625"	0"
Invert 2										
Invert 3										
Invert 4										
Invert 5										
Invert 6										
Invert 7										
Invert 8										

RIGHT-SIDE UP VIEW (int. dimensions)

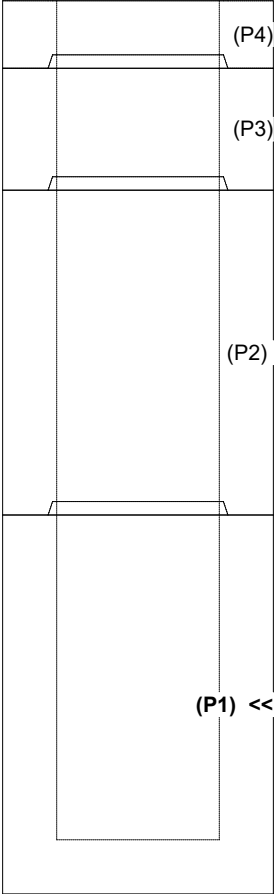

UPSIDE-DOWN VIEW (int. dimensions)

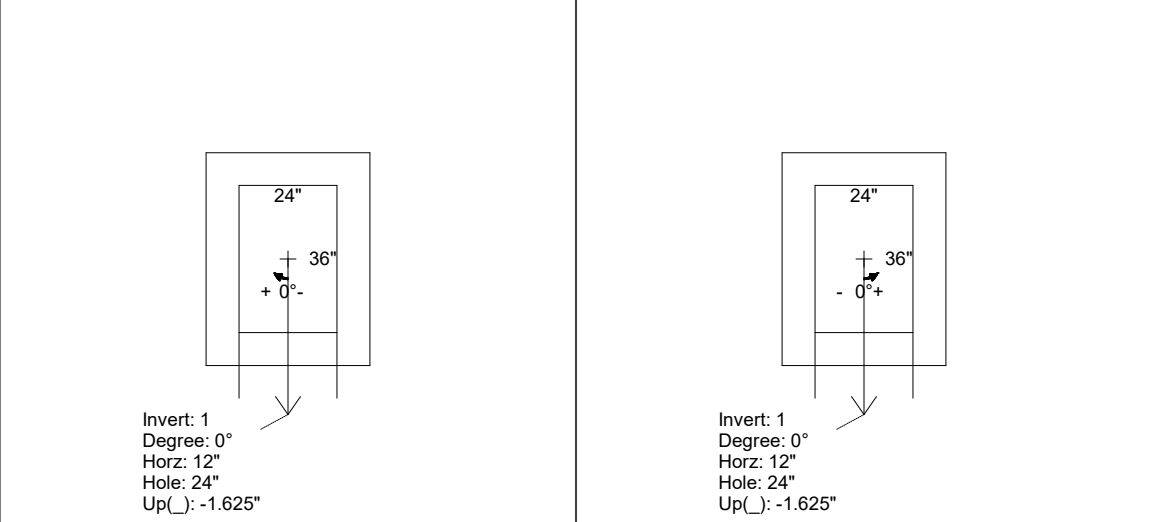

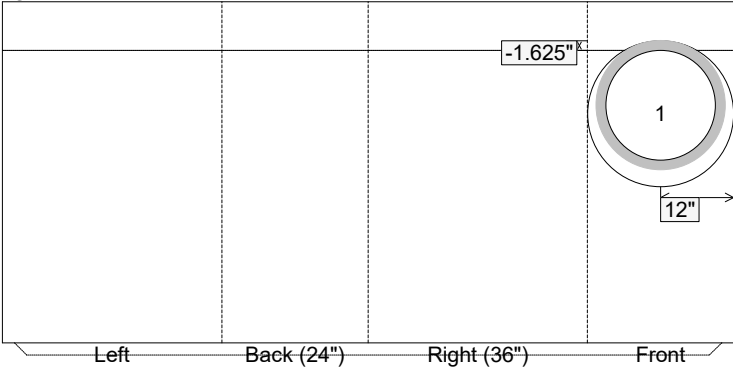INSIDE WALL DIMENSIONS	
	

Coating (Int): Coating (Ext):	Seam Up: Tongue Seam Dn: n/a	Wall Thickness: 8" Floor Height: 8"	Height (Int): 48" Height (Ext): 56"	Weight (Net): 6066 lb Volume (Net): 1.55cu.yd
----------------------------------	---------------------------------	--	--	--
