


Job Name: 26-3280 - G.N. Miles Estates Subdivision Ph.4 Job Location: Nicholasville, KY Contractor: PECCO, Inc.				Plant: 100 8/24/2026 11:00:47 AM		Tech: Jared - F PC: A. Chambers					
Structure ID: CI302 CBIA											
P1 BX2436-08BVF				BOX BASE 8inW, 8inF, Variable Ht T/n							
P3) 24" x 120" - CB INLET KY A 10' TOP LEFT F/G - 10" P2) 24" x 120" - CB INLET KY A 10' BOTTOM LEFT T/G - 18" P1) 24" x 36" - BOX BASE 8inW, 8inF, Variable Ht T/n - 23" 1) CASTING - HOE KY-206 F/C (KY CBI A) 1) 24" x 36" - Conseal CS-102 1.00" 1) Hole - 20				3400 lb 5270 lb 3445 lb 206 lb 0 lb 0 lb ----- Structure Total: 12320 lb		Structure Notes: 1. PER KYTC CBI TYPE A / ASTM C913 SPEC'S. 2. CONCRETE = 4,000 PI AT 28 DAYS. 3. CASTING BY ICAST (HOE KY-206 F/C (KY CBI A)). REINFORCING PER ASTM A615 (GRADE 60). - TOP PHASE (As .62) #5 BARS AT 6" C.C.E.W. - WALLS (As .31) #5 BARS AT 12" C.C.E.W. - FLOOR (As .31) #5 BARS AT 12" C.C.E.W.					
Rim: 948.14'				Rim to Invert: 4.25'		Slack: 0"		Sump: 0"		Step Position:	
Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up ()	Offset	
Invert 1	943.89'	135°	30.5"	15" HDPE	17.6"	Hole 20	20"	28.284"	-1.25"	-11"	
Invert 2											
Invert 3											
Invert 4											
Invert 5											
Invert 6											
Invert 7											
Invert 8											


RIGHT-SIDE UP VIEW (int. dimensions)

Invert: 1
Degree: 135°
Horz: 14.5"
Hole: 20"
Up(): -1.25"

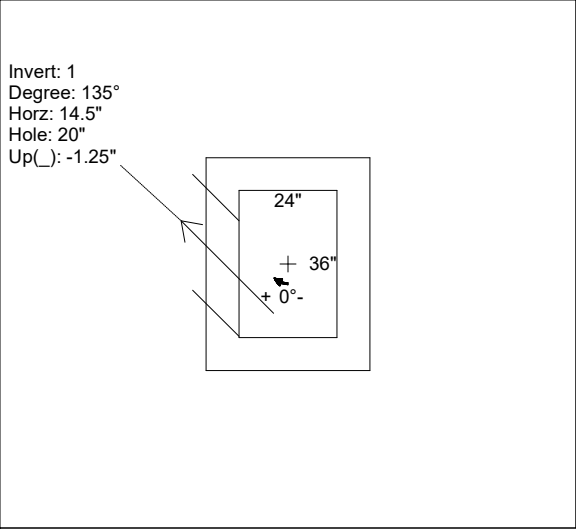


UPSIDE-DOWN VIEW (int. dimensions)

Invert: 1
Degree: 135°
Horz: 14.5"
Hole: 20"
Up(): -1.25"

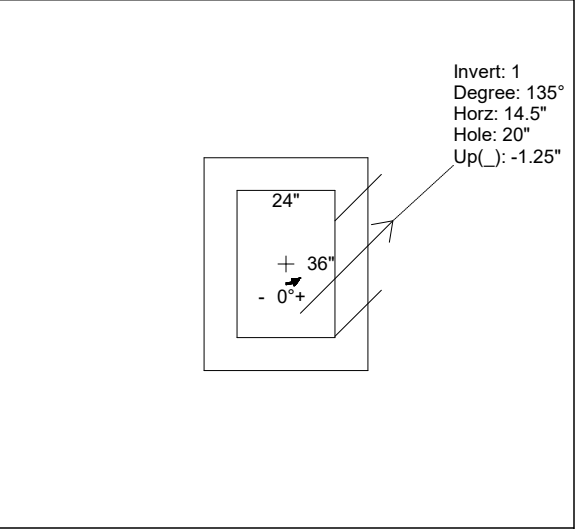

INSIDE WALL DIMENSIONS

(P1)

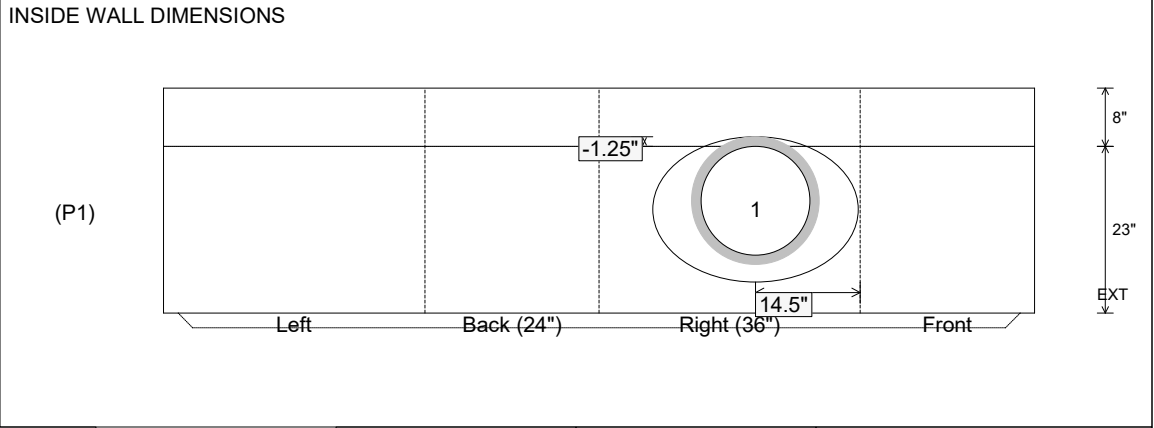

Coating (Int): Coating (Ext):	Seam Up: Tongue Seam Dn: n/a	Wall Thickness: 8" Floor Height: 8"	Height (Int): 23" Height (Ext): 31"	Weight (Net): 3445 lb Volume (Net): 0.88cu.yd
----------------------------------	---------------------------------	--	--	--
