



Job Name: 26-3280 - G.N. Miles Estates Subdivision Ph.4 Job Location: Nicholasville, KY Contractor: PECCO, Inc.					Plant: 100 8/24/2026 11:00:50 AM		Tech: Jared - F PC: A. Chambers				
Structure ID: CI402 CBIA											
P1 BX24120-08BVF BOX BASE 8inW, 8inF, Variable Ht T/n											
P2) 24" x 120" - CB INLET KY A 10' TOP LEFT F/G - 10" P1) 24" x 120" - BOX BASE 8inW, 8inF, Variable Ht T/n - 72" 1) CASTING - HOE KY-206 F/C (KY CBI A) 1) SNOUT - BMP SNOUT 18F w/ KIT 1) 24" x 120" - Conseal CS-102 1.00" 2) Hole - 20 1) Horiz Slot n/n - 120"x8" 1) Orifice - 5"					3400 lb 18154 lb 206 lb 25 lb 0 lb 0 lb 0 lb 0 lb ----- Structure Total: 21785 lb		Structure Notes: 1. PER KYTC CBI TYPE A / ASTM C913 SPEC'S. 2. CONCRETE = 4,000 PI AT 28 DAYS. 3. CASTING BY ICAST (HOE KY-206 F/C (KY CBI A)). 4. BMP 18F SNOUT w/KIT SUPPLIED BY ICAST & INSTALLED BY OTHERS. 5. #5 BAR @ 12" C.C.E.W. (GRADE 60) TO BE STUBBED OUT OF 120"x8" THROAT (INVERT 2) FOR CURB POUR TIE-IN. REINFORCING PER ASTM A615 (GRADE 60). - TOP PHASE (As .62) #5 BARS AT 6" C.C.E.W. - WALLS (As .31) #5 BARS AT 12" C.C.E.W. - FLOOR (As .31) #5 BARS AT 12" C.C.E.W.				
Rim: 950.75' Rim to Invert: 3.36' Slack: 0.32" Sump: 42" Step Position:											
Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up ()	Offset	
Invert 1	947.39'	125°	72.25"	15" HDPE	17.6"	Hole 20	20"	24.415"	39.5"	-8"	
Invert 2	947.39'	270°	68"	15" HDPE	17.6"	Hole 20	20"	20"	39.5"	0"	
Invert 3	949.223'	270°	68"	120" x 8" Horiz Slot	120" x 8"	Horiz Slot 120"x8"	120" x 8"	120"	64"	0"	
Invert 4	948.47'	270°	86"	5" Orifice	5"	Orifice 5"	5"	5"	55"	18"	
Invert 5											
Invert 6											
Invert 7											
Invert 8											

FIRST POUR DRAWING

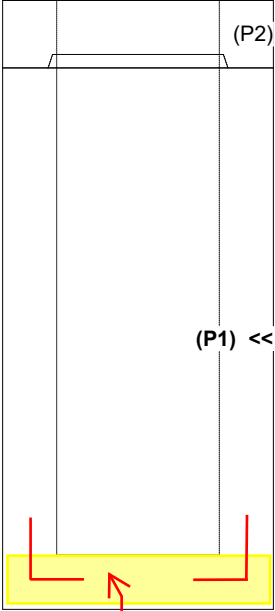

1ST POUR (FLOOR)
WET STICK 14" X 30" #5
L-BARS @ 12" C.C.E.W.
(GRADE 60) OUT TOP
OF FLOOR FOR WALL
POUR TIE-IN

RIGHT-SIDE UP VIEW (int. dimensions)

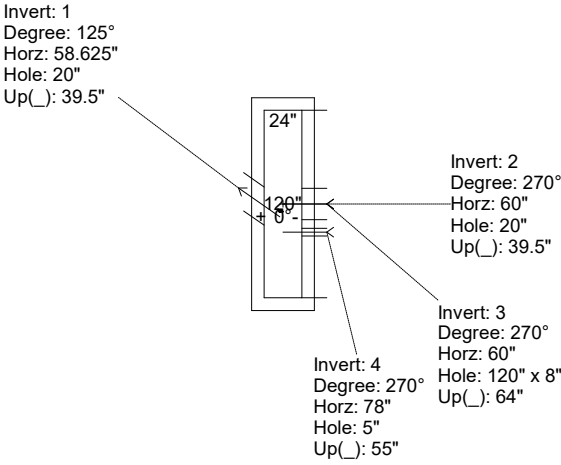

UPSIDE-DOWN VIEW (int. dimensions)


WEIGHTS

FIRST POUR - 3,652 LBS

SECOND POUR - 14,502 LBS

TOTAL - 18,154 LBS


INSIDE WALL DIMENSIONS



Coating (Int): Coating (Ext):	Seam Up: Tongue Seam Dn: n/a	Wall Thickness: 8" Floor Height: 8"	Height (Int): 72" Height (Ext): 80"	Weight (Net): 18154 lb Volume (Net): 4.64cu.yd
----------------------------------	---------------------------------	--	--	---


Job Name: 26-3280 - G.N. Miles Estates Subdivision Ph.4 Job Location: Nicholasville, KY Contractor: PECCO, Inc.					Plant: 100 8/24/2026 11:00:50 AM		Tech: Jared - F PC: A. Chambers				
Structure ID: CI402 CBIA											
P1 BX24120-08BVF BOX BASE 8inW, 8inF, Variable Ht T/n											
P2) 24" x 120" - CB INLET KY A 10' TOP LEFT F/G - 10" P1) 24" x 120" - BOX BASE 8inW, 8inF, Variable Ht T/n - 72" 1) CASTING - HOE KY-206 F/C (KY CBI A) 1) SNOUT - BMP SNOUT 18F w/ KIT 1) 24" x 120" - Conseal CS-102 1.00" 2) Hole - 20 1) Horiz Slot n/n - 120"x8" 1) Orifice - 5"					3400 lb 18154 lb 206 lb 25 lb 0 lb 0 lb 0 lb 0 lb ----- Structure Total: 21785 lb		Structure Notes: 1. PER KYTC CBI TYPE A / ASTM C913 SPEC'S. 2. CONCRETE = 4,000 PI AT 28 DAYS. 3. CASTING BY ICAST (HOE KY-206 F/C (KY CBI A)). 4. BMP 18F SNOUT w/KIT SUPPLIED BY ICAST & INSTALLED BY OTHERS. 5. #5 BAR @ 12" C.C.E.W. (GRADE 60) TO BE STUBBED OUT OF 120"x8" THROAT (INVERT 2) FOR CURB POUR TIE-IN. REINFORCING PER ASTM A615 (GRADE 60). - TOP PHASE (As .62) #5 BARS AT 6" C.C.E.W. - WALLS (As .31) #5 BARS AT 12" C.C.E.W. - FLOOR (As .31) #5 BARS AT 12" C.C.E.W.				
Rim: 950.75' Rim to Invert: 3.36' Slack: 0.32' Sump: 42' Step Position:											
Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up ()	Offset	
Invert 1	947.39'	125°	72.25"	15" HDPE	17.6"	Hole 20	20"	24.415"	39.5"	-8"	
Invert 2	947.39'	270°	68"	15" HDPE	17.6"	Hole 20	20"	20"	39.5"	0"	
Invert 3	949.223'	270°	68"	120" x 8" Horiz Slot	120" x 8"	Horiz Slot 120"x8"	120" x 8"	120"	64"	0"	
Invert 4	948.47'	270°	86"	5" Orifice	5"	Orifice 5"	5"	5"	55"	18"	
Invert 5											
Invert 6											
Invert 7											
Invert 8											

SECOND POUR DRAWING

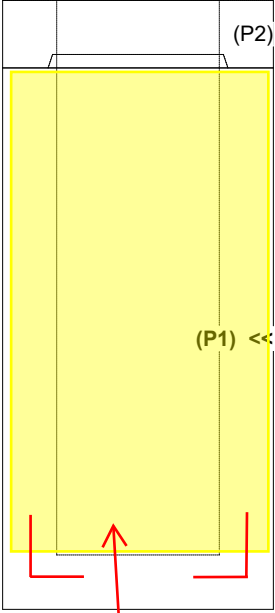


2ND POUR WALLS

RIGHT-SIDE UP VIEW (int. dimensions)

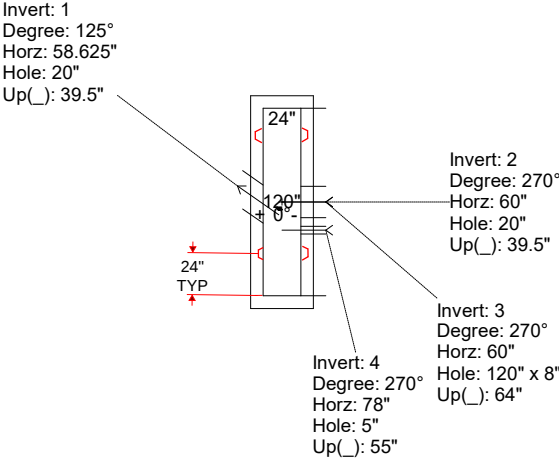

INSIDE WALL DIMENSIONS

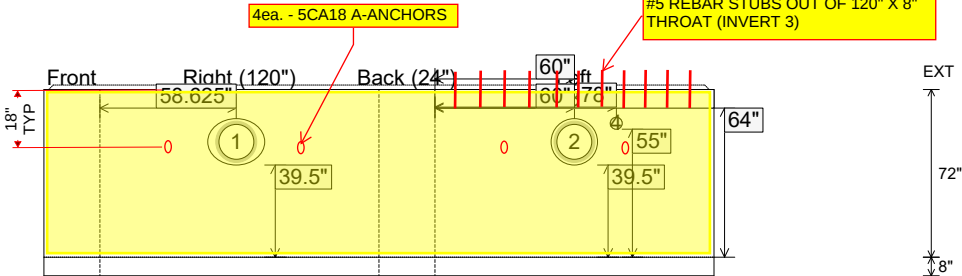


UPSIDE-DOWN VIEW (int. dimensions)

WEIGHTS

FIRST POUR - 3,652 LBS

SECOND POUR - 14,502 LBS

TOTAL - 18,154 LBS



REBAR STUB DETAIL

Coating (Int): Coating (Ext):	Seam Up: Tongue Seam Dn: n/a	Wall Thickness: 8" Floor Height: 8"	Height (Int): 72" Height (Ext): 80"	Weight (Net): 18154 lb Volume (Net): 4.64cu.yd
----------------------------------	---------------------------------	--	--	---
