

Contractor: PECCO, Inc.

Plant: 100



Type: SAN.MH w/Ext. Drop/ConBlock-CDA Red
Size: 48"

Rim: 947.93'
Invert: 939.79'
Rim to Invert: 8.14'

Sump: 2"
Floor (Top): 939.623'
Floor Height: 6"


Floor (Bot): 939.123'
Overall Height: 8.583'
Slack: 2.68"

1. PER ASTM C478 SPECIFICATIONS.
2. CONCRETE = 4,000 PSI AT 28 DAYS..
3. ADMIXTURE = CONBLOCK CDA RED.
4. CASTING BY ICAST (HOE MC-315 F/C SANITARY).
5. EXTERIOR DROP ASSEMBLY BY ICAST @ 271 DEGREES.

- CONE (As .12)
- RISER/WALLS (As .12)
- FLOOR (As .31) #5 BARS AT 12" C.C.E.W.



- P3) 24" - CASTING HEIGHT - 7"
- P2) 48" - ECC CONE w/ 24" HOLE, w/ConBlock-CDA Red - 42"
- P1) 48" - MH BASE w/DROP/ConBlock-CDA Red - 48"
- 1) JOINT WRAP - 0.065"x6"x50' CONSEAL CS212
- 1) JOINT WRAP PRIMER - CONSEAL CS-75 (1 gal.)
- 1) 48" - MH INVERT CHANNEL w/ConBlock-CDA Red - FULL HEIGHT
- 1) CASTING - HOE MC-315 F/C Sanitary
- 1) 48" - Conseal CS-102 1.00" (Double)
- 1) 24" - Conseal CS-102 1.00" (Double)
- 2) PSX - 12-08 NYLO
- 1) Drop Tee - 8" PVC
- 1) Drop Elbow - 8" PVC
- 8) MH Step ML-10-TDS-NCR - 10"

Structure Total: 9370 lb

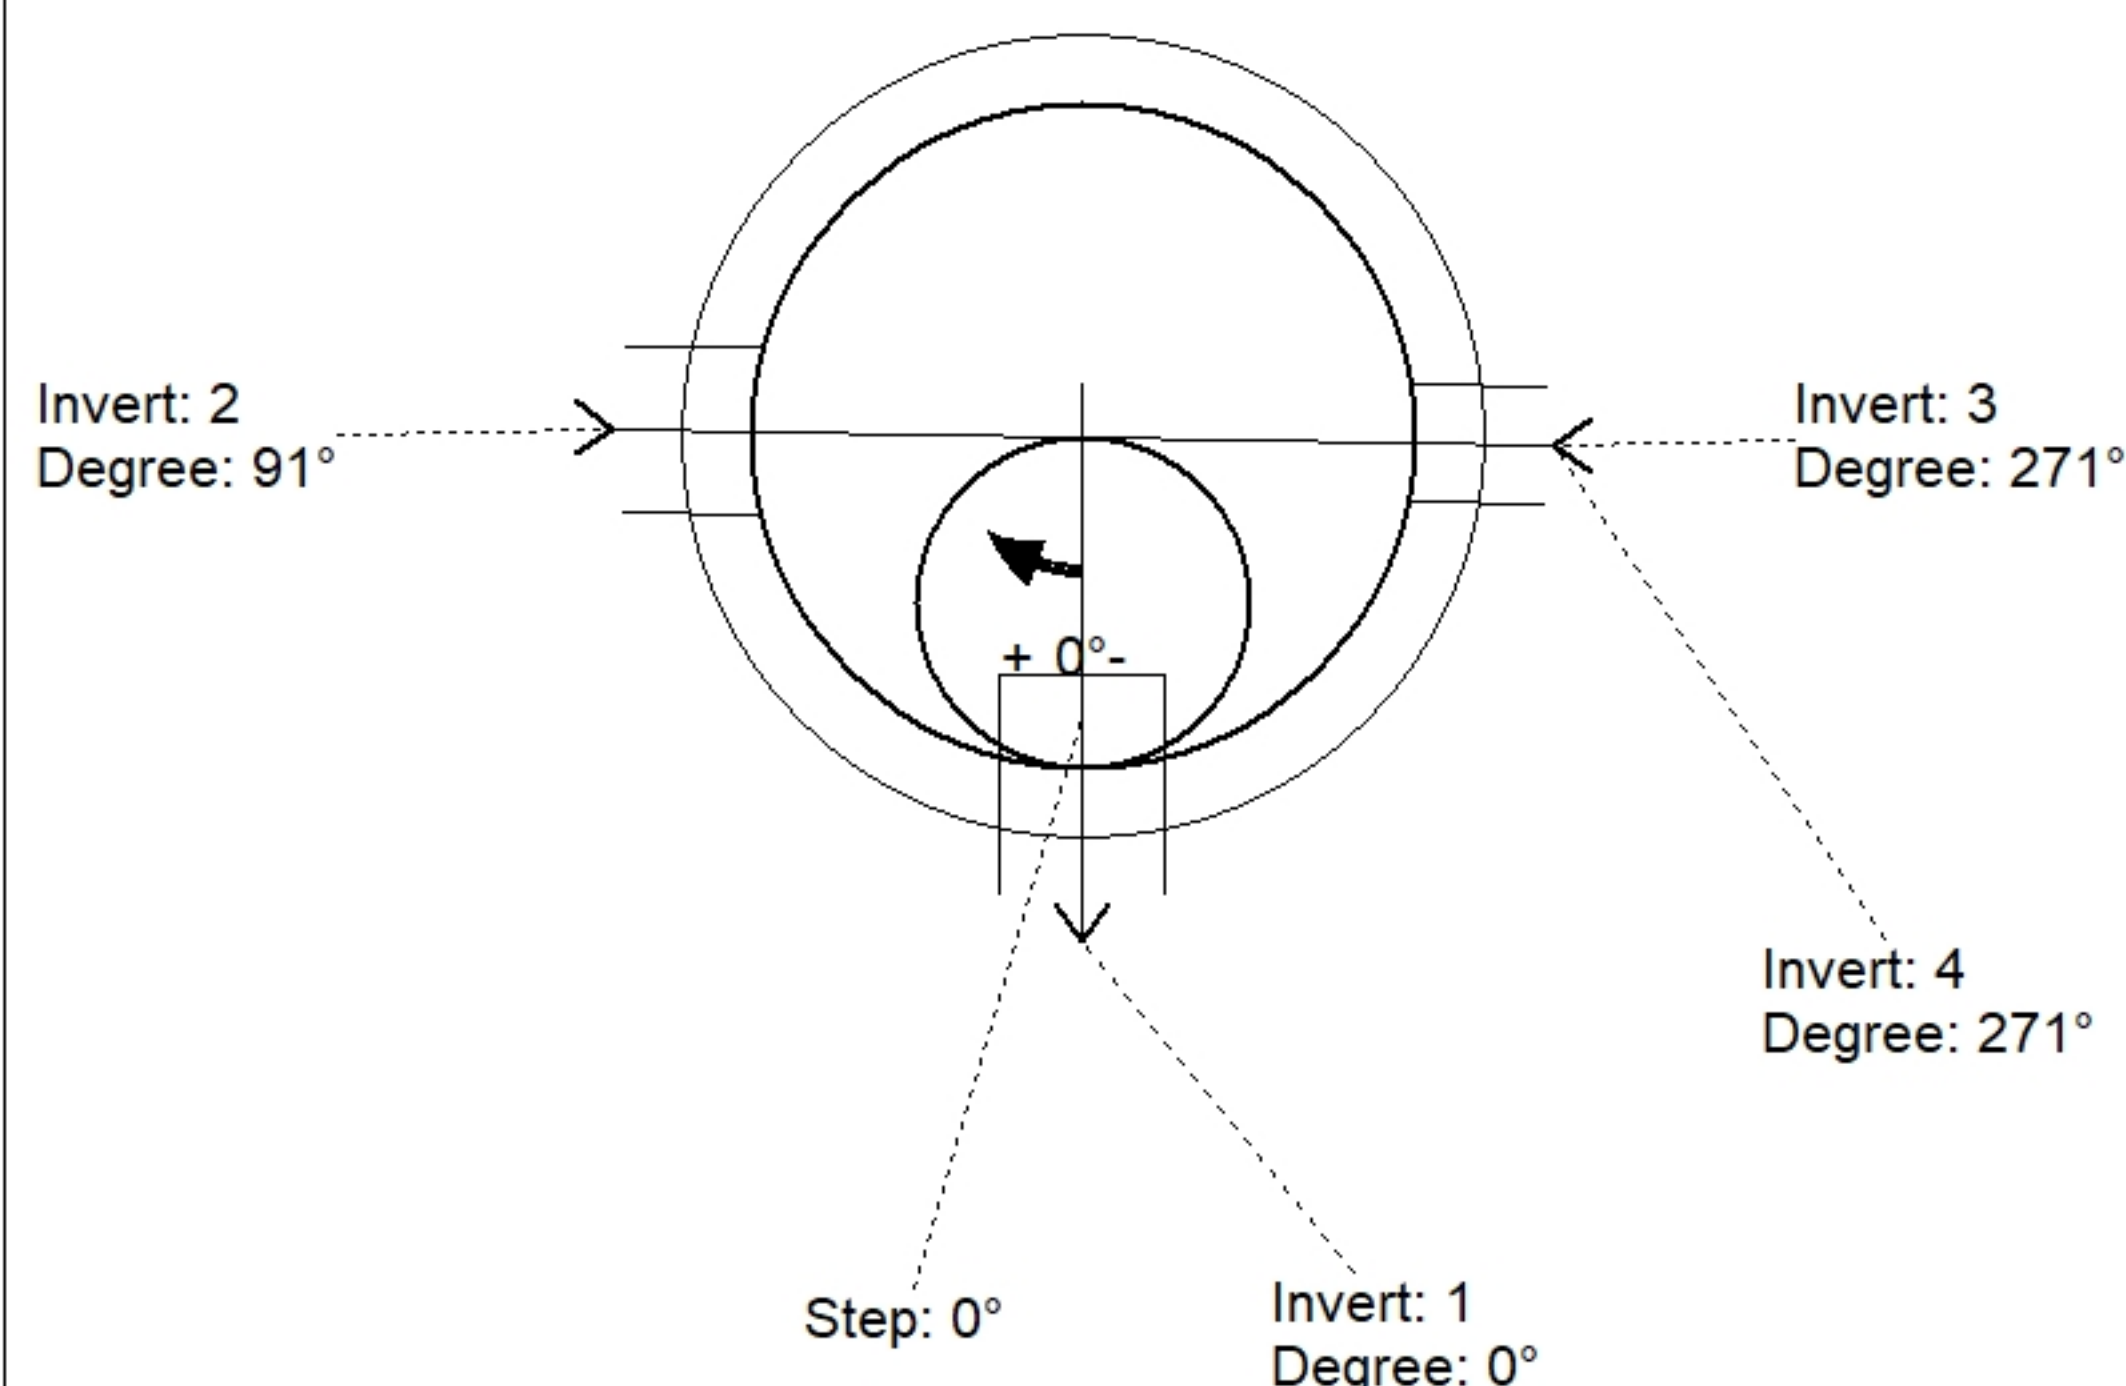

Position	Elev	Angle	Pipe	Pipe OD	Hole	Connector	Up (')	Ref
Rim	947.93'							
Reducer								
Invert 1	939.79'	0°	8" PVC SDR35	8.5"	12"	PSX 12-08 NYLO	0"	P1
Invert 2	939.89'	91°	8" PVC SDR35	8.5"	12"	PSX 12-08 NYLO	1.2"	P1
Invert 3	942.34'	271°	8" PVC SDR35	8.5"	8.5"	Drop Tee 8" PVC	32.35"	P1
Invert 4	939.89'	271°	8" PVC SDR35	8.5"	8.5"	Drop Elbow 8" PVC	2.95"	P1
Invert 5								
Invert 6								
Invert 7								
Invert 8								

Default - Interior Dimensions

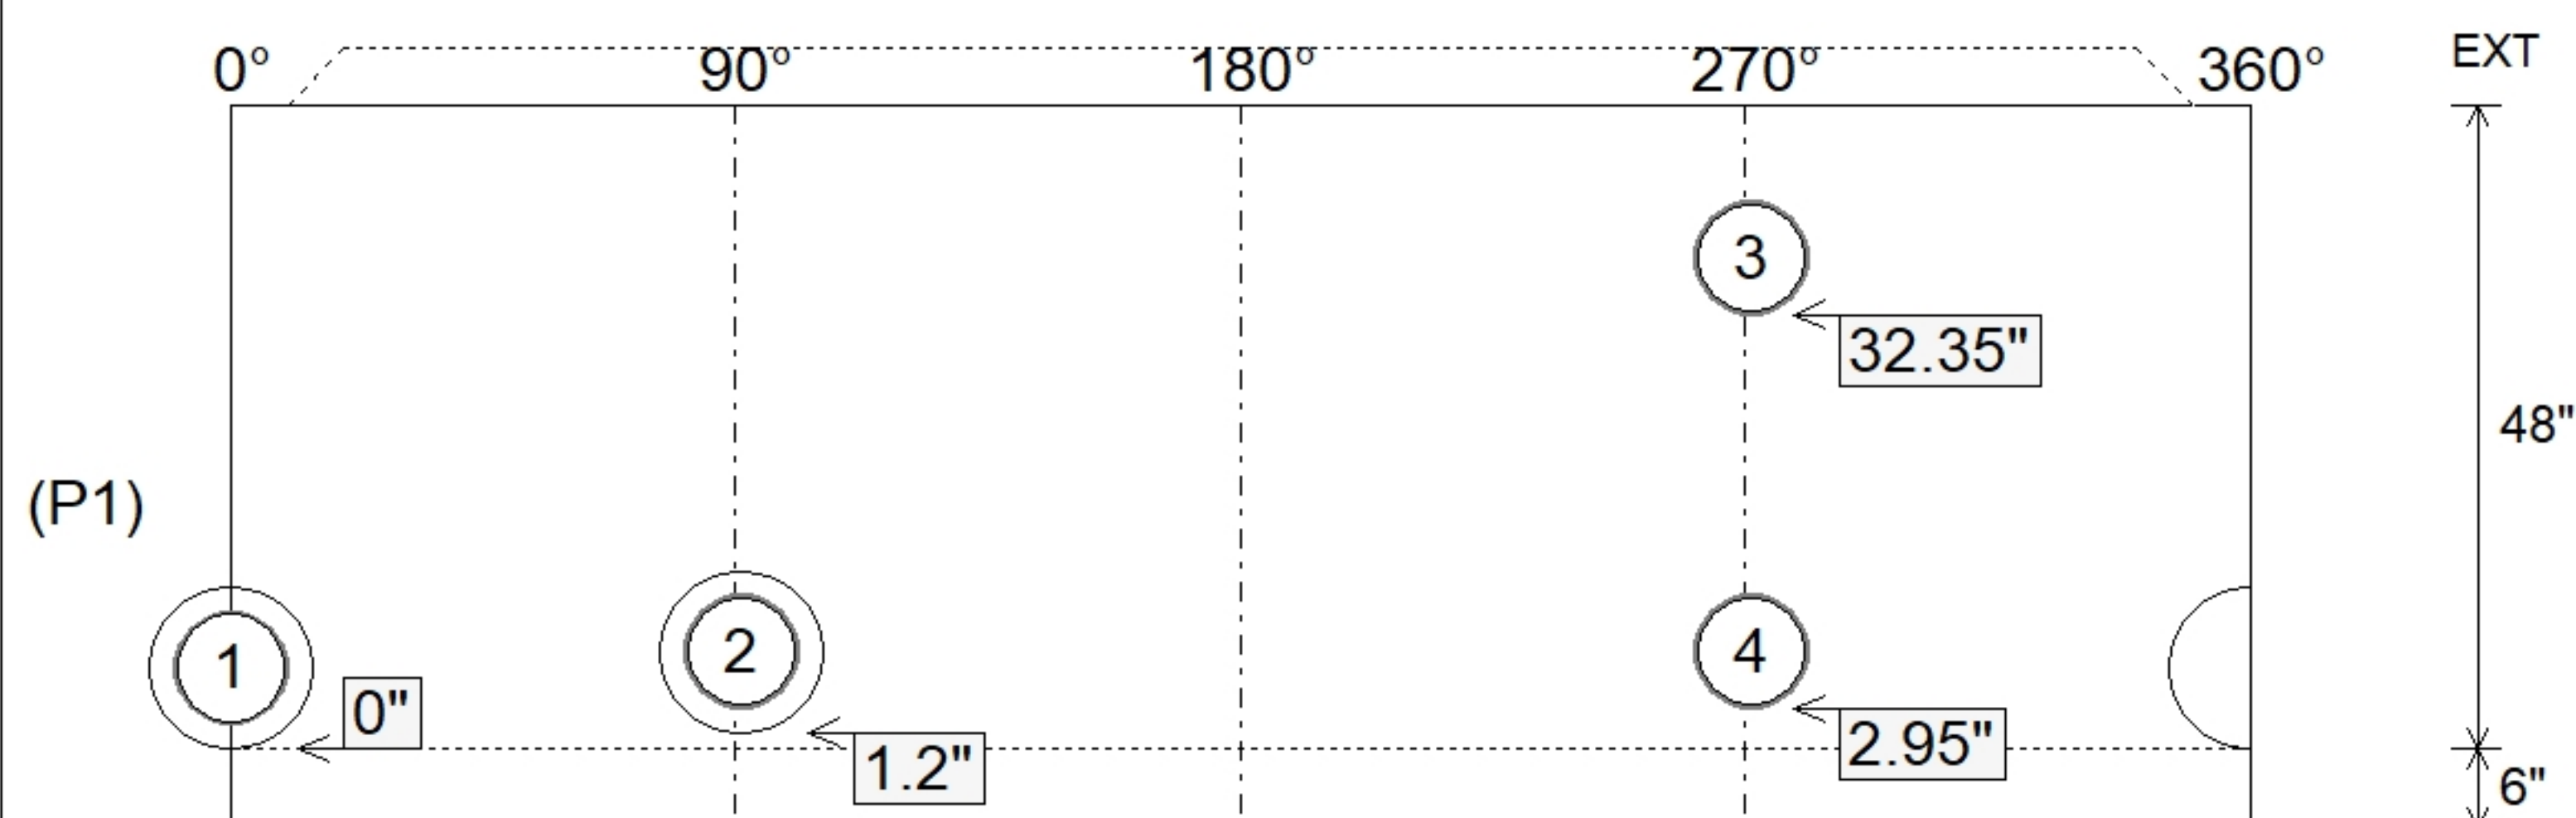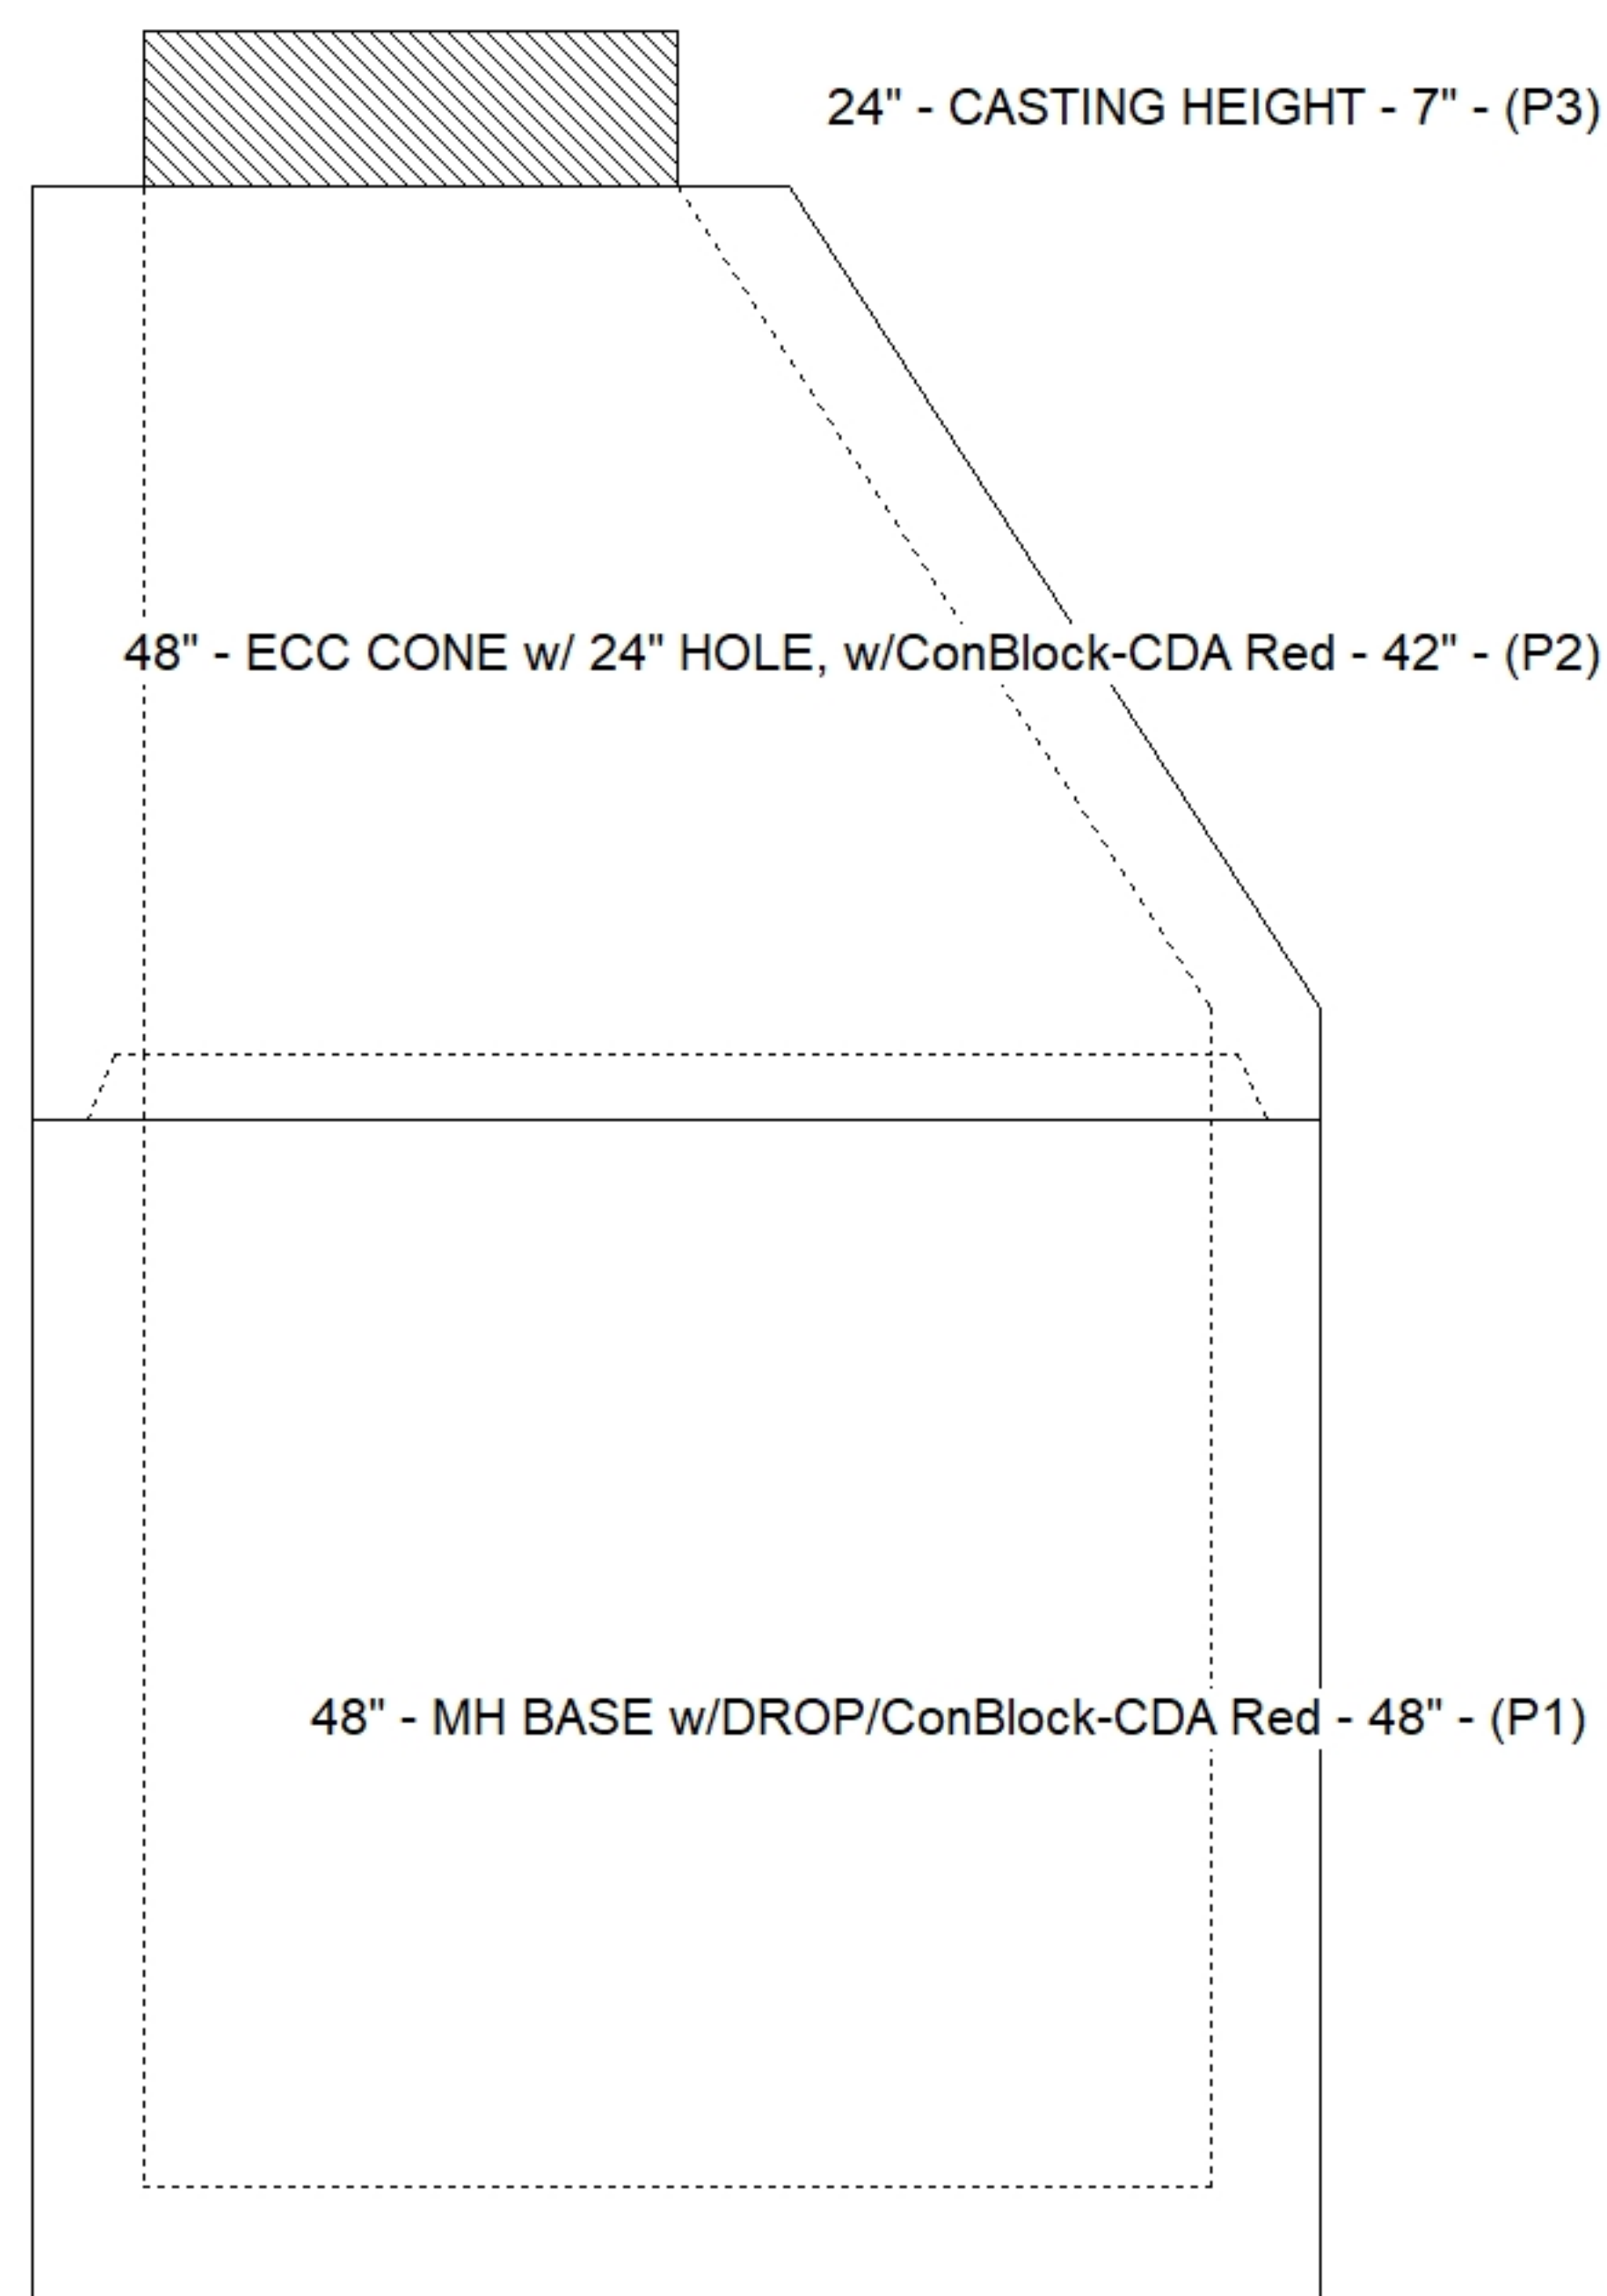

Submittal Drawing
8/27/2026 12:16:18 PM

SUBMITTAL
APPROVED BY:
