



Structure Notes:

1. PER ASTM C913 SPECIFICATIONS.
2. CONCRETE = 4,000 PSI AT 28 DAYS.
3. CASTING BY ICAST (HALLIDAY H2R 48"X48" & HOE MCS-288 F/C CAST-IN)

REINFORCING PER ASTM A615 (GRADE 60).

- TOP SLAB (As .62) #5 BARS AT 6" C.C.E.W.
- WALLS (As .12) #5 BARS AT 8" C.C.E.W.
- FLOOR (As .12) #5 BARS AT 8" C.C.E.W.

Position	Elev	Angle	Pipe	Pipe OD	Hole	Connector	Up ()	Ref
Rim	8'							
Reducer								
Invert 1	1.75'	0°	6" DI	6.875"	12"	PSX 12-06 NYLO	18"	P1
Invert 2	1.75'	180°	6" DI	6.875"	12"	PSX 12-06 NYLO	18"	P1
Invert 3								
Invert 4								
Invert 5								
Invert 6								
Invert 7								
Invert 8								

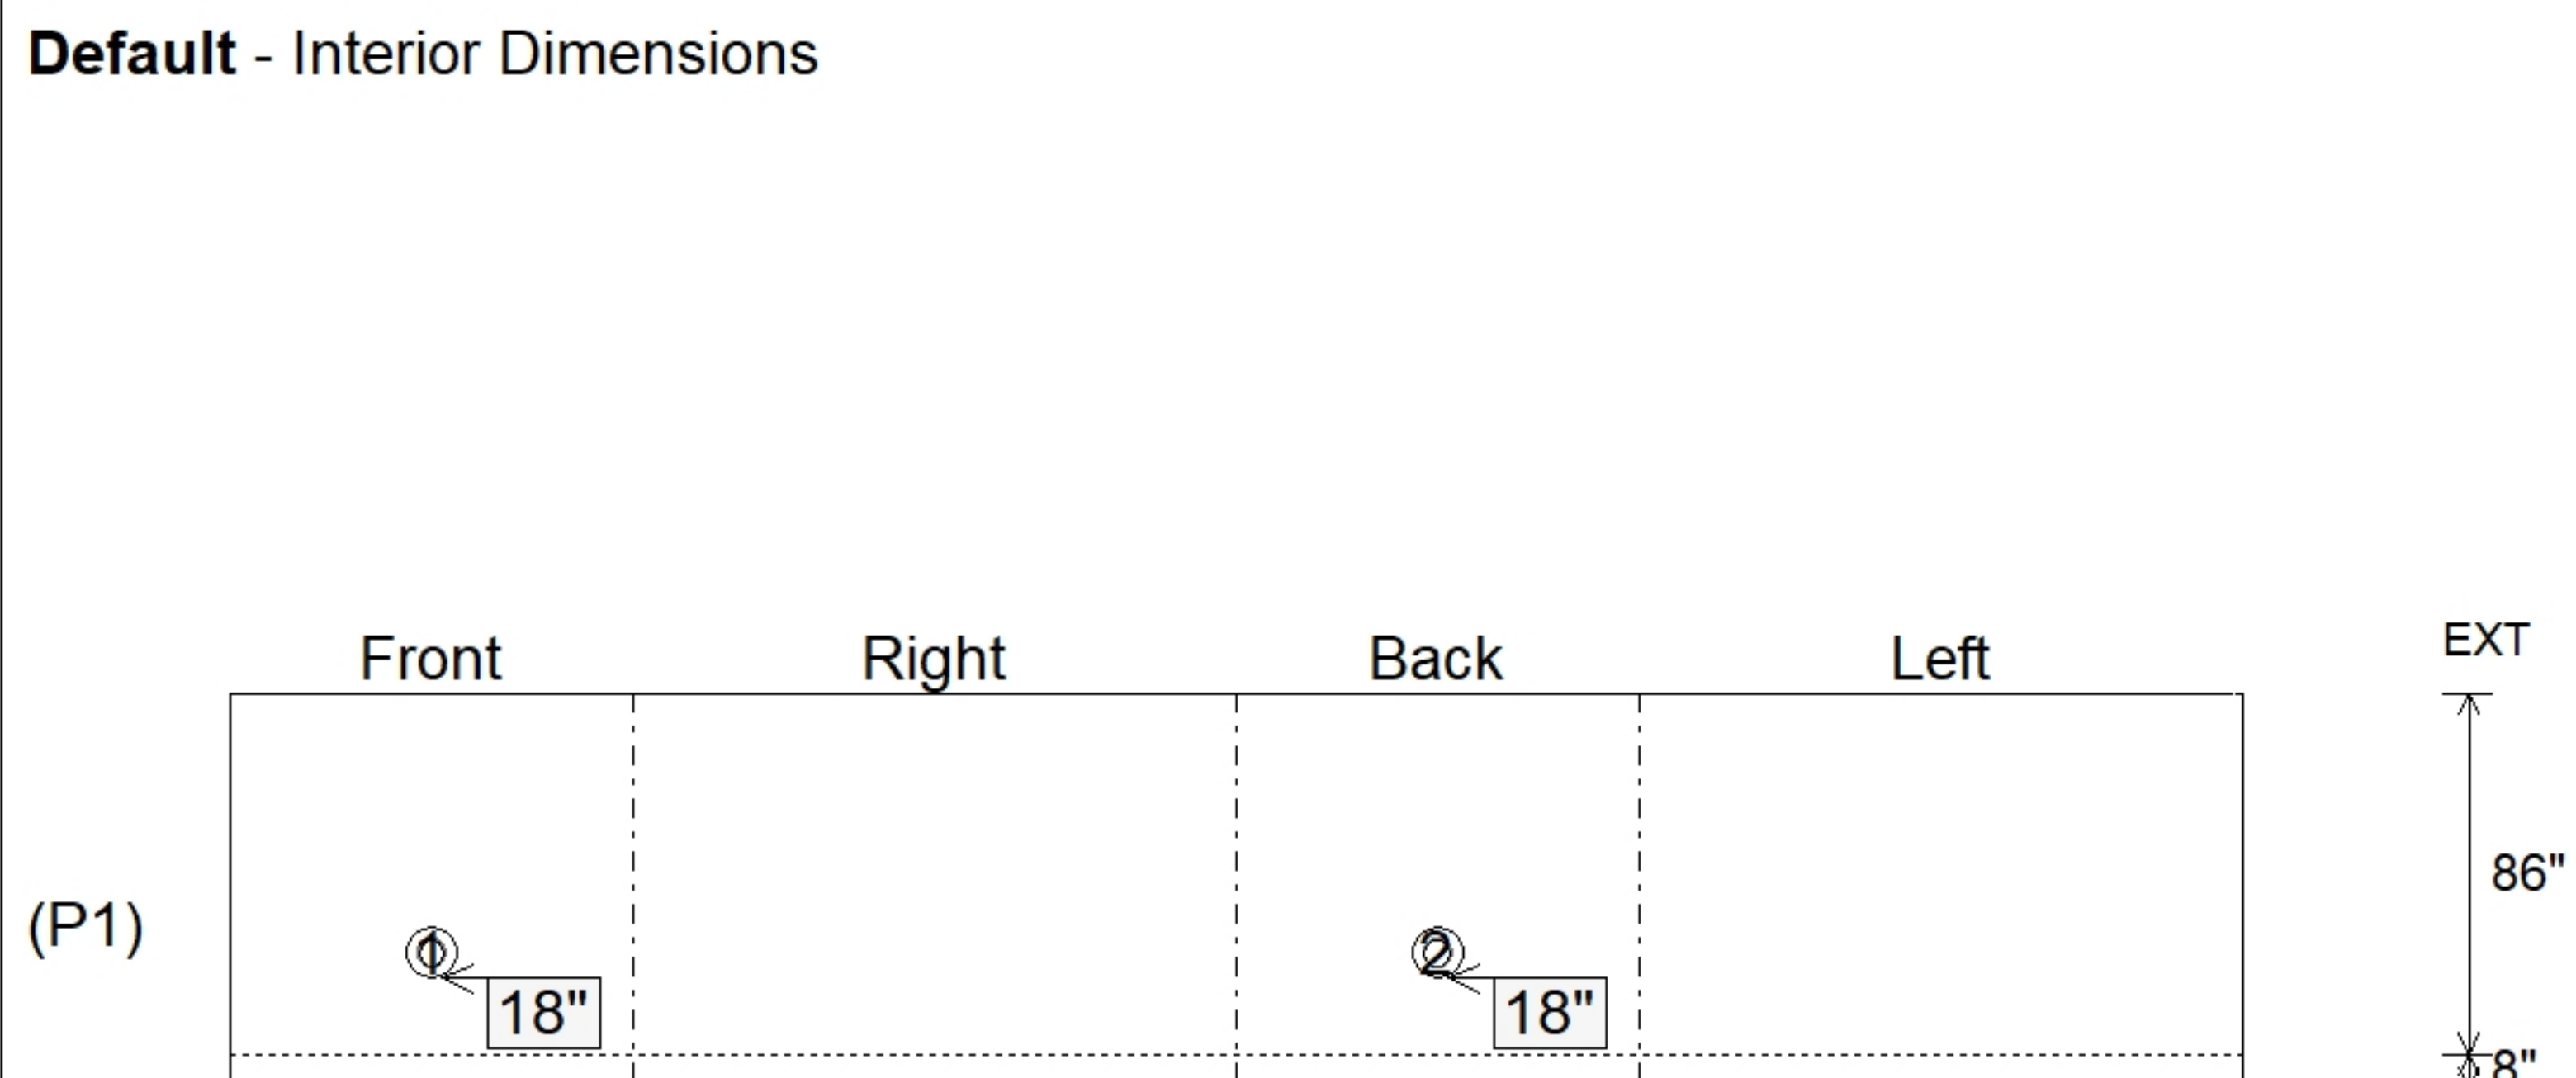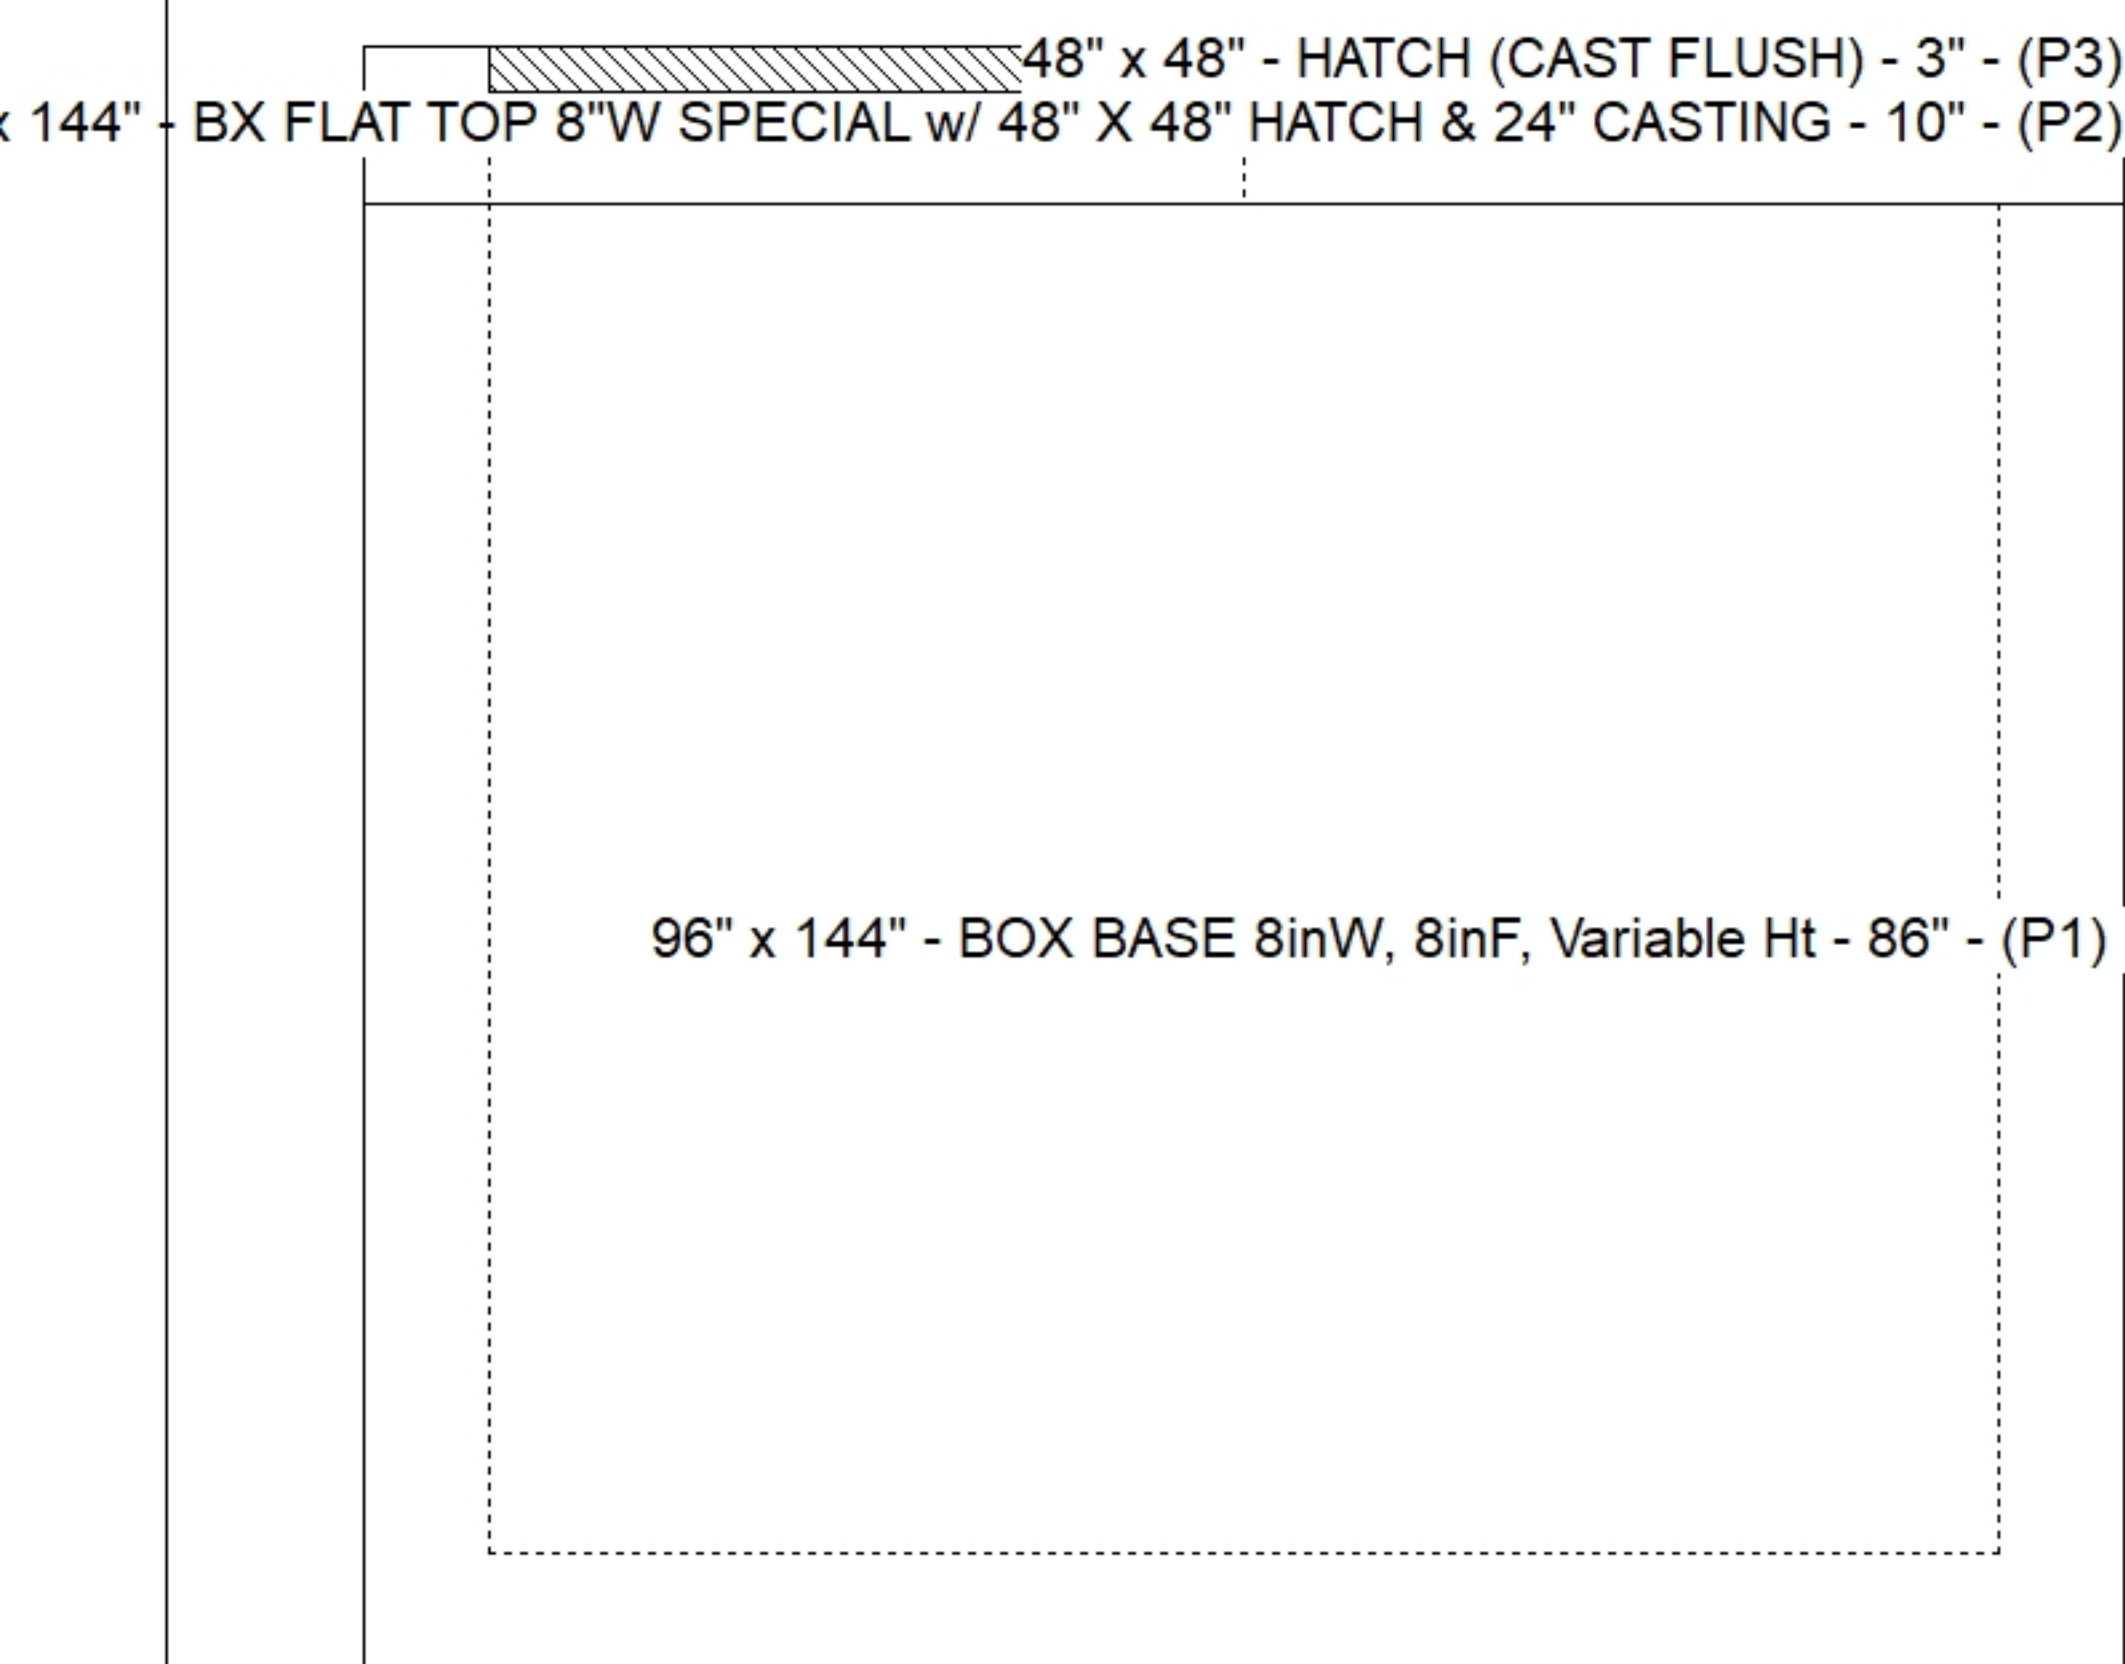

Submittal Drawing 9/29/2026 11:37:42 AM	SUBMITTAL APPROVED BY:
--	---------------------------
