

Job Name: 26-3293 - 2025 Sewer System Rehab
Job Location: Westmoreland, TN
Contractor: Luttrell & Sons, LLC

Plant: Beaver Dam

Tech: J. Coppage

9/10/2026 9:04:16 AM

PC: A. Chambers



Structure ID: SMH-3A SS-MH

P1 MH048BA36CDARED

MH BASE w/ConBlock-CDA Red

- P3) 24" - CASTING HEIGHT - 7"
P2) 48" - ECC CONE w/ 24" HOLE, w/ConBlock-CDA Red - 42"
P1) 48" - MH BASE w/ConBlock-CDA Red - 36"
1) JOINT WRAP - 0.065"x6"x50' CONSEAL CS212
1) JOINT WRAP PRIMER - CONSEAL CS-75 (1 gal.)
1) 48" - MH INVERT CHANNEL w/ConBlock-CDA Red - FULL HEIGHT
1) CASTING - JBS 1150 F/C SANITARY
1) 48" - Conseal CS-102 1.00" (Double)
1) 24" - Conseal CS-102 1.00" (Double)
3) PSX - 12-08 NYLO
7) MH Step ML-10-TDS-NCR - 10"



- 0 lb
3116 lb
3701 lb
0 lb
0 lb
1440 lb
250 lb
0 lb
0 lb
24 lb
0 lb
Structure Total: 8532 lb
- Structure Notes:
1. JBS-1150 SAN PROVIDED BY ICAST.
2. PER ASTM C478 SPECIFICATIONS.
3. CONCRETE = 4,000 PSI AT 28 DAYS.
4. ADMIXTURE = CONBLOCK CDA RED.
5. REINFORCING PER ASTM A615 (GRADE 60).
- CONE (As .12)
- RISER/WALLS (As .12)
- FLOOR (As .31) #5 BARS AT 12" C.C.E.W.

Rim: 911.25' Rim to Invert: 7.16' Slack: 2.92" Sump: 2" Step Position: 91.5°


Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up ()	Offset
Invert 1	904.09'	0°	0"	8" PVC SDR26	8.5"	PSX 12-08 NYLO	12"	12.129"	0"	0"
Invert 2	904.19'	183°	92.625"	8" PVC SDR26	8.5"	PSX 12-08 NYLO	12"	12.129"	1.2"	0"
Invert 3	904.19'	267°	135.141"	8" PVC SDR26	8.5"	PSX 12-08 NYLO	12"	12.129"	1.2"	0"
Invert 4										
Invert 5										
Invert 6										
Invert 7										
Invert 8										

RIGHT-SIDE UP VIEW (int. dimensions)

UPSIDE-DOWN VIEW (int. dimensions)

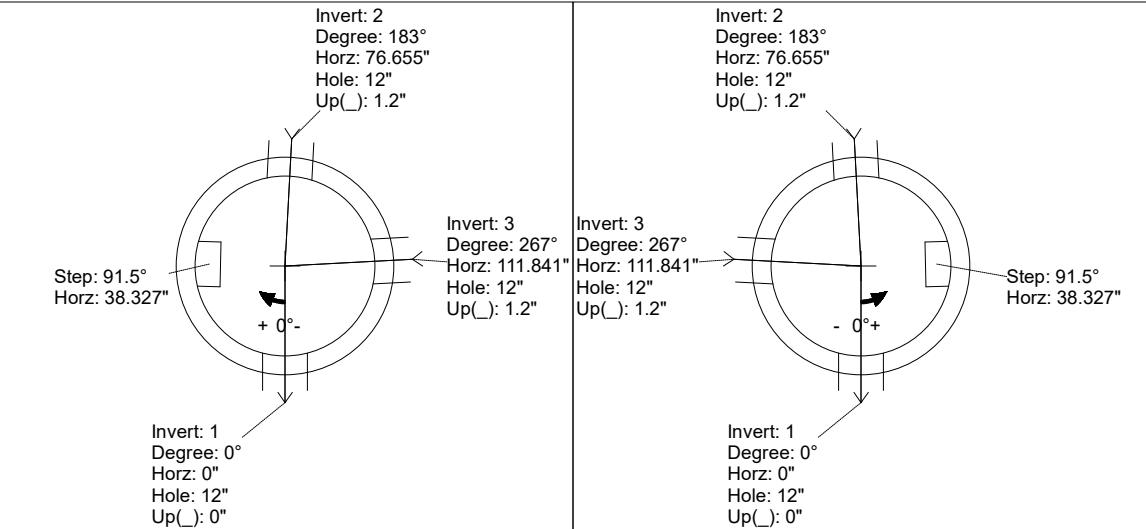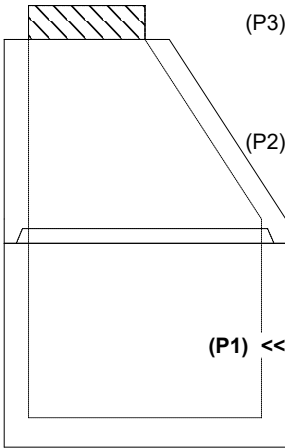

INSIDE WALL DIMENSIONS

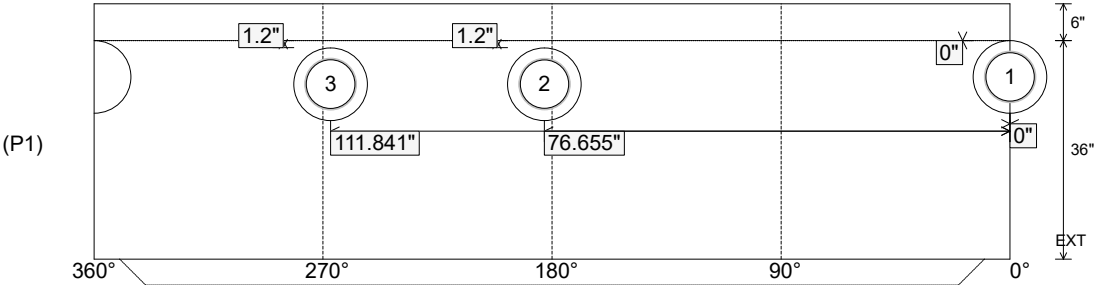

Coating (Int): Coating (Ext):	Seam Up: Tongue Seam Dn: n/a	Wall Thickness: 5" Floor Height: 6"	Height (Int): 36" Height (Ext): 42"	Weight (Net): 3701 lb Volume (Net): 0.94cu.yd
----------------------------------	---------------------------------	--	--	--

Job Name: 26-3293 - 2025 Sewer System Rehab
Job Location: Westmoreland, TN
Contractor: Luttrell & Sons, LLC

Plant: Beaver Dam

Tech: J. Coppage

9/10/2026 9:04:16 AM

PC: A. Chambers



Structure ID: SMH-3A SS-MH

P1 MH048BA36CDARED

MH BASE w/ConBlock-CDA Red

- P3) 24" - CASTING HEIGHT - 7"
P2) 48" - ECC CONE w/ 24" HOLE, w/ConBlock-CDA Red - 42"
P1) 48" - MH BASE w/ConBlock-CDA Red - 36"
1) JOINT WRAP - 0.065"x6"x50' CONSEAL CS212
1) JOINT WRAP PRIMER - CONSEAL CS-75 (1 gal.)
1) 48" - MH INVERT CHANNEL w/ConBlock-CDA Red - FULL HEIGHT
1) CASTING - JBS 1150 F/C SANITARY
1) 48" - Conseal CS-102 1.00" (Double)
1) 24" - Conseal CS-102 1.00" (Double)
3) PSX - 12-08 NYLO
7) MH Step ML-10-TDS-NCR - 10"

- 0 lb
3116 lb
3701 lb
0 lb
0 lb
1440 lb
250 lb
0 lb
0 lb
24 lb
0 lb
Structure Total: 8532 lb
- Structure Notes: .
1. JBS-1150 SAN PROVIDED BY ICAST.
2. PER ASTM C478 SPECIFICATIONS.
3. CONCRETE = 4,000 PSI AT 28 DAYS.
4. ADMIXTURE = CONBLOCK CDA RED.
5. REINFORCING PER ASTM A615 (GRADE 60).
- CONE (As .12)
- RISER/WALLS (As .12)
- FLOOR (As .31) #5 BARS AT 12" C.C.E.W.



Rim: 911.25' Rim to Invert: 7.16' Slack: 2.92" Sump: 2" Step Position: 91.5°

INVERT CHANNEL DRAWING
FULL HEIGHT INVERT


Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up ()	Offset
Invert 1	904.09'	0°	0"	8" PVC SDR26	8.5"	PSX 12-08 NYLO	12"	12.129"	0"	0"
Invert 2	904.19'	183°	92.625"	8" PVC SDR26	8.5"	PSX 12-08 NYLO	12"	12.129"	1.2"	0"
Invert 3	904.19'	267°	135.141"	8" PVC SDR26	8.5"	PSX 12-08 NYLO	12"	12.129"	1.2"	0"
Invert 4										
Invert 5										
Invert 6										
Invert 7										
Invert 8										

RIGHT-SIDE UP VIEW (int. dimensions)

UPSIDE-DOWN VIEW (int. dimensions)

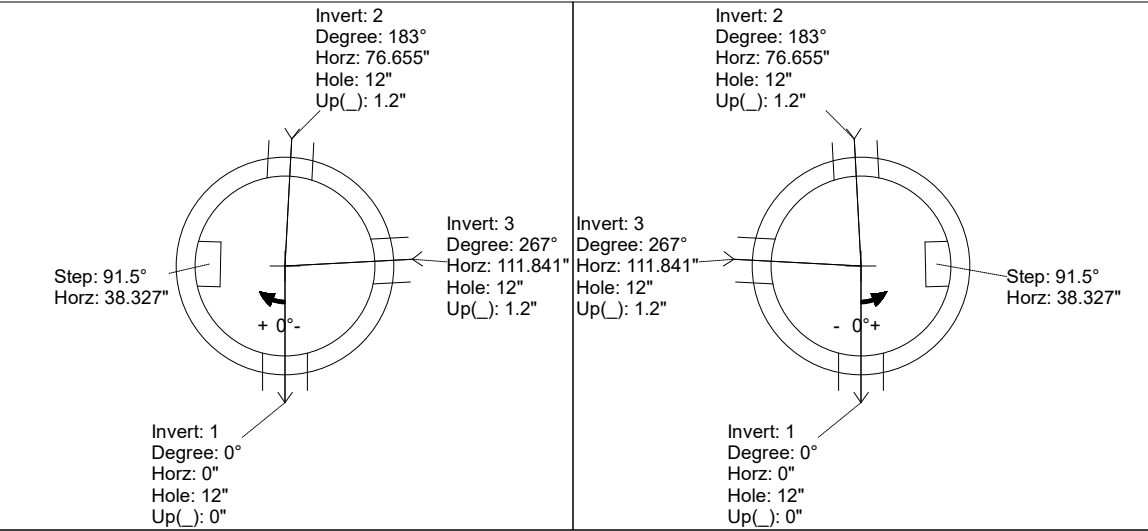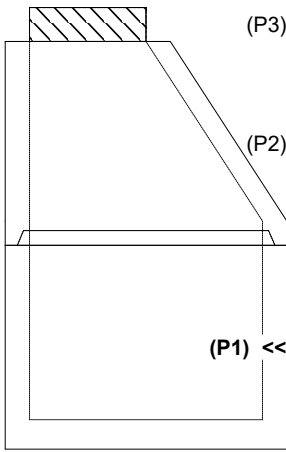

INSIDE WALL DIMENSIONS

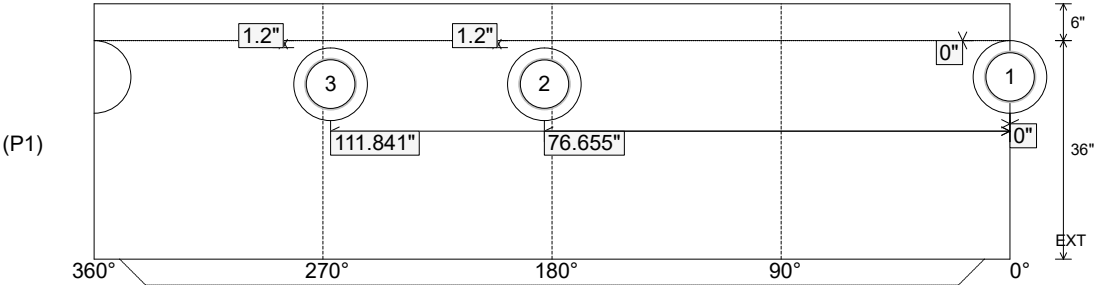

Coating (Int):
Coating (Ext):

Seam Up: Tongue
Seam Dn: n/a

Wall Thickness: 5"
Floor Height: 6"

Height (Int): 36"
Height (Ext): 42"

Weight (Net): 3701 lb
Volume (Net): 0.94cu.yd
