



Job Name: 26-3341 - C&P Trucking Job Location: Owensboro, KY Contractor: Winwater Hartford KY Co.					Plant: 100 8/26/2026 10:53:23 AM		Tech: Jared - F PC: A. Chambers				
Structure ID: AA2 ST-DBI											
P1 BX2424-08BAVF		BOX BASE 8inW, 8inF, Variable Ht F/n									
P2) 24" x 24" - CASTING HEIGHT - 4" P1) 24" x 24" - BOX BASE 8inW, 8inF, Variable Ht F/n - 20" 1) CASTING - HOE 280T F/G 1) 24" x 24" - Conseal CS-102 1.00" 2) Hole - 14					0 lb 2579 lb 182 lb 0 lb 0 lb ----- 2761 lb Structure Total:		Structure Notes: 1. PER ASTM C913 SPECIFICATIONS. 2. CONCRETE = 4,000 PSI AT 28 DAYS. 3. NO STEPS AND NO INVERT CHANNEL. 4. CASTING BY ICAST (HOE 280T F/G). REINFORCING PER ASTM A615 (GRADE 60). - WALLS (As .12) #5 BARS AT 12" C.C.E.W. - FLOOR (As .12) #5 BARS AT 12" C.C.E.W.				
Rim: 408.44' Rim to Invert: 2.11' Slack: 2.07" Sump: 0.75" Step Position:											
Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up ()	Offset	
Invert 1	406.33'	0°	20"	10" HDPE	11.4"	Hole 14	14"	14"	0"	0"	
Invert 2	406.33'	160°	17"	10" HDPE	11.4"	Hole 14	14"	14.898"	0"	4"	
Invert 3											
Invert 4											
Invert 5											
Invert 6											
Invert 7											
Invert 8											


RIGHT-SIDE UP VIEW (int. dimensions)

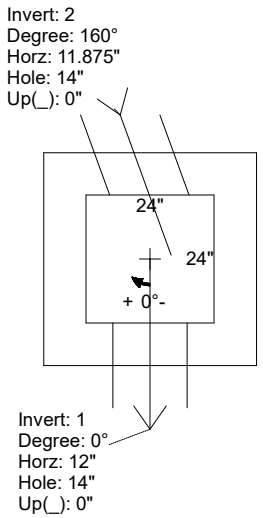

UPSIDE-DOWN VIEW (int. dimensions)

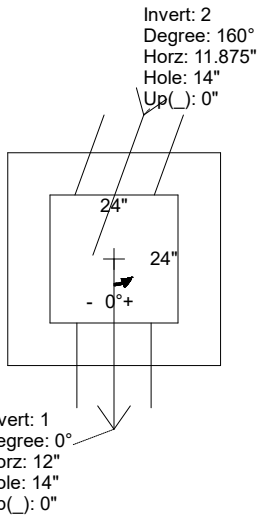

INSIDE WALL DIMENSIONS

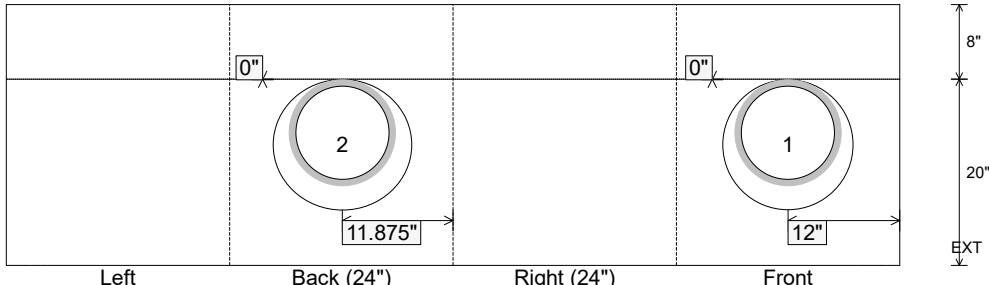

Coating (Int): Coating (Ext):	Seam Up: Flat Seam Dn: n/a	Wall Thickness: 8" Floor Height: 8"	Height (Int): 20" Height (Ext): 28"	Weight (Net): 2579 lb Volume (Net): 0.66cu.yd
----------------------------------	-------------------------------	--	--	--
