



Floor (Bot): 527.257'
Overall Height: 26.167'
Slack: 0.916"

P8) 24" - CASTING HEIGHT - 7"	0 lb
P7) 24" - GRADE RING - 4"	270 lb
P6) 48" - ECC CONE w/ 24" HOLE - 36"	3000 lb
P5) 48" - MH RISER - 60"	4192 lb
P4) 48" - MH RISER - 72"	5030 lb
P3) 120" x 120" - CB TRANSITION SLAB 48" HOLE - 15"	22392 lb
P2) 120" x 120" - BOX RISER 10inW, Variable Ht - 120"	33156 lb
P1) 120" x 120" - P.I.P. BY OTHERS - BTM SLAB - 0"	0 lb
3) 48" - SGL 1"x14.5' Butyl	0 lb
2) DOGHOUSE - 90"x90"	0 lb
1) Hole - 90	0 lb
25) MH Step ML-10-TDS-NCR - 10"	0 lb


Structure Total:	68040 lb

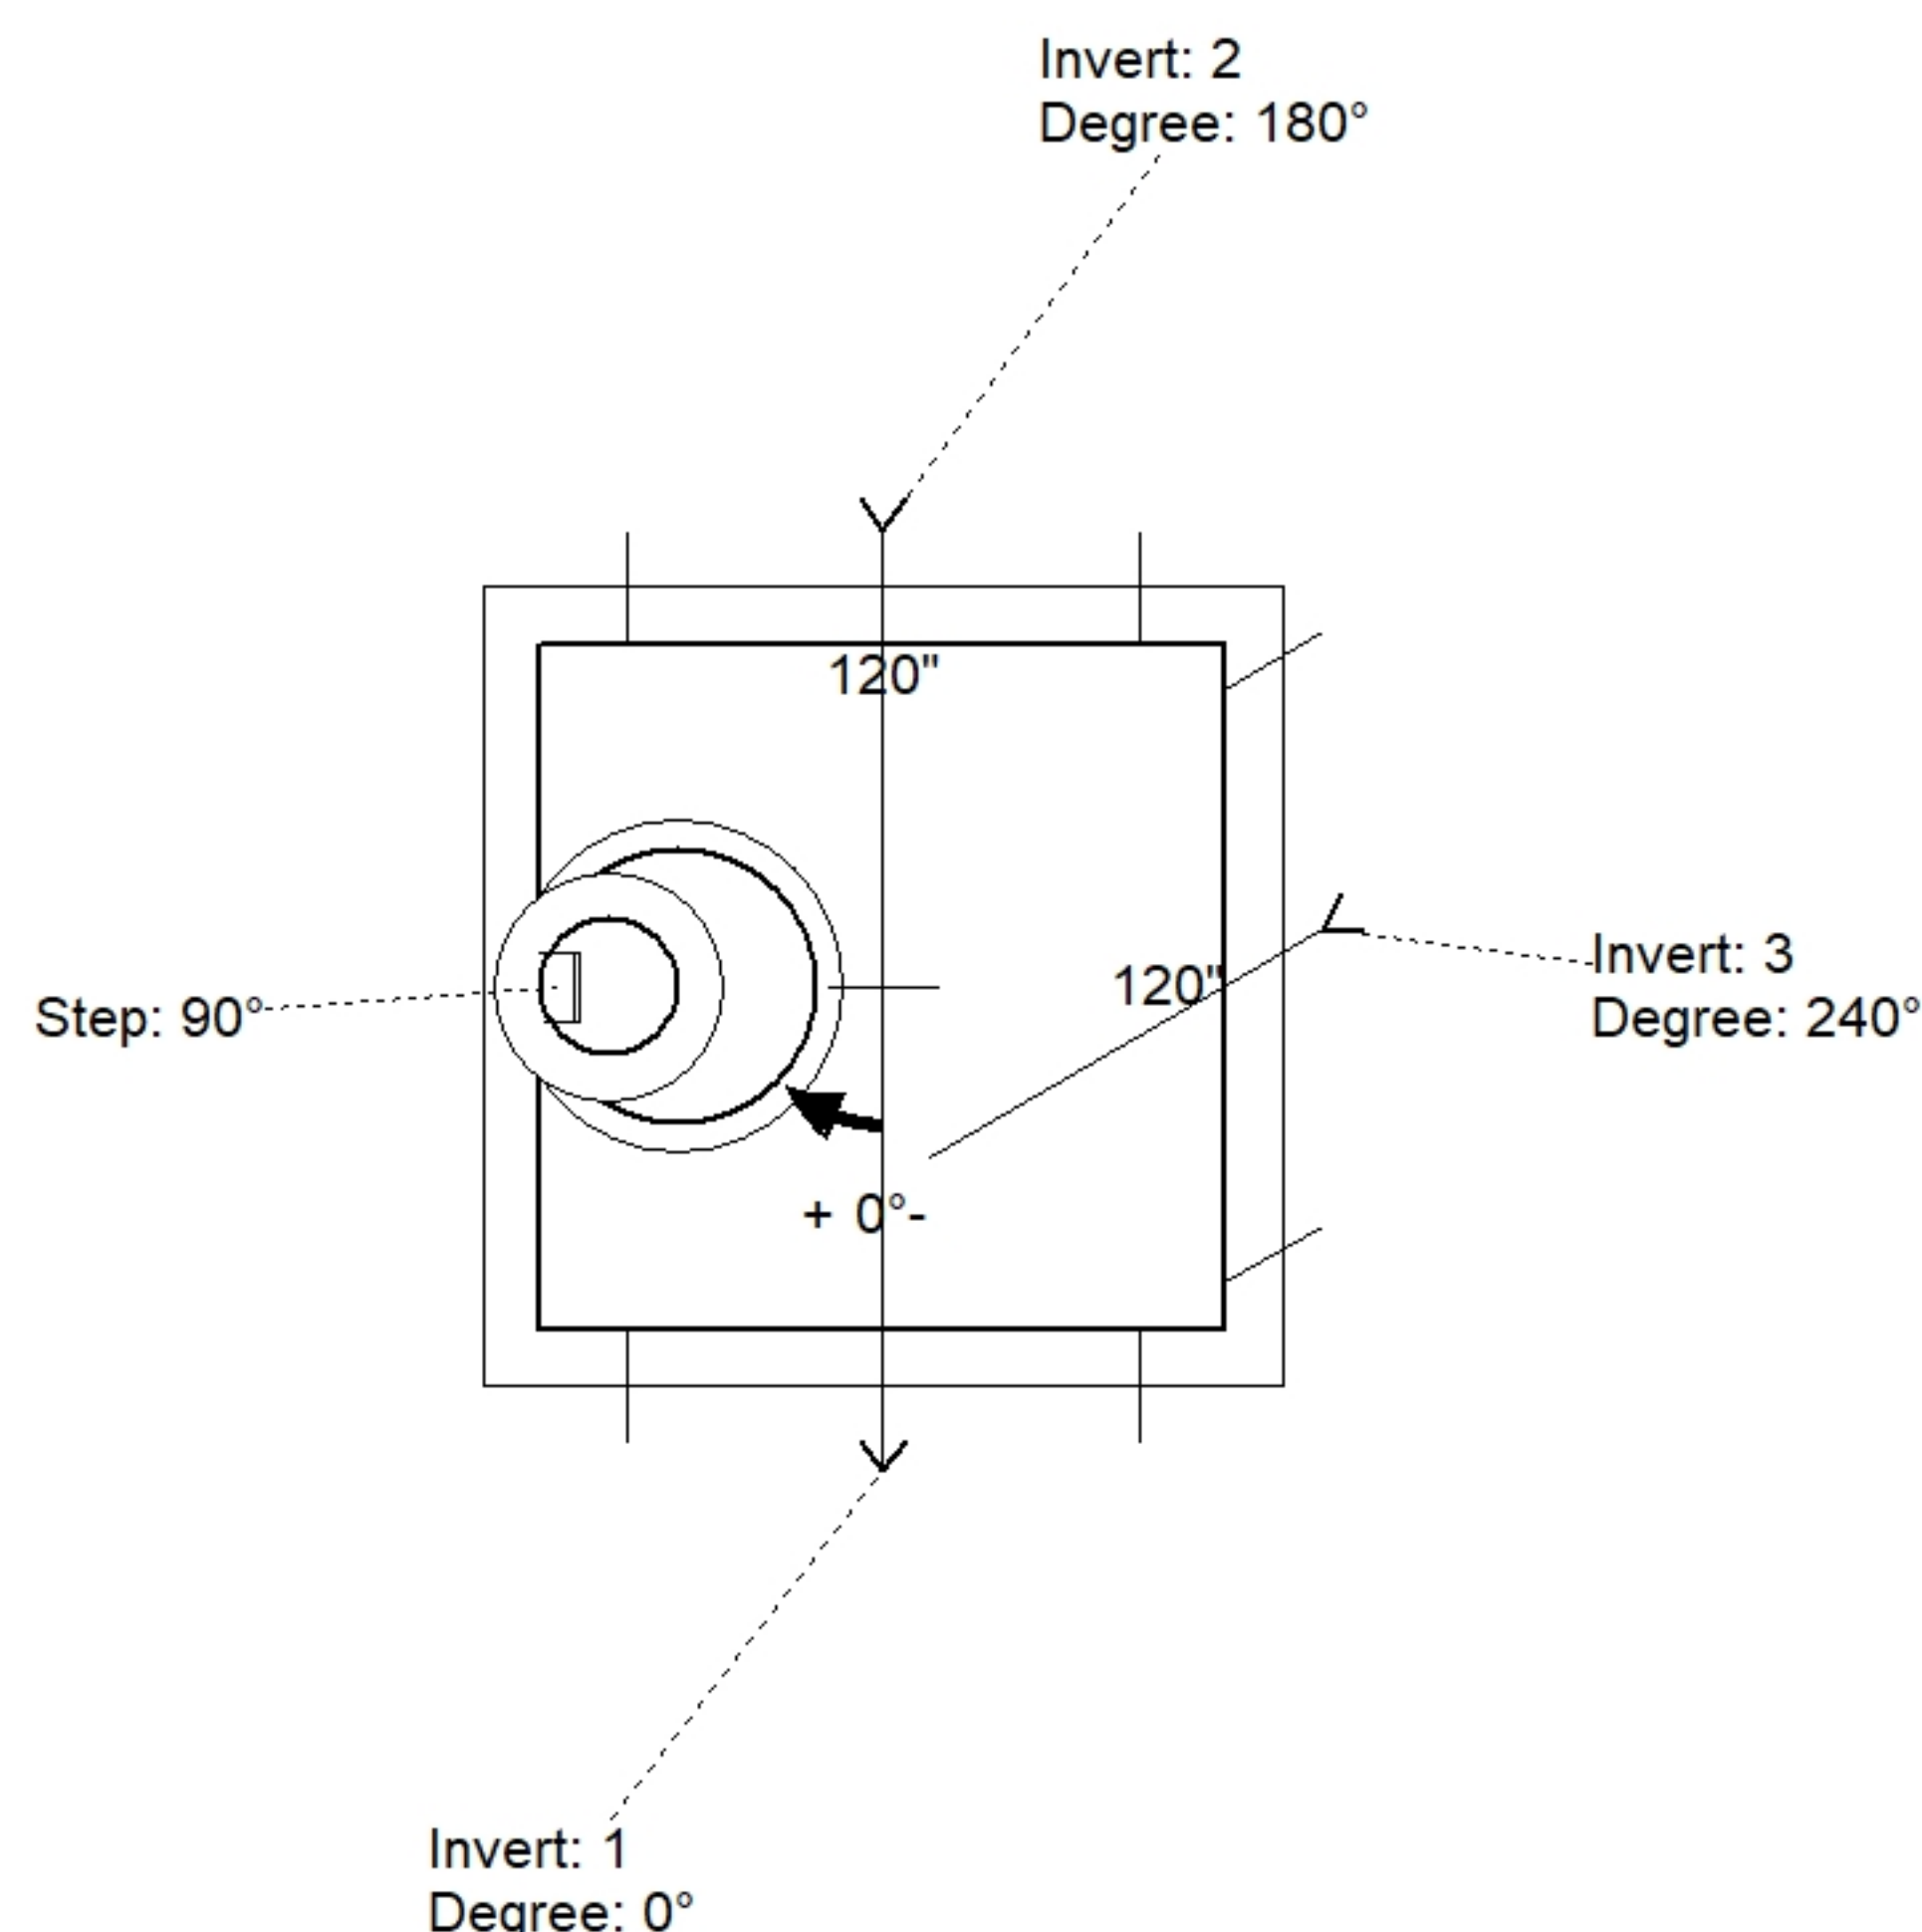

Position	Elev	Angle	Pipe	Pipe OD	Hole	Connector	Up (')	Ref
Rim	553.5'							
Reducer	537.257'							
Invert 1	528.34'	0°	72" RCP B WALL	86"	90" x 90"	DOGHOUSE 90"x90"	5.996"	P2
Invert 2	528.34'	180°	72" RCP B WALL	86"	90" x 90"	DOGHOUSE 90"x90"	5.996"	P2
Invert 3	528.34'	240°	72" RCP B WALL	86"	90"	Hole 90	5.996"	P2
Invert 4								
Invert 5								
Invert 6								
Invert 7								
Invert 8								

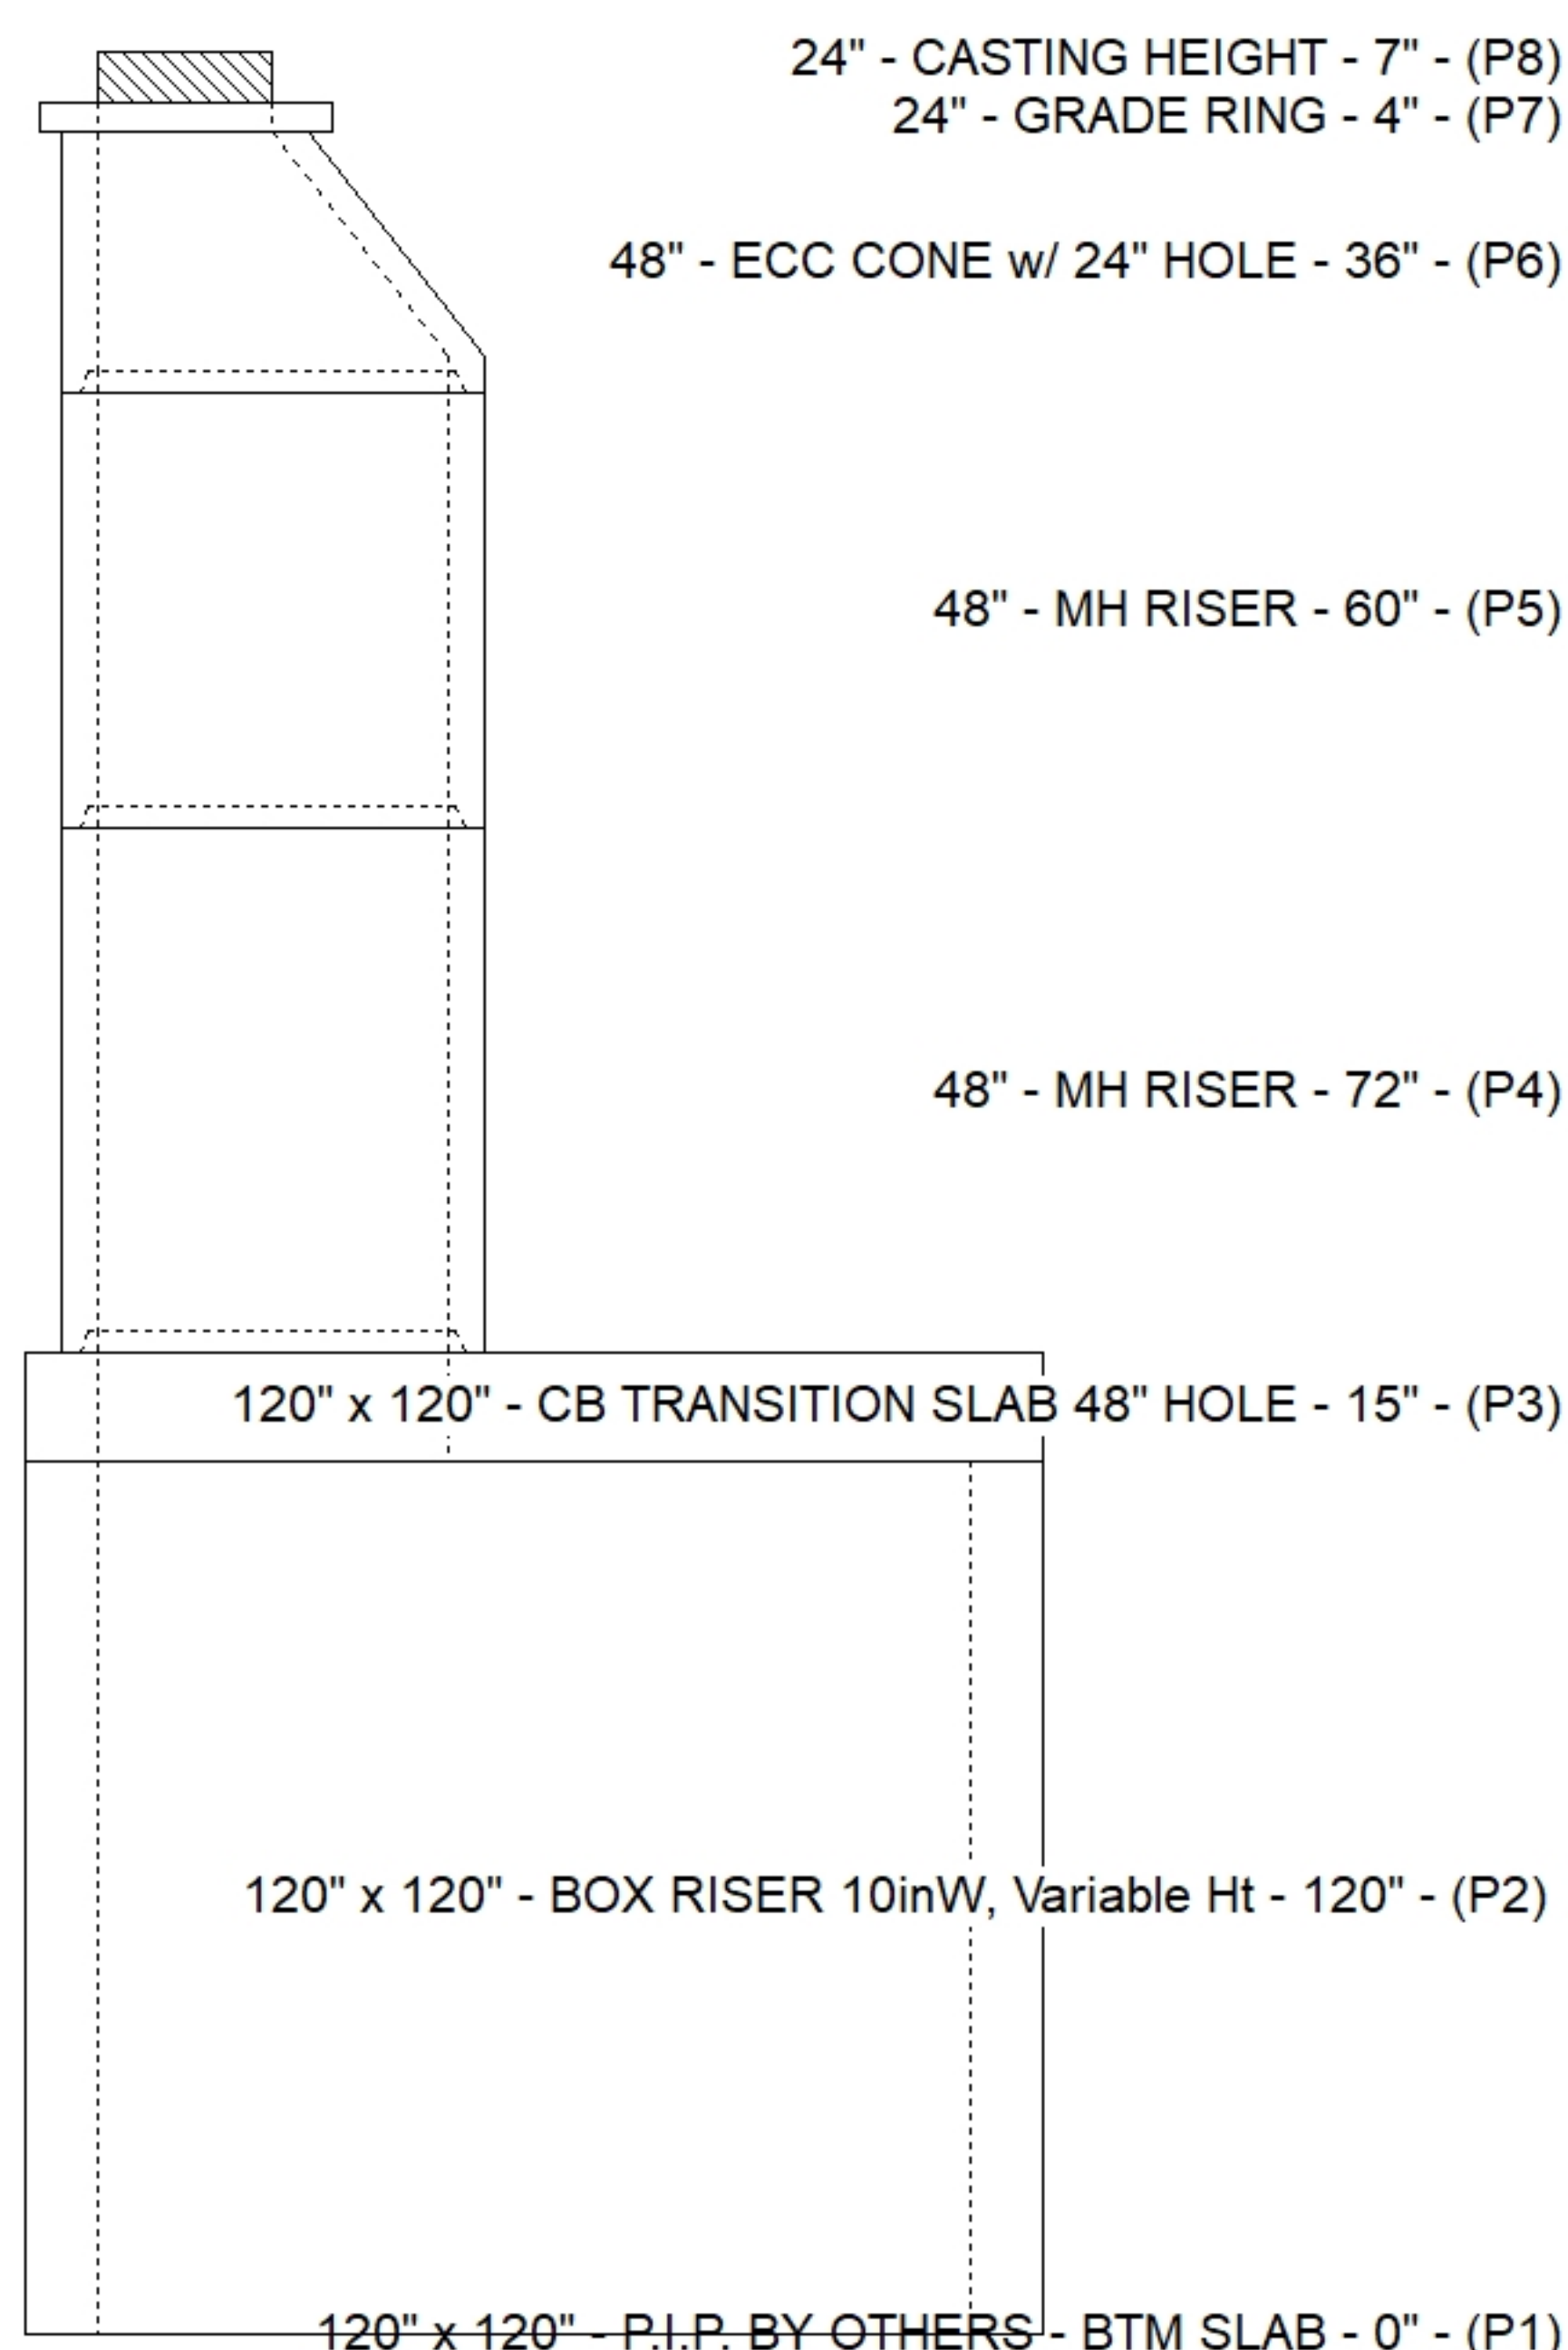

Default - Interior Dimensions

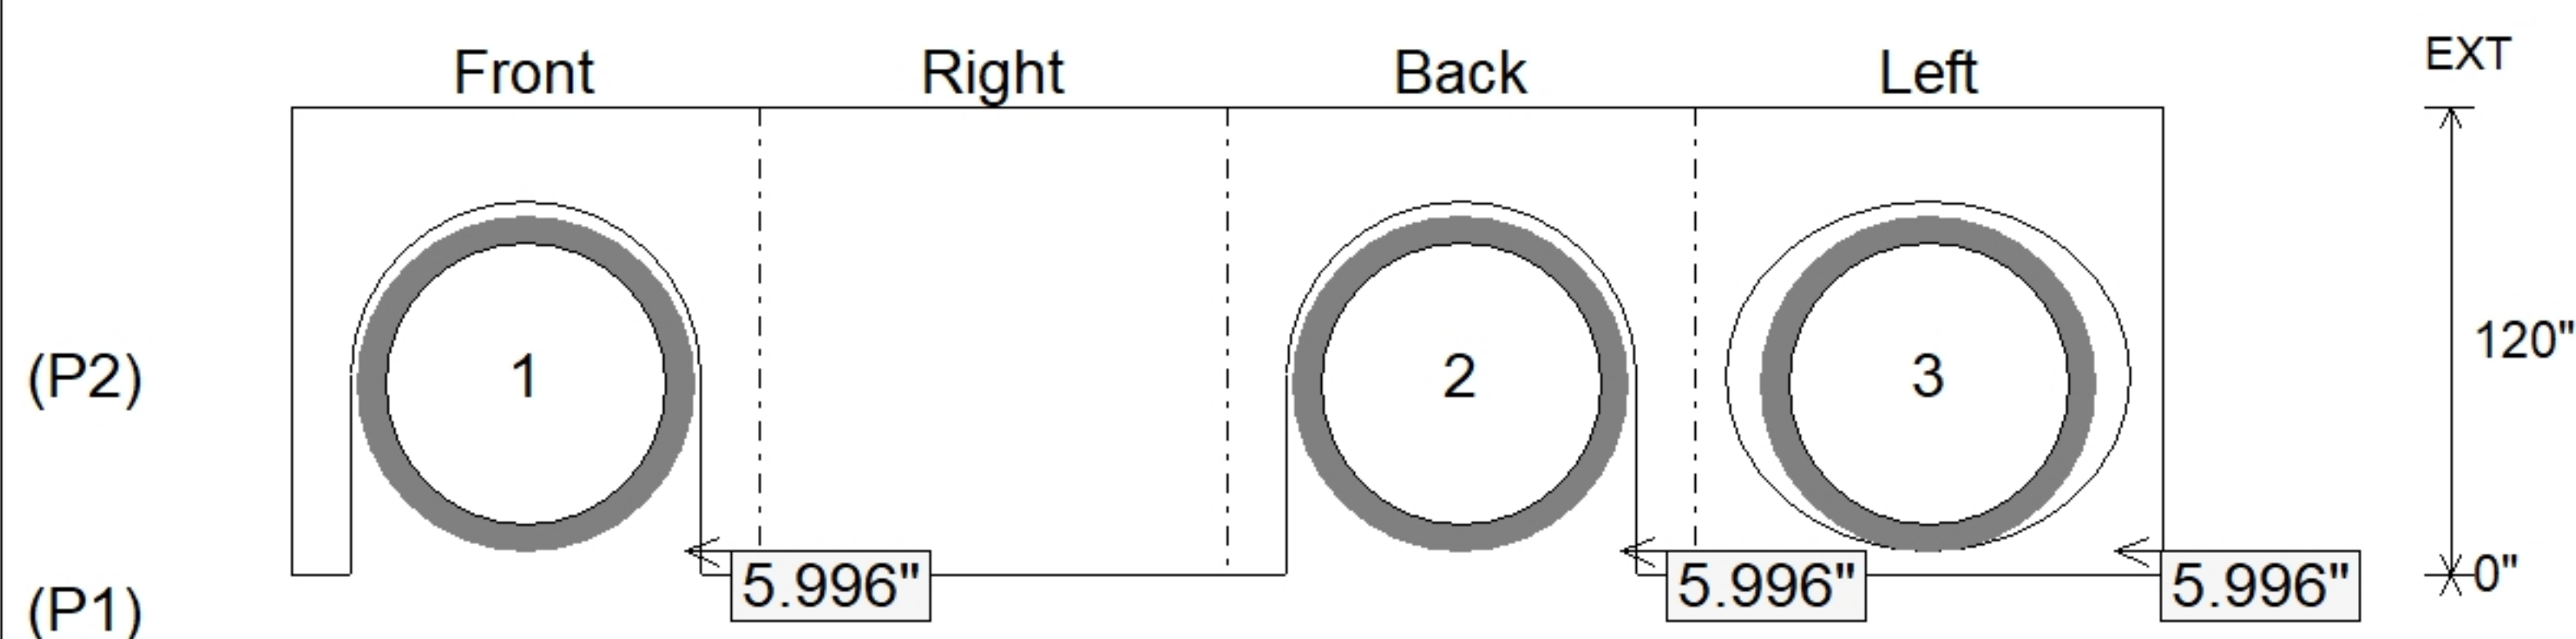

SUBMITTAL
APPROVED BY:
