



Floor (Bot): 527.917'
Overall Height: 23.083'
Slack: 2.4"

P6) 24" - CASTING HEIGHT - 7"	0 lb
P5) 48" - ECC CONE w/ 24" HOLE - 30"	2050 lb
P4) 48" - MH RISER - 60"	4192 lb
P3) 48" - MH RISER - 60"	4192 lb
P2) 120" - MH Transition Slab 48" Hole - 12"	8887 lb
P1) 120" - MH BASE - 96"	39415 lb
1) 120" - Conseal CS-102 1.00"	0 lb
3) 48" - Conseal CS-102 1.00"	0 lb
1) 24" - Conseal CS-102 1.00"	0 lb
2) Hole - 90	0 lb
20) MH Step ML-10-TDS-NCR - 10"	0 lb


Structure Total:	58735 lb

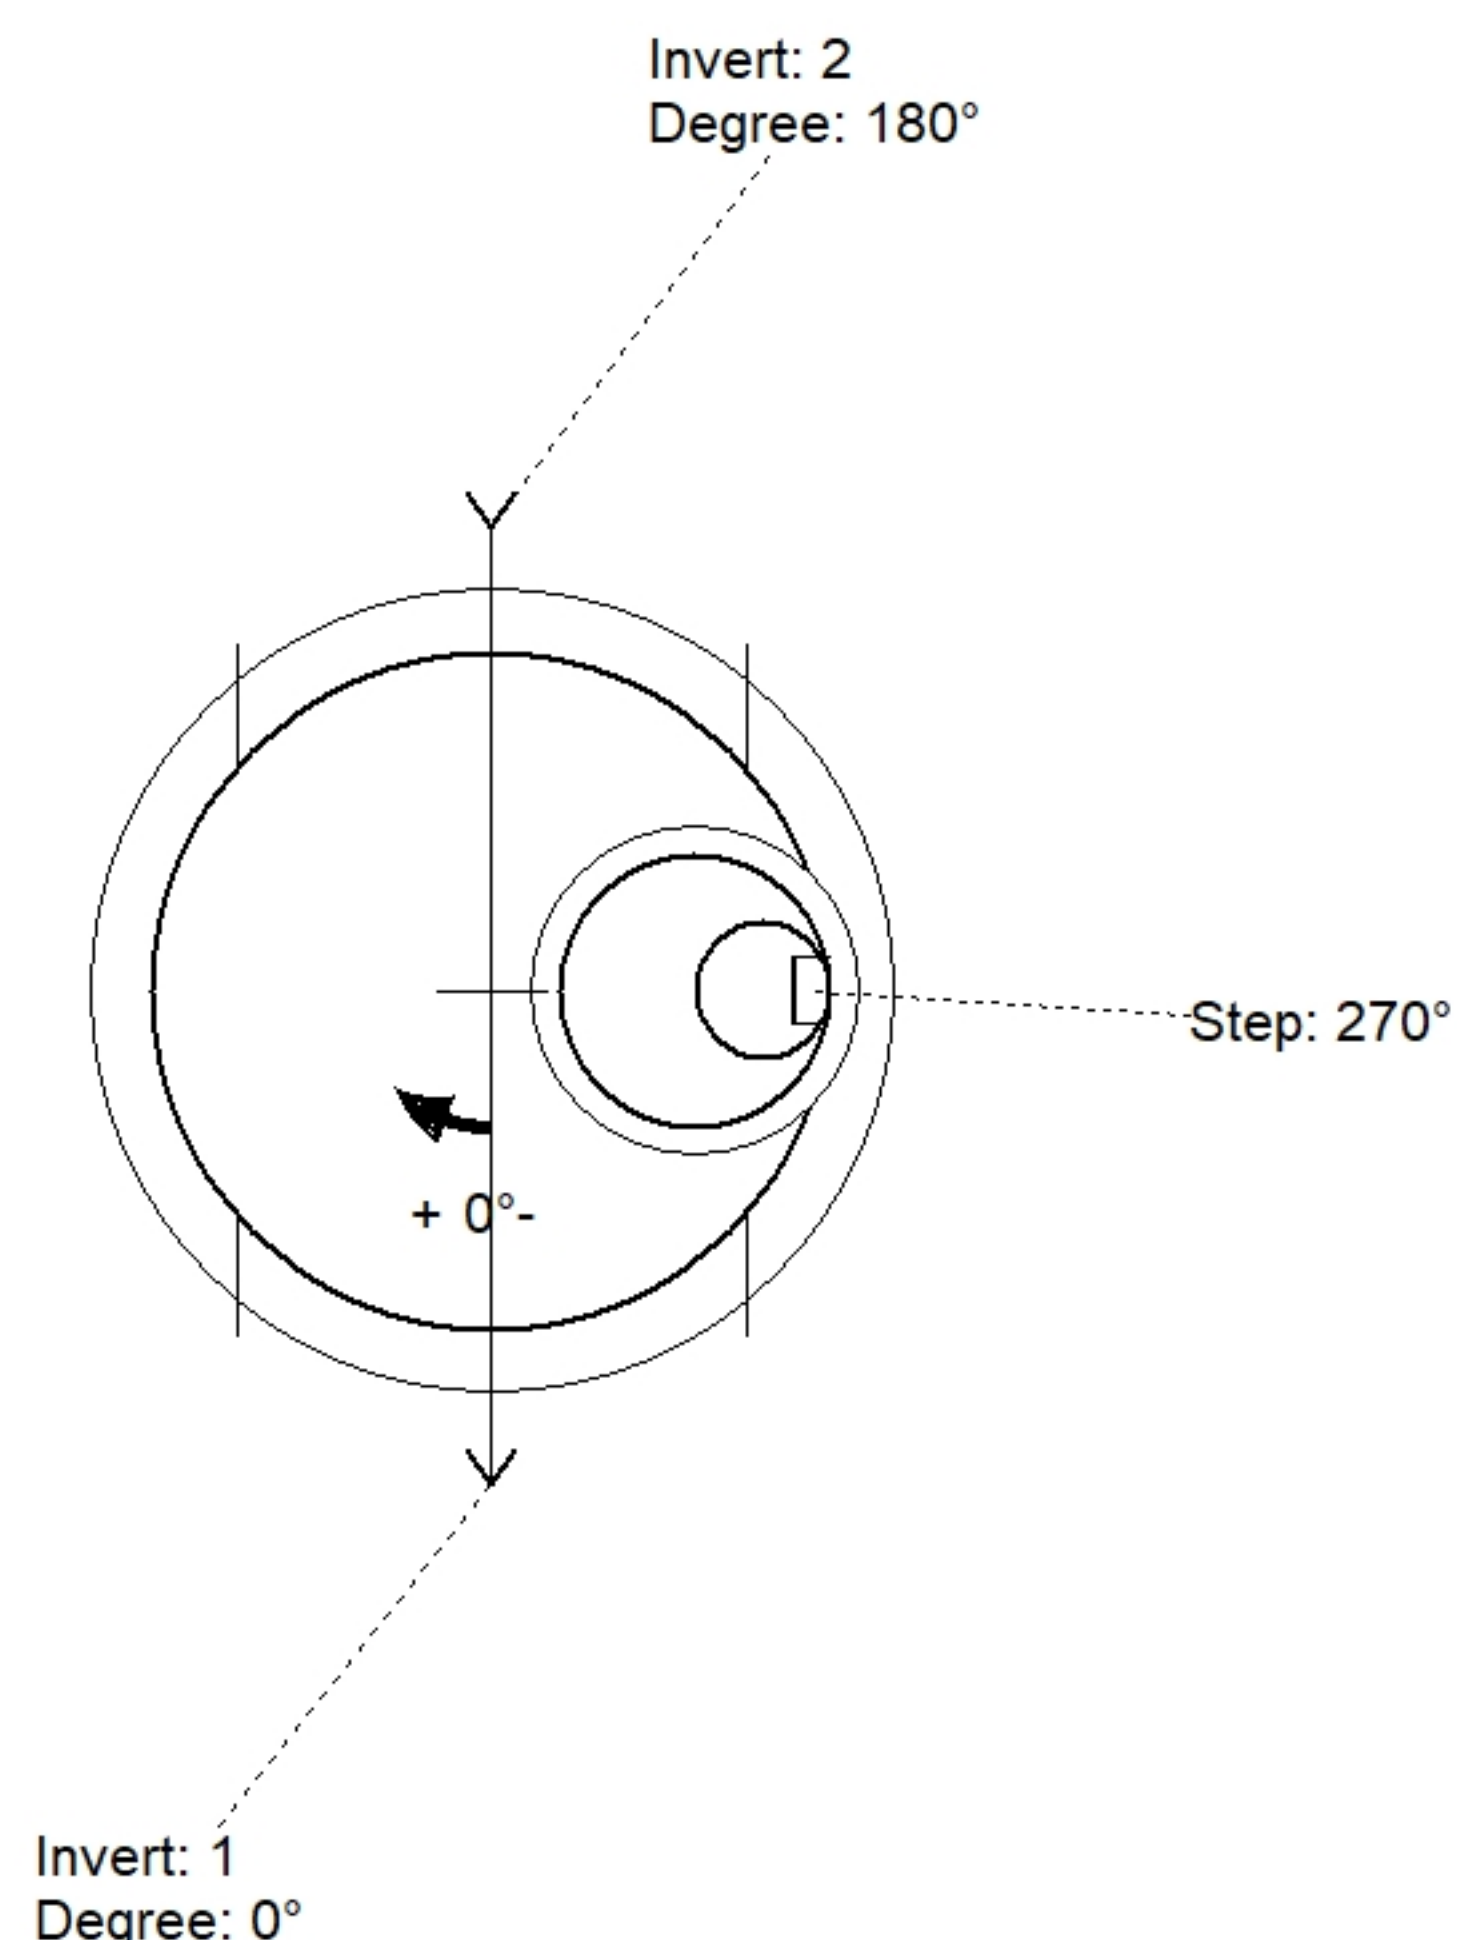

Position	Elev	Angle	Pipe	Pipe OD	Hole	Connector	Up ()	Ref
Rim	551.2'							
Reducer	536.917'							
Invert 1	529.5'	0°	72" RCP B WALL	86"	90"	Hole 90	0"	P1
Invert 2	529.5'	180°	72" RCP B WALL	86"	90"	Hole 90	0"	P1
Invert 3								
Invert 4								
Invert 5								
Invert 6								
Invert 7								
Invert 8								

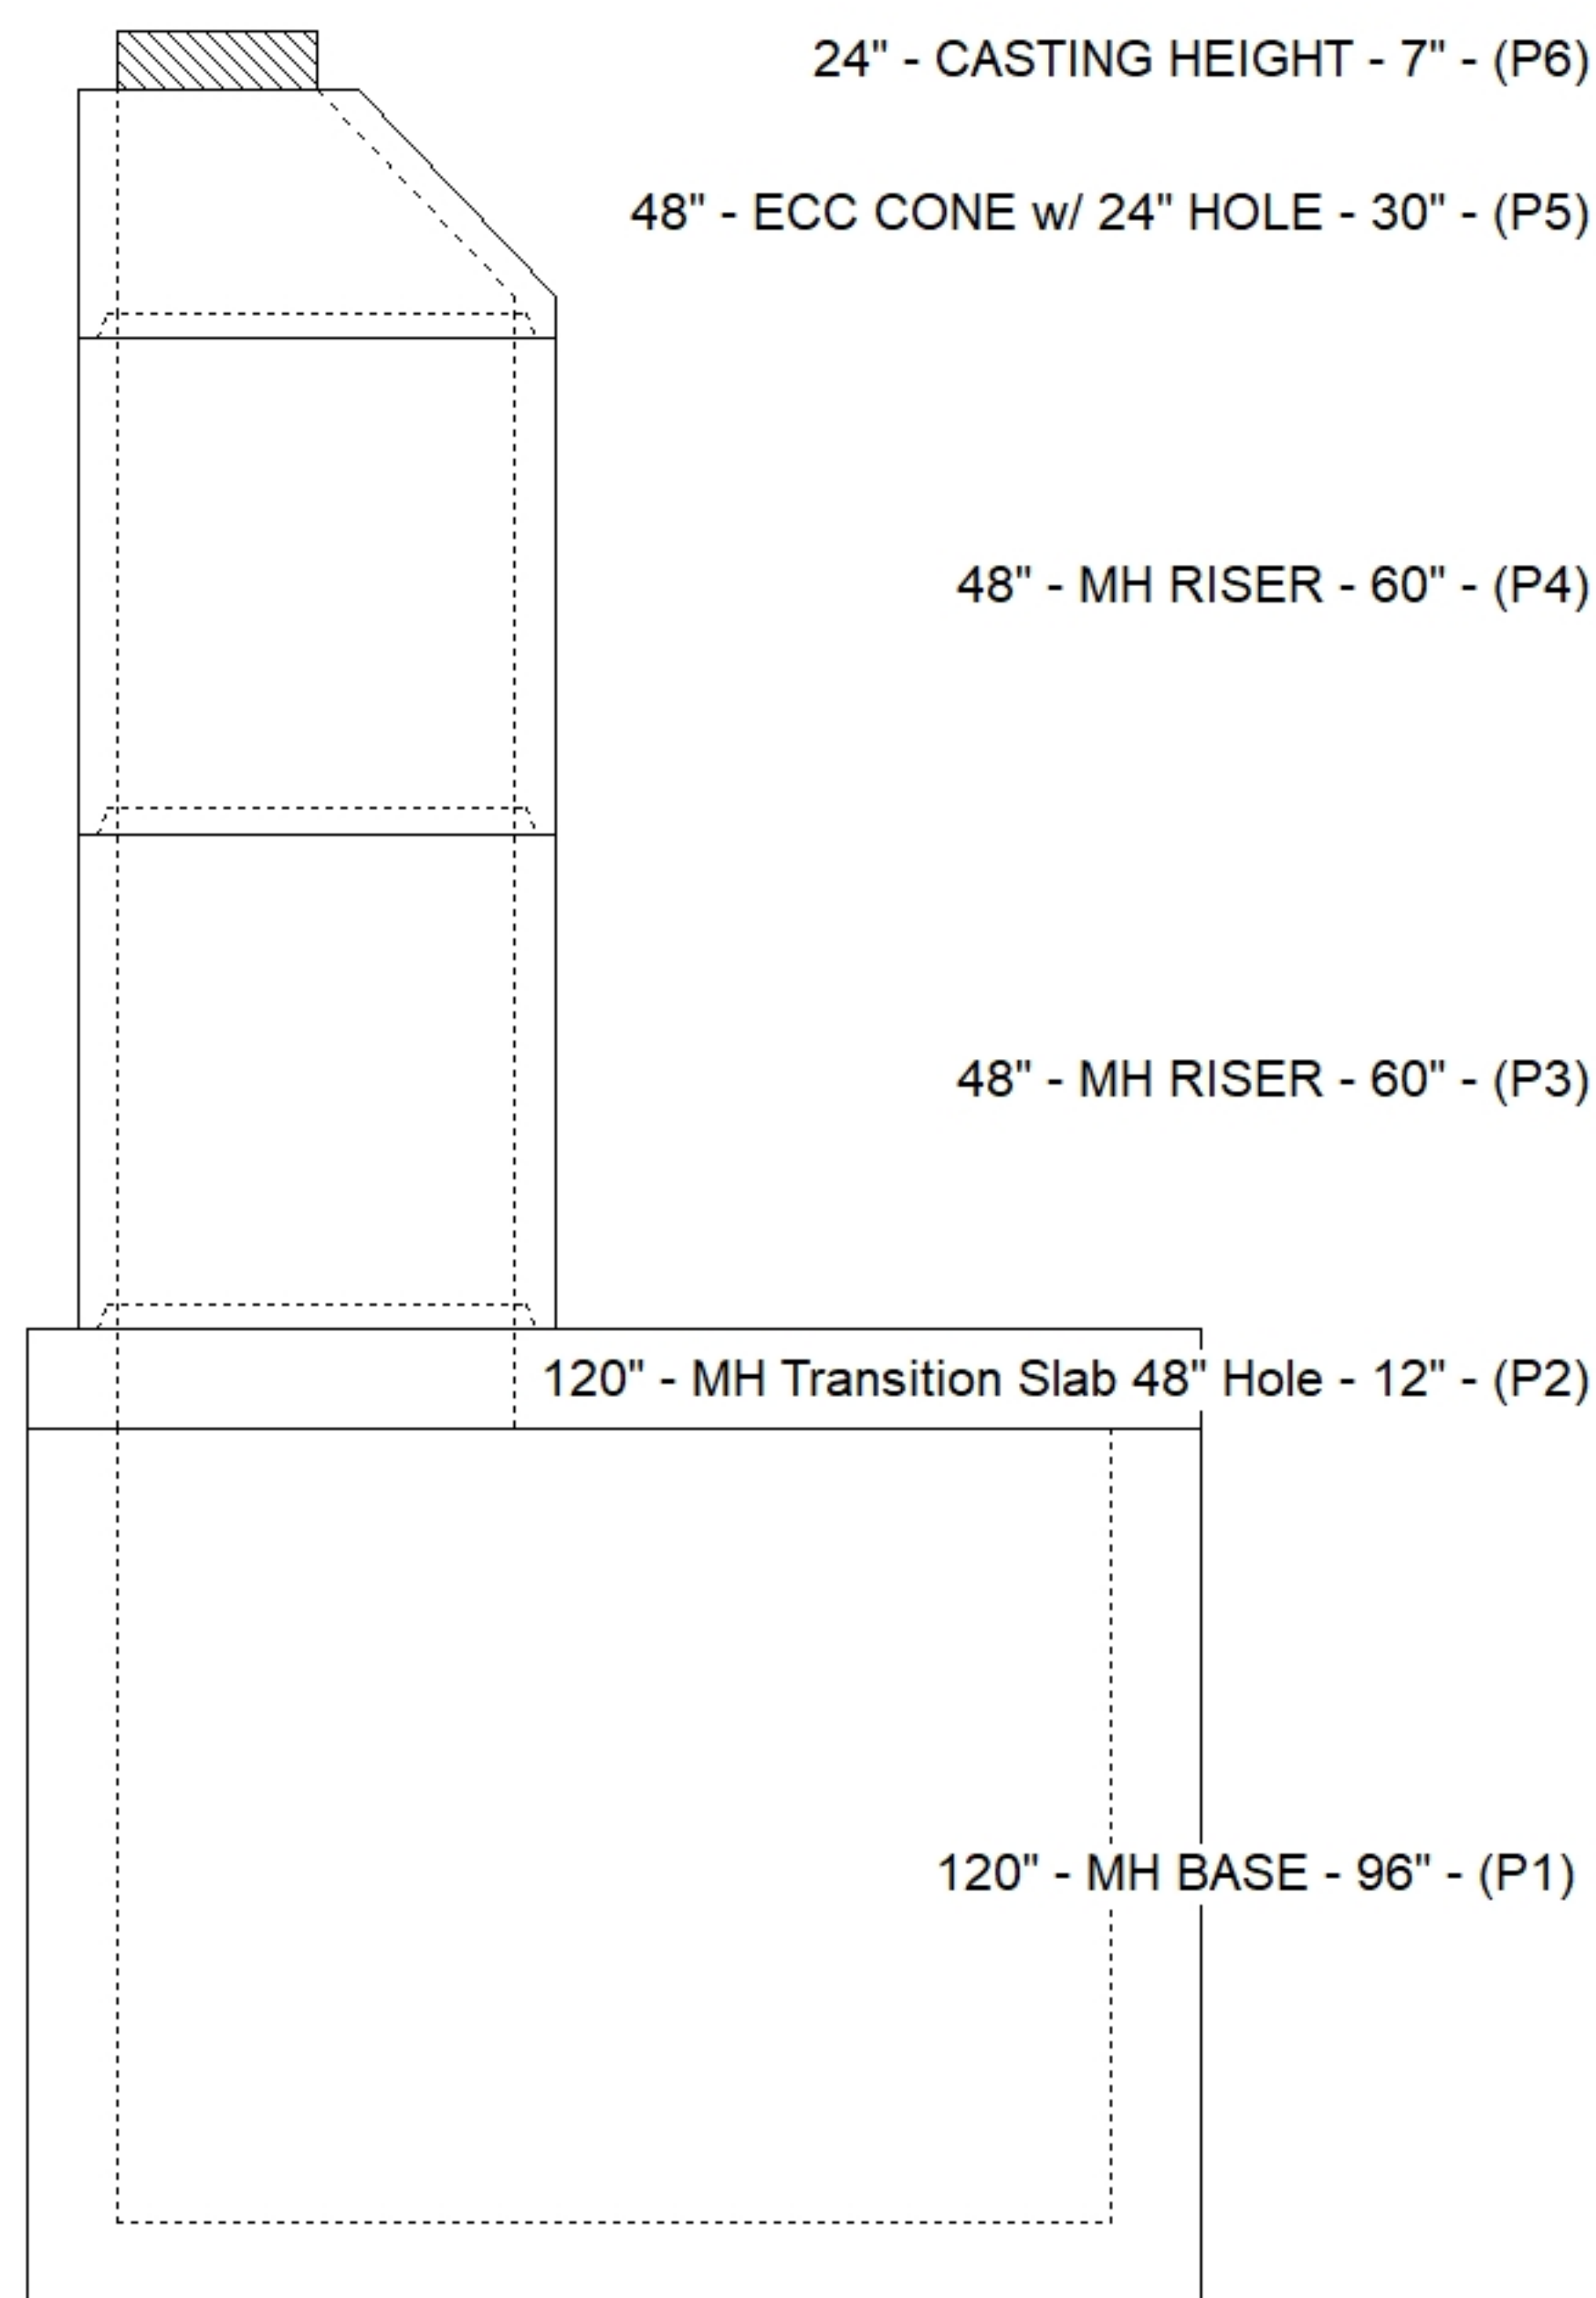

Default - Interior Dimensions

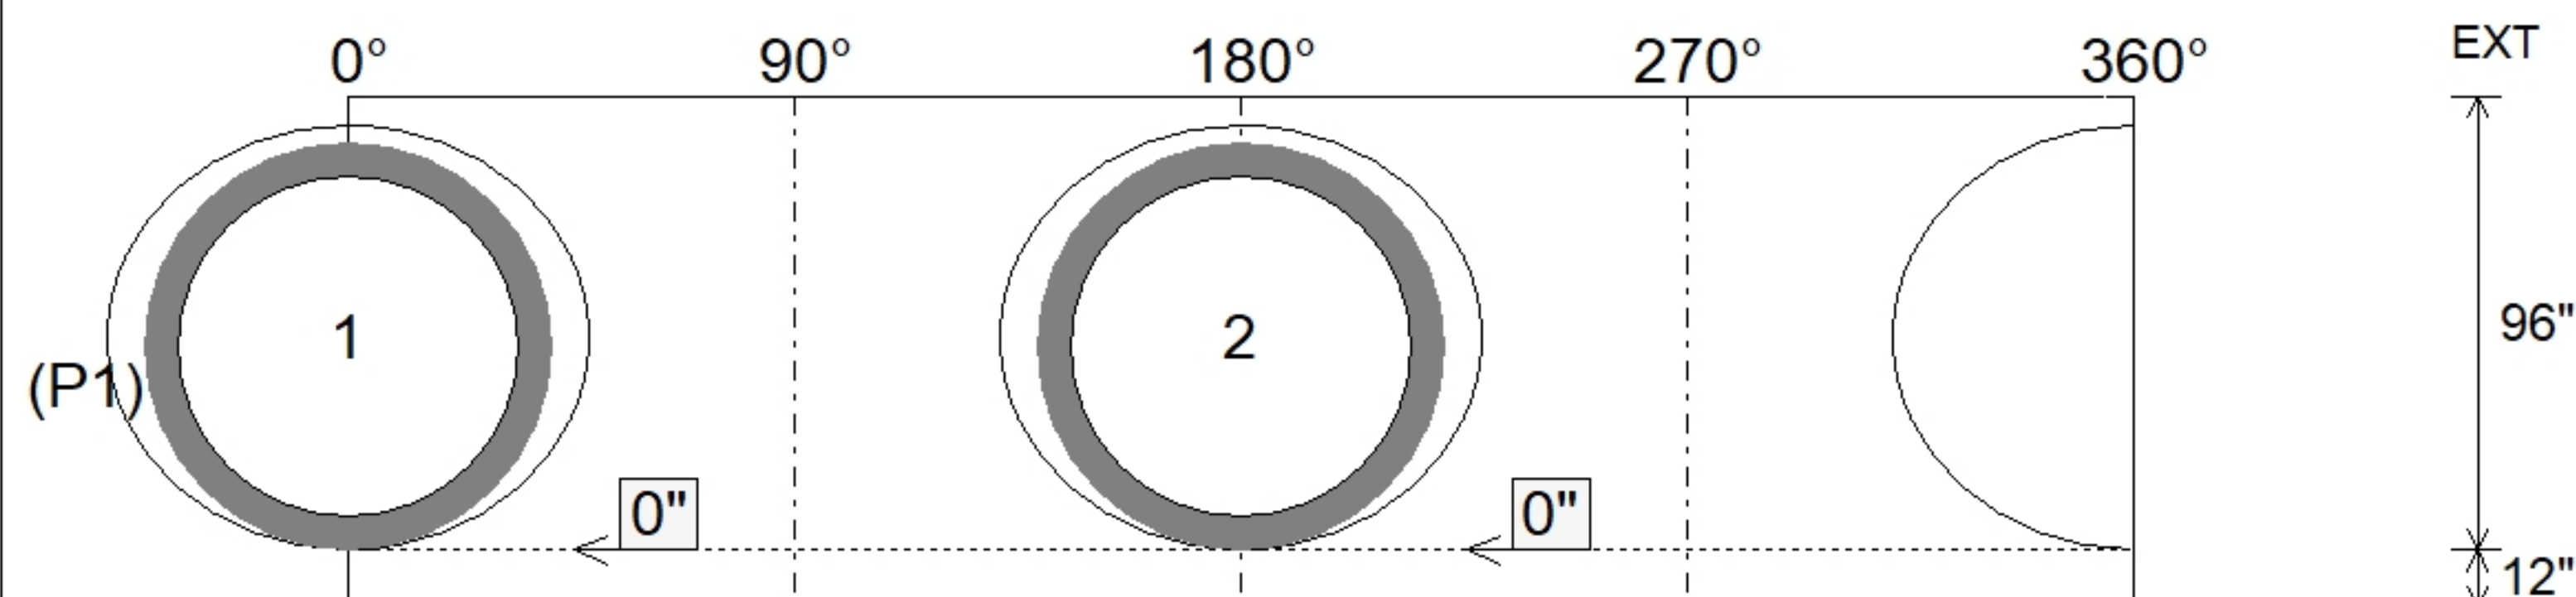

SUBMITTAL
APPROVED BY:
