

Job Name: 26-3439 - Vertiv Warehouse
Job Location: Ironton, OH 45638
Contractor: J&H Reinforcing & Structural Erectors

Plant: Beaver Dam
9/17/2026 2:22:12 PM

Tech: J. Coppage
PC: M. Sullivan



Structure ID: JB-5


P3 BX120120-15TS10W-48ECC

CB TRANSITION SLAB 48" HOLE

- P6) 24" - CASTING HEIGHT - 7"
P5) 48" - ECC CONE w/ 24" HOLE - 36"
P4) 48" - MH RISER - 60"
P3) 120" x 120" - CB TRANSITION SLAB 48" HOLE - 15"
P2) 120" x 120" - BOX RISER 10inW, Variable Ht - 120"
P1) 120" x 120" - P.I.P. BY OTHERS - BTM SLAB - 0"
2) 48" - SGL 1"x14.5' Butyl
1) Hole - 90
1) DOGHOUSE INVRTD - 24"x24"
1) DOGHOUSE - 90"x90"
19) MH Step ML-10-TDS-NCR - 10"

Structure Total:


- 0 lb
3000 lb
4192 lb
22392 lb
39878 lb
0 lb
0 lb
0 lb
0 lb
0 lb
0 lb
69462 lb
- Structure Notes:
1. JR HOE MC-375 PROVIDED BY ICAST.
2. PER ASTM C913/C478 SPECIFICATIONS.
3. CONCRETE = 4,000 PSI AT 28 DAYS.
4. REINFORCEMENT PER ASTM A615 (GRADE 60)
- 48" CONE (As .12)
- 48" RISER (As .12)
- TRANS SLAB
-- TOP MAT: #4 BAR @ 10"
-- BOT. MAT: #5 BAR @ 6"
- WALLS: DBL MATS #5 BAR @ 8" O.C.E.W.
5. BOTTOM RISER (P2) TO BE DELIVERED
W/ THE STYROFOAM & REBAR IN PLACE FOR
INV. #1 OPENING & REMOVED IN THE FIELD
BY OTHERS ONCE IT IS SET IN PLACE.

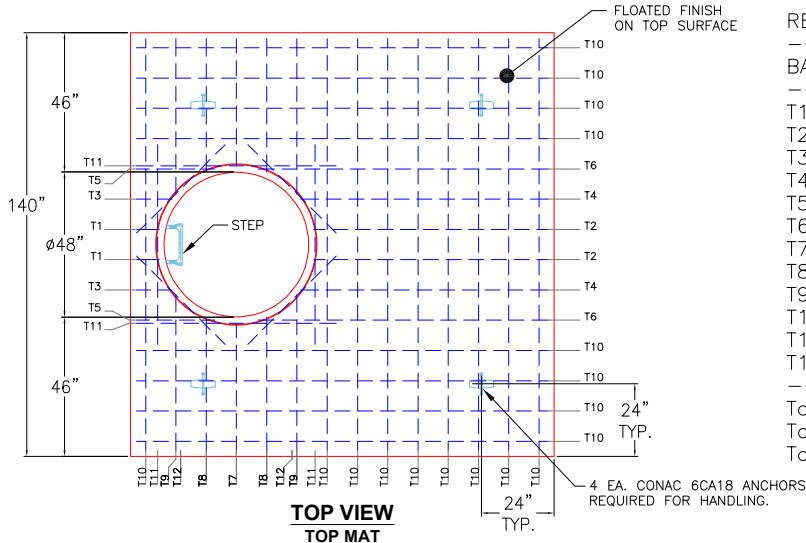

REBAR TAKEOFF (TOP LAYER)

BAR	SIZE	LENGTH	QTY	SHAPE
T1	4	7 in (0'-7")	2 pcs	STR
T2	4	77 in (6'-5")	2 pcs	STR
T3	4	12 in (1'-0")	2 pcs	STR
T4	4	82 in (6'-10")	2 pcs	STR
T5	4	26 in (2'-2")	2 pcs	STR
T6	4	96 in (8'-0")	2 pcs	STR
T7	4	42 in (3'-6")	2 pcs	STR
T8	4	44 in (3'-8")	4 pcs	STR
T9	4	51 in (4'-3")	4 pcs	STR
T10	4	136 in (11'-4")	17 pcs	STR
T11	4	66 in (5'-6")	4 pcs	STR
T12	4	41 in (3'-5")	4 pcs	DIAG


Total Pieces: 47 Pcs
Total Footage: 317.28 LF
Total Weight: 211.94 lbs (0.106 Tons)

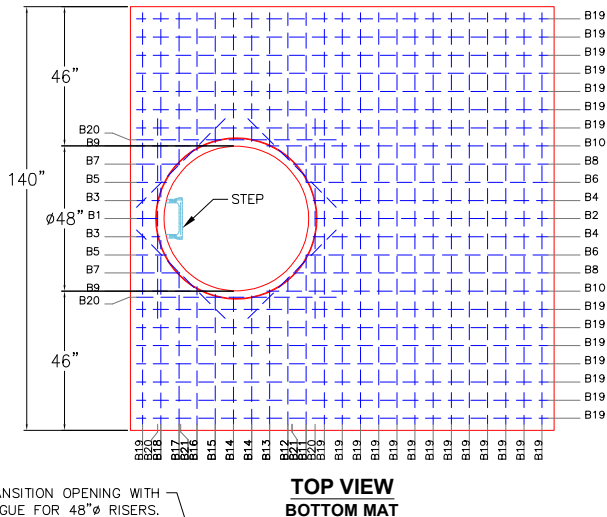

REBAR TAKEOFF (BOTTOM LAYER)

BAR	SIZE	LENGTH	QTY	SHAPE
B1	5	7 in (0'-7")	1 pcs	STR
B2	5	77 in (6'-5")	1 pcs	STR
B3	5	8 in (0'-8")	2 pcs	STR
B4	5	78 in (6'-6")	2 pcs	STR
B5	5	10 in (0'-10")	2 pcs	STR
B6	5	80 in (6'-8")	2 pcs	STR
B7	5	14 in (1'-2")	2 pcs	STR
B8	5	84 in (7'-0")	2 pcs	STR
B9	5	23 in (1'-11")	2 pcs	STR
B10	5	93 in (7'-9")	2 pcs	STR
B11	5	56 in (4'-8")	2 pcs	STR
B12	5	48 in (4'-0")	2 pcs	STR
B13	5	44 in (3'-8")	2 pcs	STR
B14	5	42 in (3'-6")	4 pcs	STR
B15	5	43 in (3'-7")	2 pcs	STR
B16	5	45 in (3'-9")	2 pcs	STR
B17	5	50 in (4'-2")	2 pcs	STR
B18	5	61 in (5'-1")	2 pcs	STR
B19	5	136 in (11'-4")	28 pcs	STR
B20	5	66 in (5'-6")	4 pcs	STR
B21	5	41 in (3'-5")	4 pcs	DIAG

Total Pieces: 72 Pcs
Total Footage: 497.19 LF
Total Weight: 518.57 lbs (0.259 Tons)



Coating (Int): Coating (Ext):	Seam Up: Tongue Seam Dn: Flat	Wall Thickness: 10"	Height (Ext): 15"	Weight (Net): 22392 lb Volume (Net): 5.72cu.yd
----------------------------------	----------------------------------	---------------------	-------------------	---
