


Job Name: 26-3474 - Marksmen Manor- Storm
 Job Location: Tell City, IN
 Contractor: Love Excavating LLC

Plant: 100
 10/14/2026 8:44:03 AM

Tech: Jared - F
 PC: M. Sullivan



Structure ID: 421

P1 BX2436-06W08F-BAVF

BOX BASE 6inW, 8inF, Variable Ht

P2) 24" x 36" - CASTING HEIGHT - 7.875

P1) 24" x 36" - BOX BASE 6inW, 8inF, Variable Ht - 19"

1) CASTING - HOE R-3287-10V SET (F/G/H)

1) 24" x 36" - Con Seal CS-102 1.00"

1) DOGHOUSE INVRTD - 20"x19"

1) Hole - 16

Structure Notes:
 1. INDOT INLET TYPE J10 / ASTM C913 SPEC'S.
 2. CONCRETE = 4,000 PSI AT 28 DAYS.
 3. NO STEPS AND NO INVERT CHANNEL.
 4. CASTING BY ICAST (HOE R-3287-10V SET (F/G/H))


Structure Total: 2707 lb
 REINFORCING PER ASTM A615 (GRADE 60).
 - WALLS (As .31) #5 BARS AT 12" C.C.E.W.
 - FLOOR (As .31) #5 BARS AT 12" C.C.E.W.

Rim: 419.41' Rim to Invert: 2.16' Slack: 0.346" Sump: 1.3" Step Position:


Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up ()	Offset
Invert 1	417.25'	90°	24"	15" HDPE	17.6"	DOGHOUSE INVRTD 20"x19"	20" x 19"	20"	0"	0"
Invert 2	417.25'	270°	24"	12" HDPE	14.5"	Hole 16	16"	16"	0.05"	0"
Invert 3										
Invert 4										
Invert 5										
Invert 6										
Invert 7										
Invert 8										

RIGHT-SIDE UP VIEW (int. dimensions)


UPSIDE-DOWN VIEW (int. dimensions)

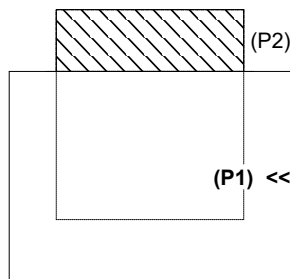

Invert: 1
 Degree: 90°
 Horz: 18"
 Hole: 20" x 19"
 Up(): 0"




Invert: 2
 Degree: 270°
 Horz: 18"
 Hole: 16"
 Up(): 0.05"



Invert: 1
 Degree: 90°
 Horz: 18"
 Hole: 20" x 19"
 Up(): 0"

INSIDE WALL DIMENSIONS

(P1)



Coating (Int):
 Coating (Ext):

Seam Up: Flat
 Seam Dn: n/a

Wall Thickness: 6"
 Floor Height: 8"

Height (Int): 19"
 Height (Ext): 27"

Weight (Net): 2265 lb
 Volume (Net): 0.58cu.yd
