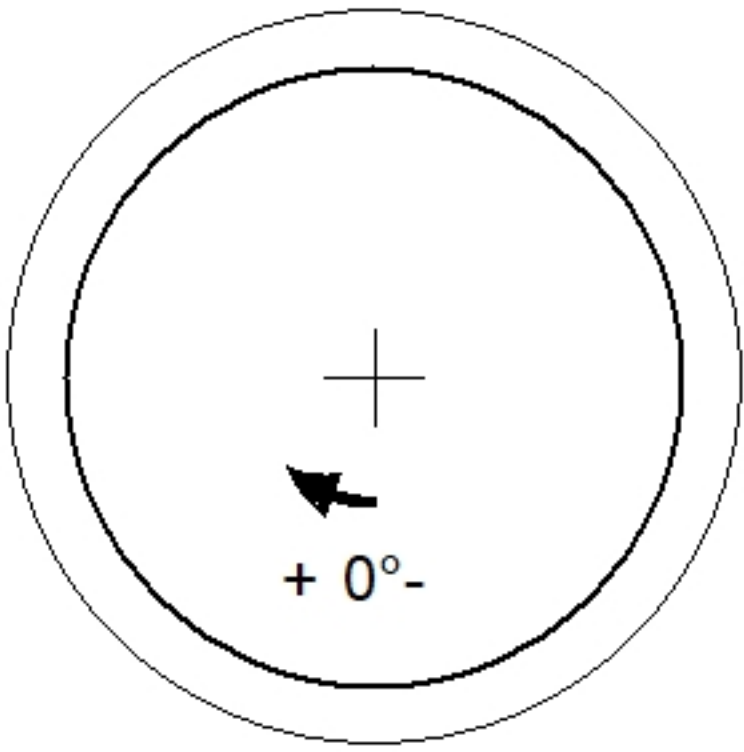
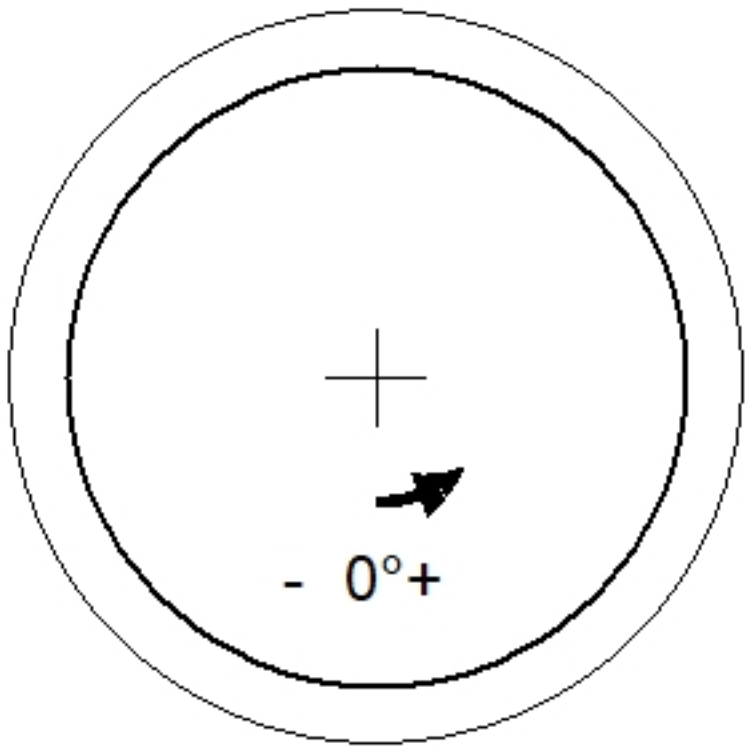
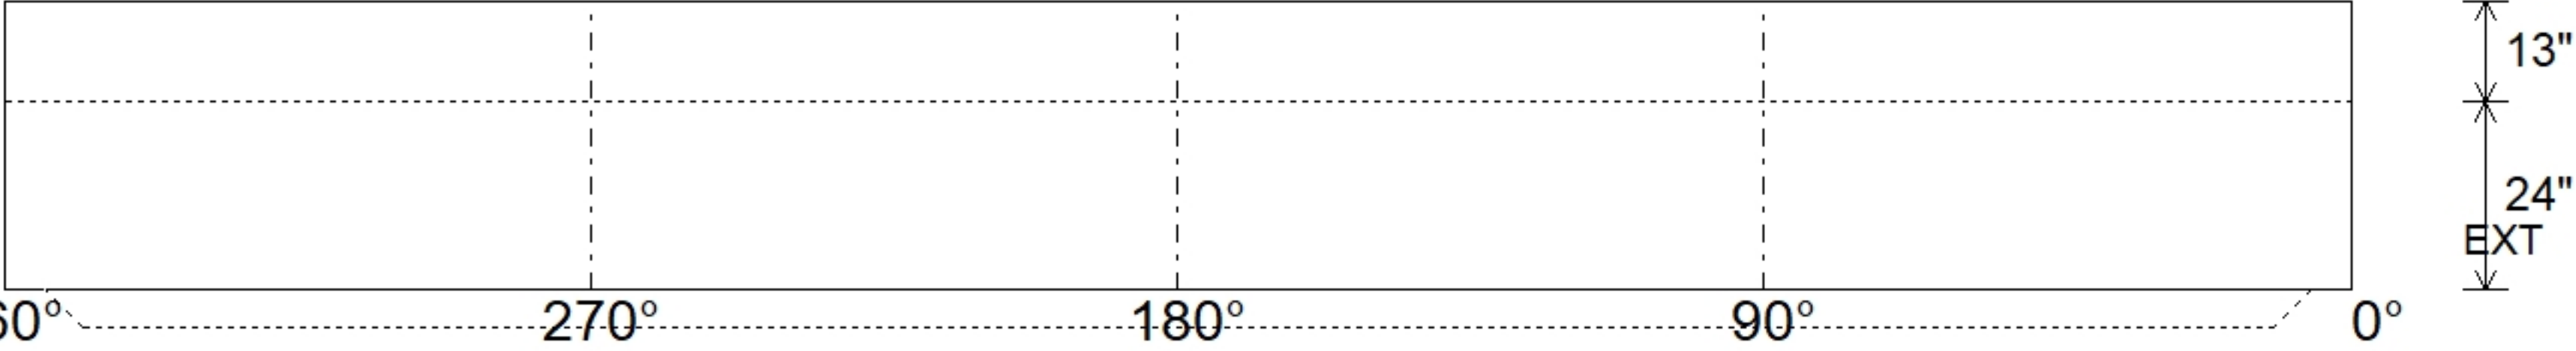


Job Name: 26-3478 859306 Schlatter Road Apartments Job Location: Louisville, KY Contractor: Contech Engineering Solutions					Plant: Beaver Dam 9/2/2026 9:43:08 AM		Tech: S. Felletter PC: C. Goff						
Structure ID: 10-CS-8													
P1		MH096BAVF			MH MONOBASE 13F, Custom Ht T/n								
P5) 24" - CASTING HEIGHT - 4" P4) 96" - MH FLAT TOP SPEC. (2 - 24"Ø HOLES) F/G - 17" P3) 96" - MH RISER T/G - 36" P2) 96" - MH RISER Custom Ht T/G - 92" P1) 96" - MH MONOBASE 13F, Custom Ht T/n - 24" 1) ASSEMBLY REQUIRED 1) CVSTENCILING 3) 96" - Conseal CS-102 1.00" 1) 24" - Conseal CS-102 1.00" 2) Hole - 24						0 lb 10015 lb 8968 lb 22227 lb 17113 lb 0 lb 0 lb 0 lb 0 lb 0 lb ----- 58323 lb		Structure Notes: 4" CASTING BY OTHERS LIFTING ANCHORS TO BE INSTALLED ON THE OUTSIDE OF THE STRUCTURE ICAST TO INSTALL THE INTERNALS CONTECH'S LOGO AS WELL AS THE INLET AND OUTLET MUST BE STENCILED ONTO THE STRUCTURE					
Rim: 652.5' Rim to Invert: 7.65' Slack: 0.844" Sump: 82.044" Step Position:													
Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up (⌋)	Offset			
Invert 1													
Invert 2													
Invert 3													
Invert 4													
Invert 5													
Invert 6													
Invert 7													
Invert 8													
RIGHT-SIDE UP VIEW (int. dimensions) UPSIDE-DOWN VIEW (int. dimenions)   INSIDE WALL DIMENSIONS 													
Coating (Int): Coating (Ext):				Seam Up: Tongue Seam Dn: n/a		Wall Thickness: 9" Floor Height: 13"		Height (Int): 24" Height (Ext): 37"		Weight (Net): 17113 lb Volume (Net): 4.37cu.yd			
