

Job Name: 26-3478 859306 Schlatter Road Apartments
Job Location: Louisville, KY
Contractor: Contech Engineering Solutions

Plant: Beaver Dam

Tech: S. Felletter

9/2/2026 9:44:02 AM

PC: C. Goff



Structure ID: 10-CS-8

P2 MH096RSVF

MH RISER Custom Ht T/G

- P5) 24" - CASTING HEIGHT - 4"
P4) 96" - MH FLAT TOP SPEC. (2 - 24"Ø HOLES) F/G - 17"
P3) 96" - MH RISER T/G - 36"
P2) 96" - MH RISER Custom Ht T/G - 92"
P1) 96" - MH MONOBASE 13F, Custom Ht T/n - 24"
1) ASSEMBLY REQUIRED
1) CVSTENCILING
3) 96" - Conseal CS-102 1.00"
1) 24" - Conseal CS-102 1.00"
2) Hole - 24"



0 lb
10015 lb
8968 lb
22227 lb
17113 lb
0 lb
0 lb
0 lb
0 lb
0 lb
Structure Total: 58323 lb

Structure Notes:
4" CASTING BY OTHERS
LIFTING ANCHORS TO BE INSTALLED
ON THE OUTSIDE OF THE STRUCTURE
ICAST TO INSTALL THE INTERNALS
CONTECH'S LOGO AS WELL AS THE
INLET AND OUTLET MUST BE
STENCILED ONTO THE STRUCTURE


Rim: 652.5' Rim to Invert: 7.65' Slack: 0.844" Sump: 82.044" Step Position:

Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up ()	Offset
Invert 1	644.85'	270°	268.606"	15" RCP B WALL	19.5"	Hole 24	24"	24.257"	48.544"	0"
Invert 2	644.85'	210°	202.905"	15" RCP B WALL	19.5"	Hole 24	24"	24.467"	48.544"	-6"
Invert 3										
Invert 4										
Invert 5										
Invert 6										
Invert 7										
Invert 8										

RIGHT-SIDE UP VIEW (int. dimensions)

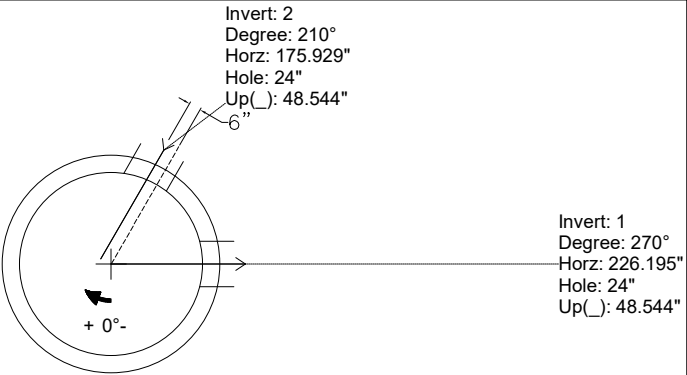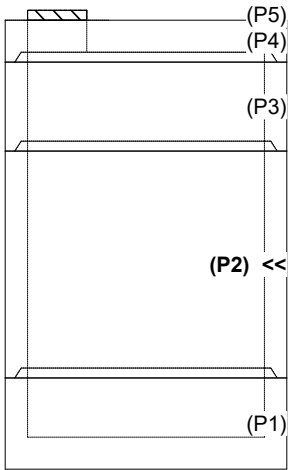

INSIDE WALL DIMENSIONS

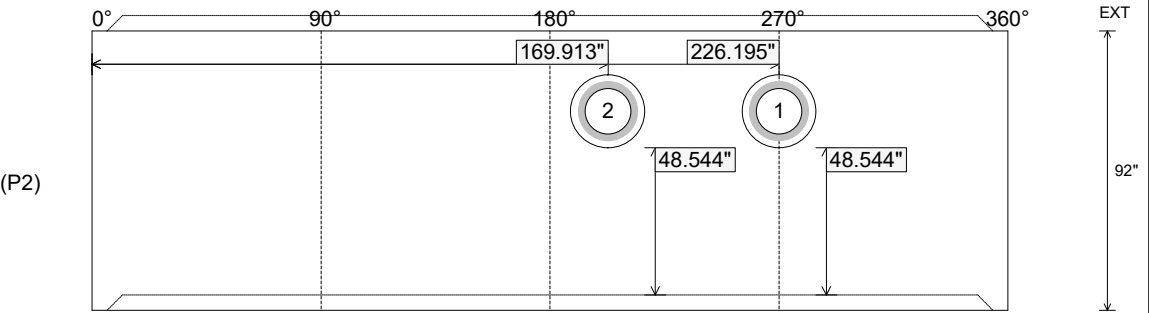

Coating (Int): Coating (Ext):	Seam Up: Tongue Seam Dn: Groove	Wall Thickness: 9" Floor Height: 0"	Height (Int): 92" Height (Ext): 92"	Weight (Net): 22227 lb Volume (Net): 5.68cu.yd
----------------------------------	------------------------------------	--	--	---
