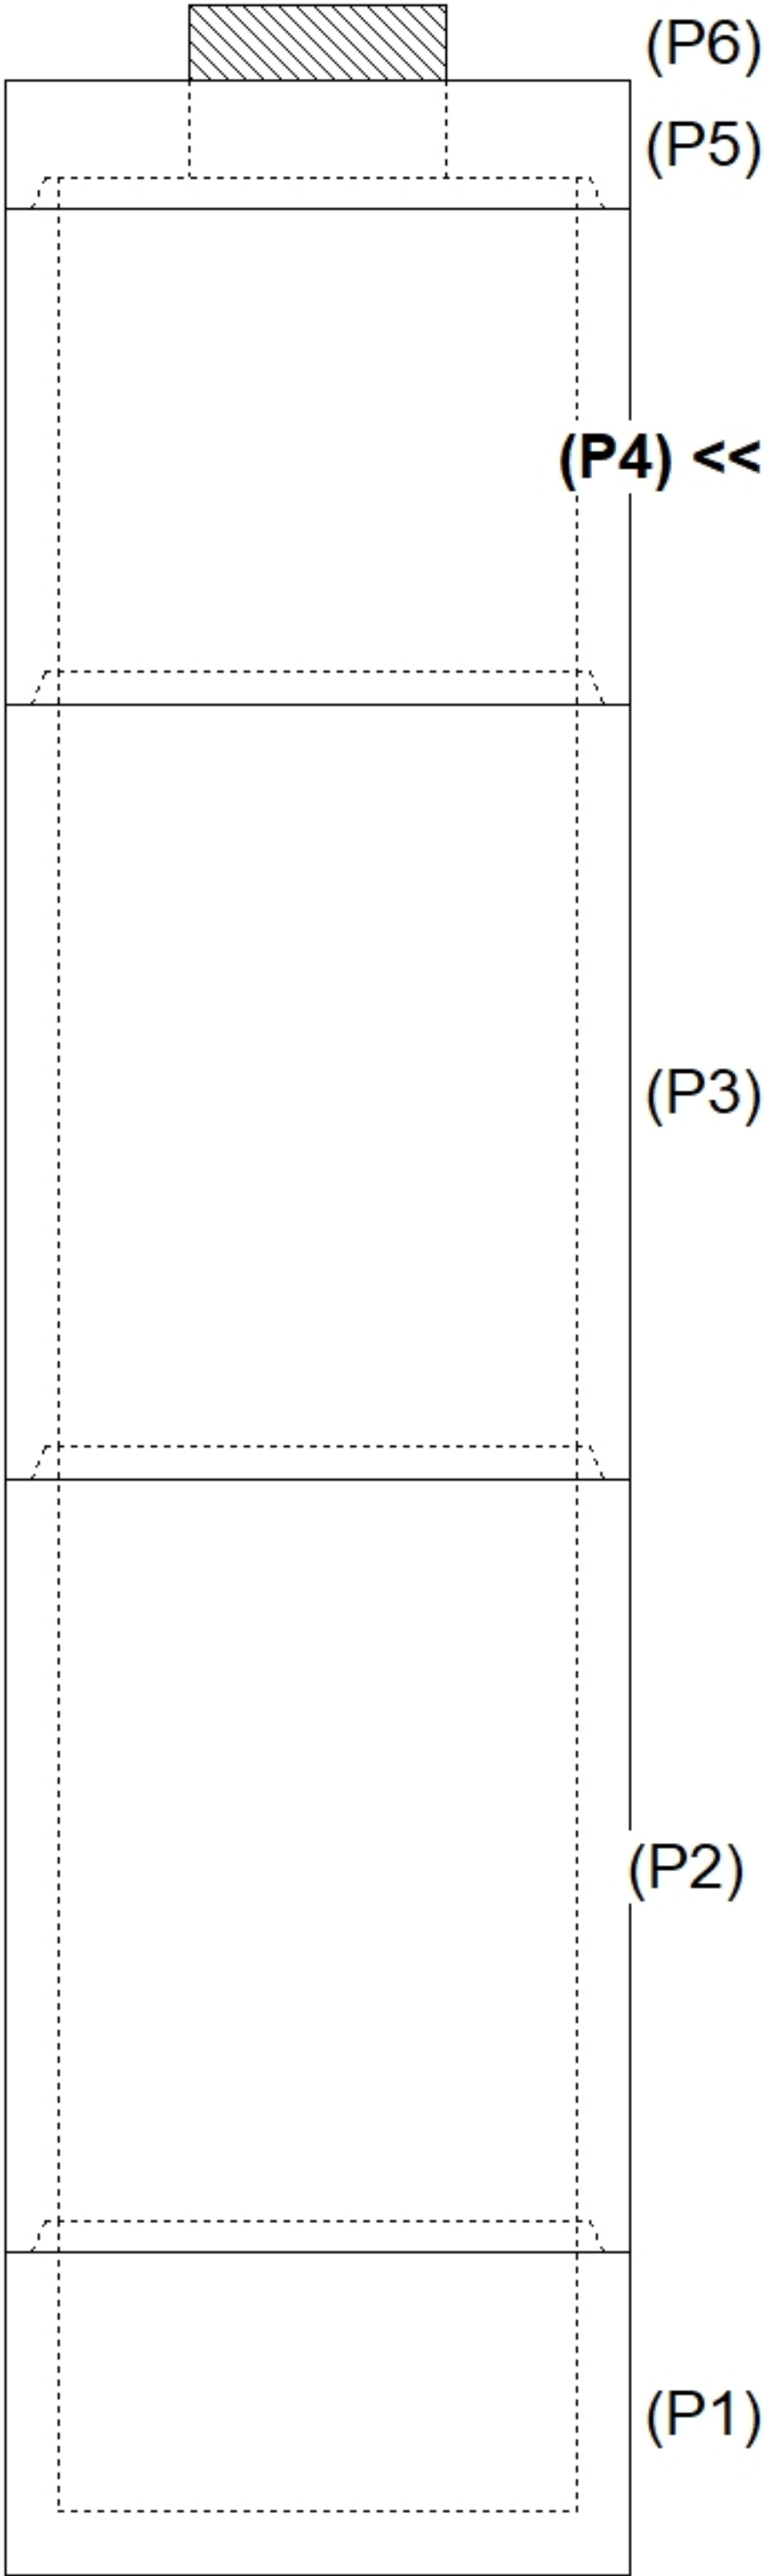
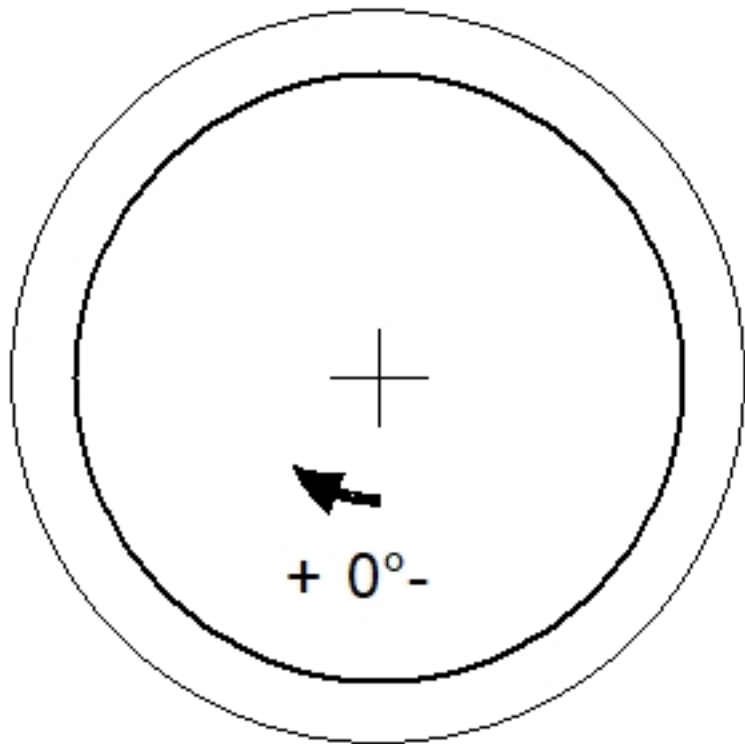
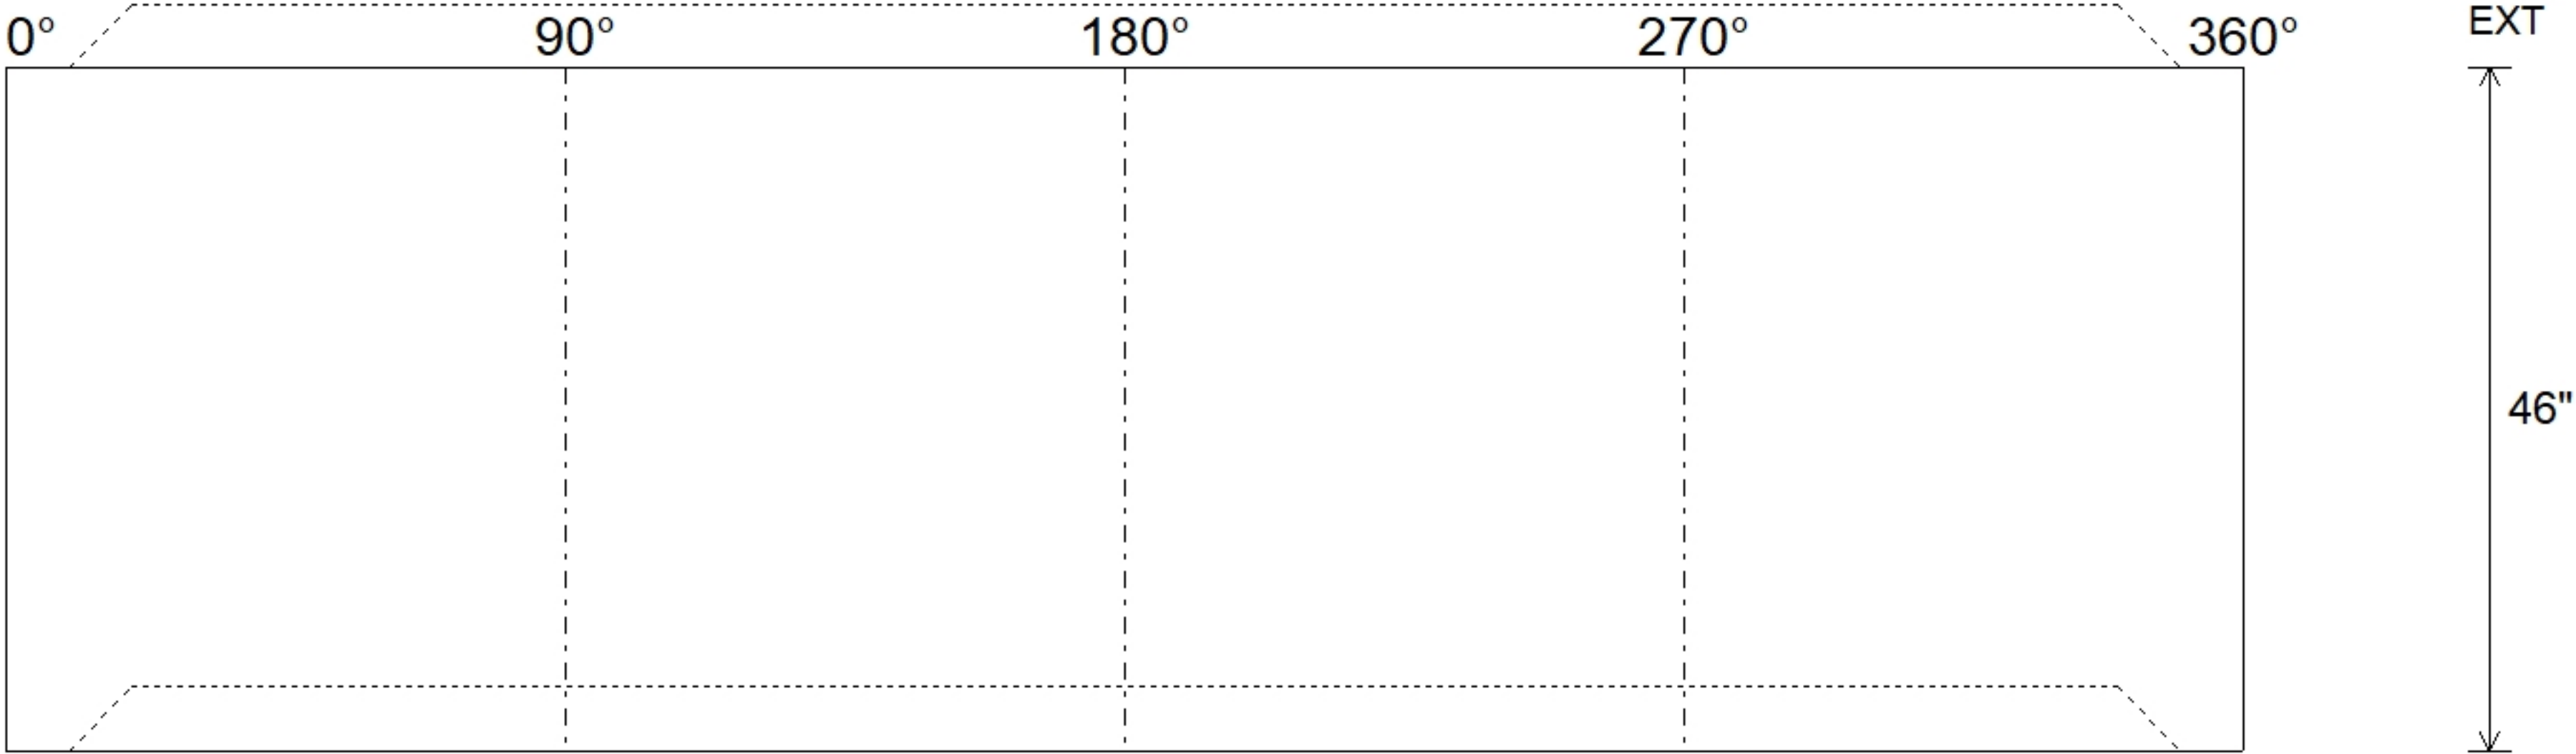


Job Name: 26-3522 ADS Miller-Blankenbaker Rd. Subdivision					Plant: Beaver Dam		Tech: S. Felletter						
Job Location: Jeffersontown, KY					9/3/2026 2:23:59 PM		PC: M. Sullivan						
Contractor: ADS Advanced Drainage Systems, Inc.													
Structure ID: STR-18													
P4			MH048RSVF			MH RISER Custom Ht T/G							
P6) 24" - CASTING HEIGHT - 7" P5) 48" - MH FLAT LID w/24" Center Hole F/G - 12" P4) 48" - MH RISER Custom Ht T/G - 46" P3) 48" - MH RISER NO STEPS T/G - 72" P2) 48" - MH RISER SPECIAL T/G - 72" P1) 48" - MH BASE T/n - 24" 1) JOINT WRAP - 0.065"x6"x50' CONSEAL CS212 1) JOINT WRAP PRIMER - CONSEAL CS-75 (1 gal.) 1) ASSEMBLY REQUIRED 1) CASTING - HOE MC-375 F/C Storm 4) 48" - Conseal CS-102 1.00" (Double) 1) 24" - Conseal CS-102 1.00" (Double) 2) Hole - 16						0 lb 1580 lb 3213 lb 5030 lb 4770 lb 3007 lb 0 lb 0 lb 0 lb 271 lb 0 lb 0 lb 0 lb		Structure Notes: . 1. PER ASTM C478 SPECIFICATIONS. 2. CONCRETE = 4,000 PSI AT 28 DAYS. 3. LIFTING ANCHORS TO BE INSTALLED ON THE OUTSIDE OF THE STRUCTURE 4. CASTING BY ICAST (HOE MC-375 F/C "STORM"). . REINFORCING PER ASTM A615 (GRADE 60). - TOP SLAB (As .62) #5 BARS AT 6" C.C.E.W. - RISER/WALLS (As .12) - FLOOR (As .31) #5 BARS AT 12" C.C.E.W.					
Rim: 722.5' Rim to Invert: 12.7' Slack: 0.4" Sump: 81" Step Position:						Structure Total: 17871 lb							
Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up ()	Offset			
Invert 1													
Invert 2													
Invert 3													
Invert 4													
Invert 5													
Invert 6													
Invert 7													
Invert 8													
RIGHT-SIDE UP VIEW (int. dimensions)													
													
INSIDE WALL DIMENSIONS													
													
Coating (Int): Coating (Ext):				Seam Up: Tongue Seam Dn: Groove		Wall Thickness: 5" Floor Height: 0"		Height (Int): 46" Height (Ext): 46"		Weight (Net): 3213 lb Volume (Net): 0.82cu.yd			
