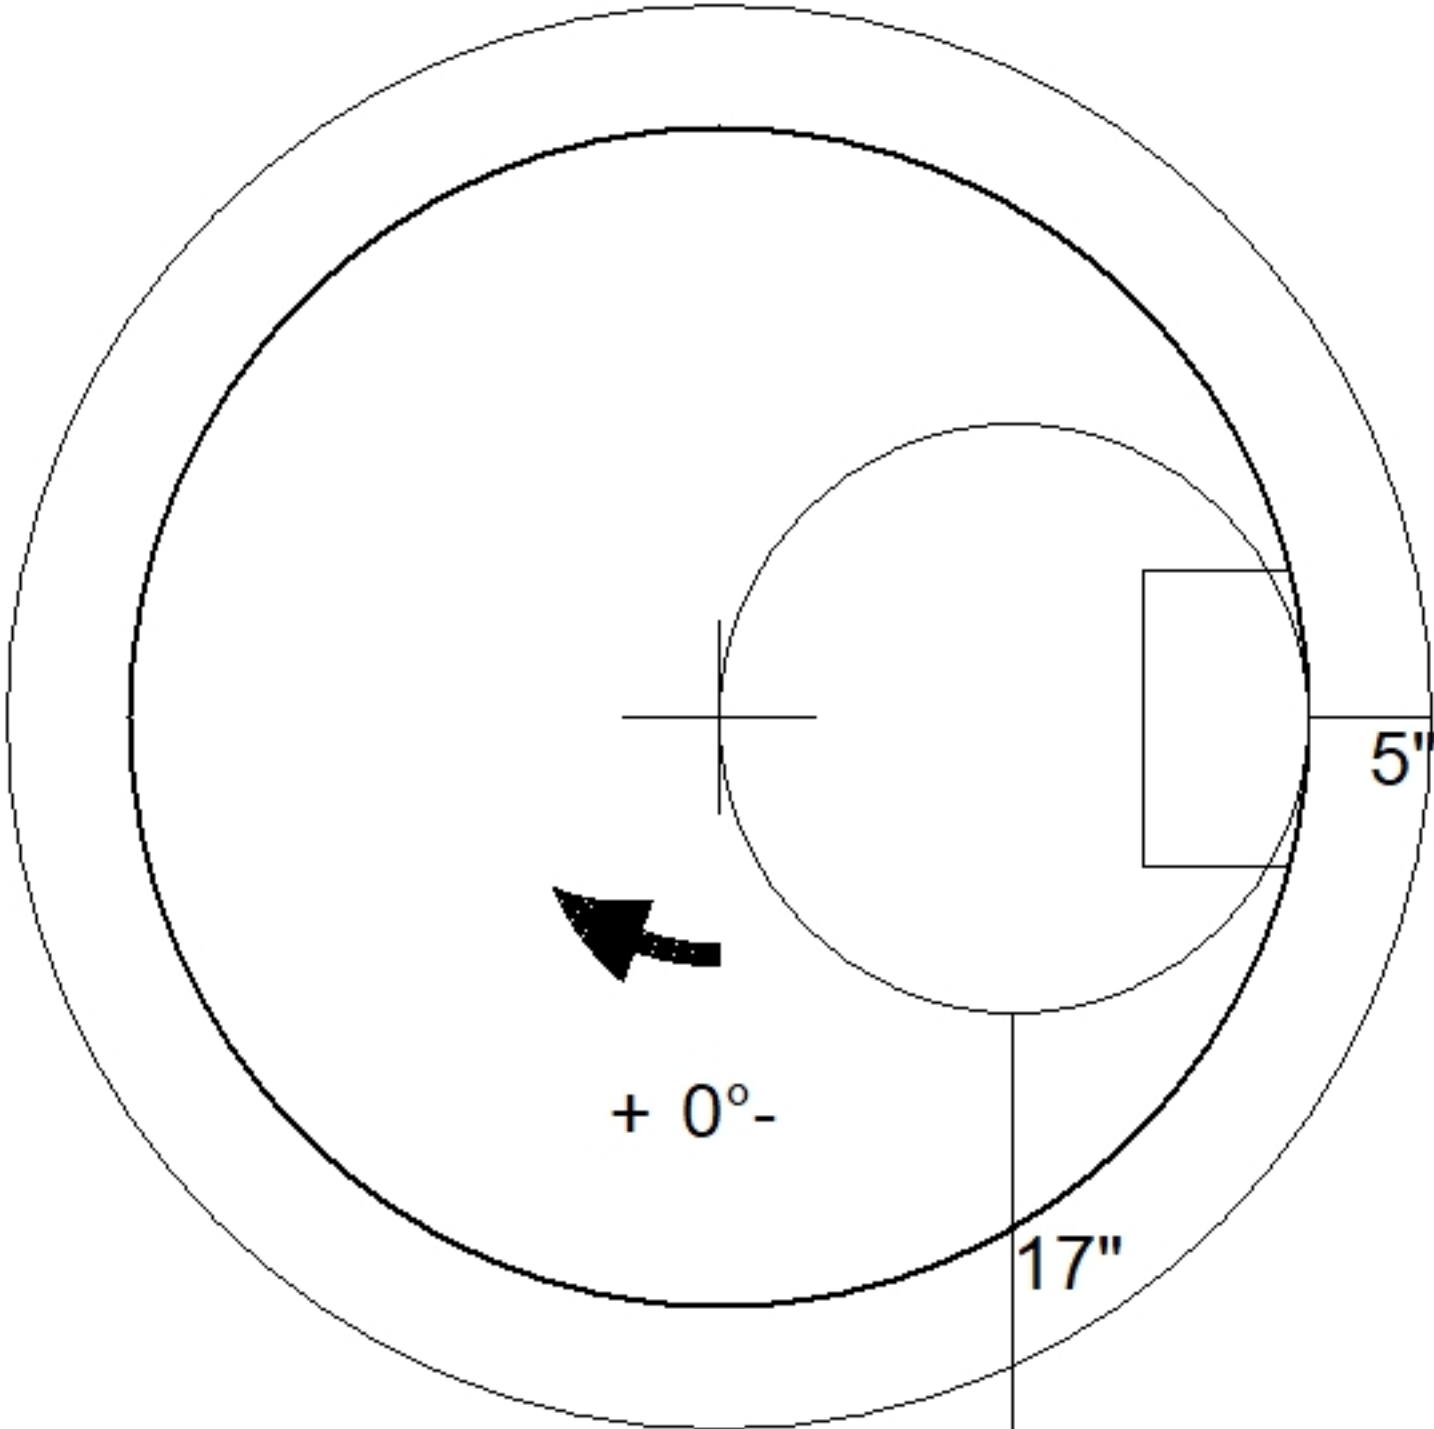
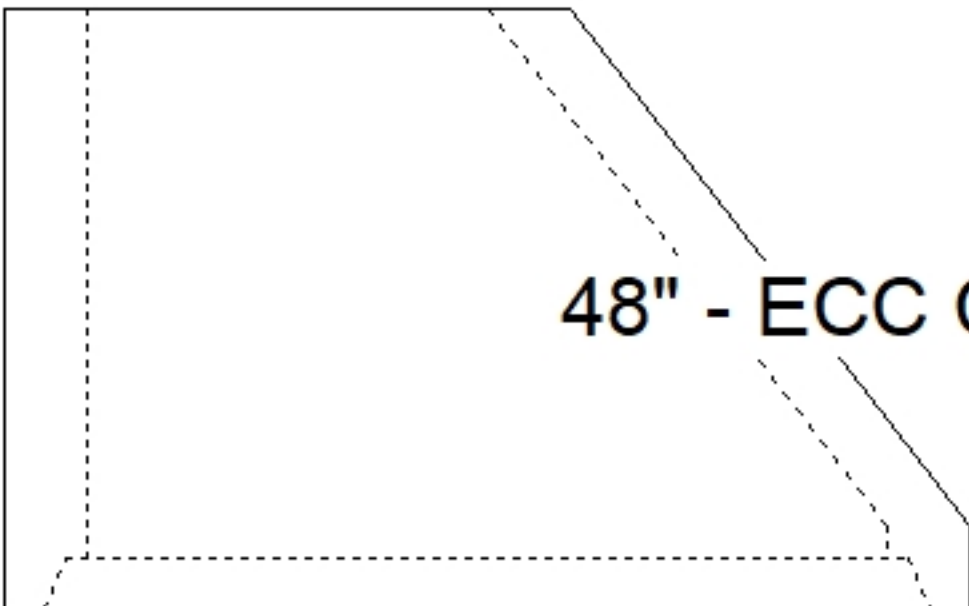


Job Name: 26-3528 Yale Drive Sanitary Sewer Improvements		Plant: Beaver Dam	Tech: S. Felletter	
Job Location: Elizabethtown, KY		9/29/2026 3:23:16 PM	PC: M. Sullivan	
Contractor: Schroeder Construction, Inc.				
Structure ID: MH18				
P2 MH048CN36		ECC CONE w/ 24" HOLE F/G		
P3) 24" - CASTING HEIGHT - 7" P2) 48" - ECC CONE w/ 24" HOLE F/G - 36" P1) 48" - MH BASE T/n - 30" 1) JOINT WRAP - 0.065"x6"x50' CONSEAL CS212 1) JOINT WRAP PRIMER - CONSEAL CS-75 (1 gal.) 1) 48" - MH INVERT CHANNEL - FULL HEIGHT 1) CASTING - HOE MC-375 F/C Sanitary 1) 48" - Conseal CS-102 1.00" (Double) 1) 24" - Conseal CS-102 1.00" (Double) 3) PSX - 12-08 NYLO 5) MH Step ML-10-TDS-NCR - 10"		0 lb 3000 lb 3282 lb 0 lb 0 lb 1440 lb 271 lb 0 lb 0 lb 24 lb 0 lb ----- Structure Total: 8017 lb	Structure Notes: . 1. PER ASTM C478 SPECIFICATIONS. 2. CONCRETE = 4,000 PSI AT 28 DAYS. 3. CASTING BY ICAST (HOE MC-375 F/C "SANITARY"). . REINFORCING PER ASTM A615 (GRADE 60). - CONE (As .12) - RISER/WALLS (As .12) - FLOOR (As .31) #5 BARS AT 12" C.C.E.W.	
				
 48" - ECC CONE w/ 24" HOLE F/G - 36" - (P2)				
Coating (Int): Coating (Ext):	Seam Up: Flat Seam Dn: Groove	Wall Thickness: 5"	Height (Ext): 36"	Weight (Net): 3000 lb Volume (Net): 0.5cu.yd
