

Job Name: 26-3528 Yale Drive Sanitary Sewer Improvements
Job Location: Elizabethtown, KY
Contractor: Schroeder Construction, Inc.

Plant: Beaver Dam
9/29/2026 3:23:55 PM

Tech: S. Felletter
PC: M. Sullivan



Structure ID: MH19

P2 MH048RS36S-D

MH RISER w/DROP T/G


- P6) 24" - CASTING HEIGHT - 7"
P5) 24" - GRADE RING F/F - 4"
P4) 48" - ECC CONE w/ 24" HOLE F/G - 42"
P3) 48" - MH RISER w/DROP T/G - 36"
P2) 48" - MH RISER w/DROP T/G - 36"
P1) 48" - MH BASE w/DROP T/n - 30"
1) JOINT WRAP - 0.065"x6"x50' CONSEAL CS212
1) JOINT WRAP PRIMER - CONSEAL CS-75 (1 gal.)
1) 48" - MH INVERT CHANNEL - FULL HEIGHT
1) CASTING - HOE MC-375 F/C Sanitary
3) 48" - Conseal CS-102 1.00" (Double)
2) 24" - Conseal CS-102 1.00" (Double)
2) PSX - 12-08 NYLO
1) Drop Tee - 8" PVC
1) Drop Elbow - 8" PVC
12) MH Step ML-10-TDS-NCR - 10"

- 0 lb
270 lb
3200 lb
4039 lb
4063 lb
3306 lb
0 lb
0 lb
1440 lb
271 lb
0 lb
0 lb
16 lb
0 lb
0 lb
0 lb
Structure Notes:
1. PER ASTM C478 SPECIFICATIONS.
2. CONCRETE = 4,000 PSI AT 28 DAYS.
3. CASTING BY ICAST (HOE MC-375 F/C "SANITARY").
4. EXTERNAL DROP @ 90 DEGREES.
REINFORCING PER ASTM A615 (GRADE 60).
- CONE (As .12)
- RISER/WALLS (As .12)
- FLOOR (As .31) #5 BARS AT 12" C.C.E.W.


Rim: 747.54' Rim to Invert: 12.77' Slack: 0.24' Sump: 2' Step Position: 180°
Structure Total: 16605 lb

Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up (_)	Offset
Invert 1										
Invert 2										
Invert 3										
Invert 4										
Invert 5										
Invert 6										
Invert 7										
Invert 8										

RIGHT-SIDE UP VIEW (int. dimensions)

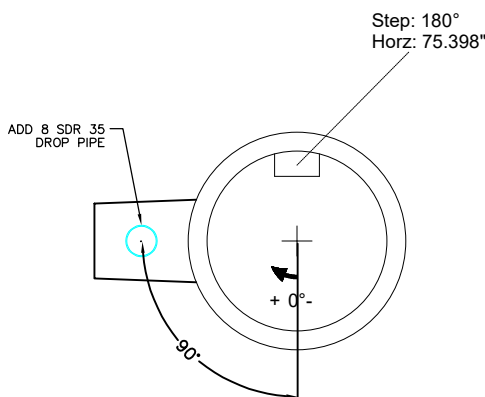

INSIDE WALL DIMENSIONS

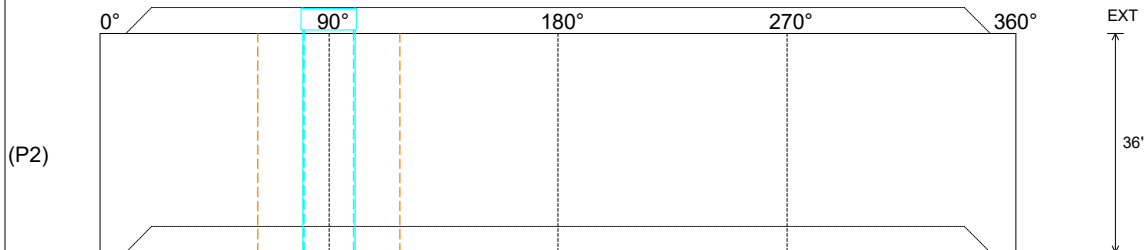

Coating (Int):	Seam Up: Tongue	Wall Thickness: 5"	Height (Int): 36"	Weight (Net): 4063 lb
Coating (Ext):	Seam Dn: Groove	Floor Height: 0"	Height (Ext): 36"	Volume (Net): 1.04cu.yd
