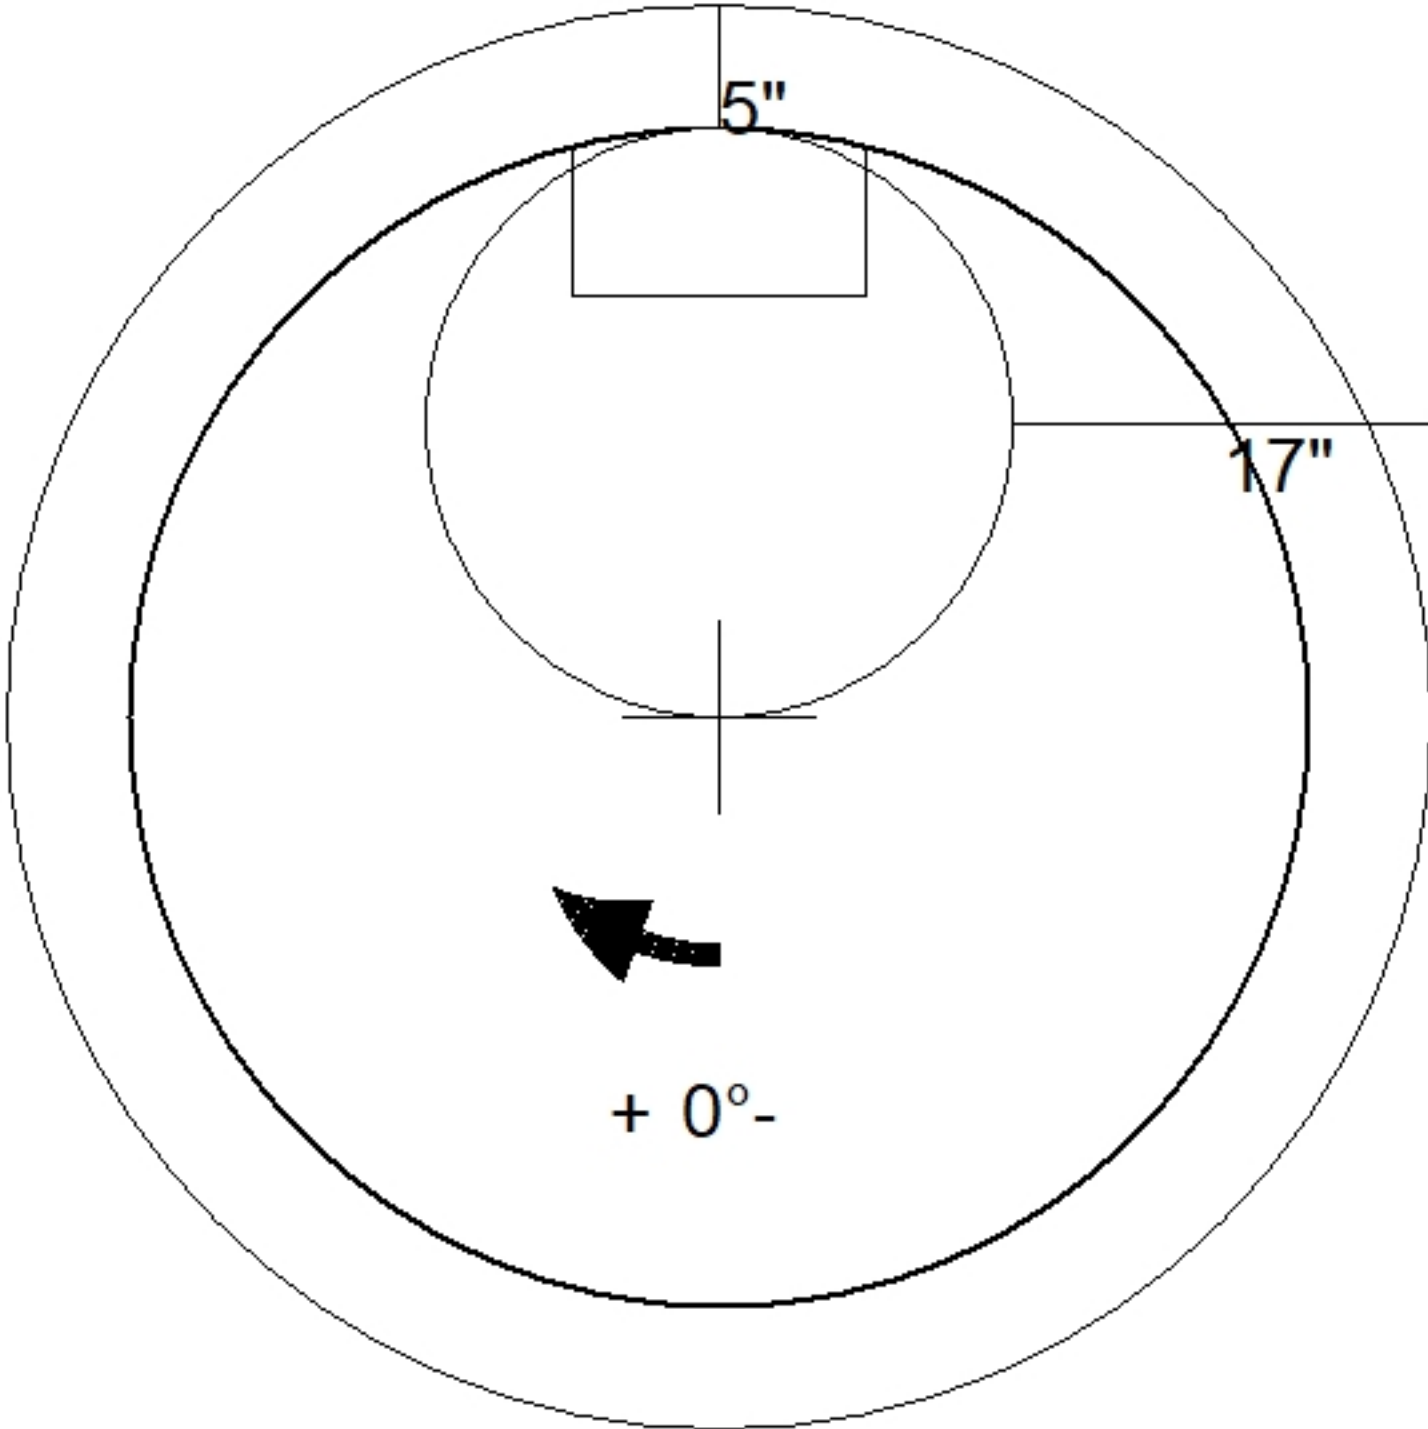
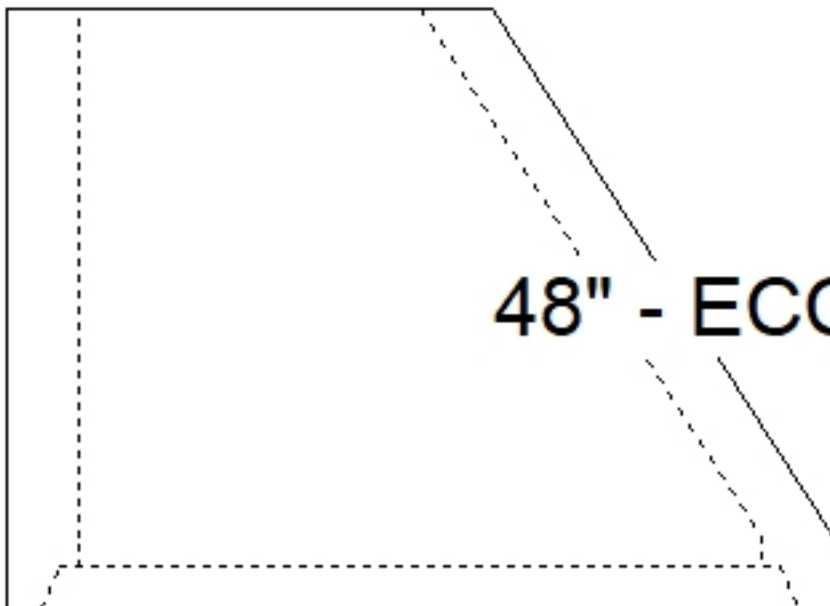


Job Name: 26-3528 Yale Drive Sanitary Sewer Improvements		Plant: Beaver Dam	Tech: S. Felletter	
Job Location: Elizabethtown, KY		9/29/2026 3:23:17 PM	PC: M. Sullivan	
Contractor: Schroeder Construction, Inc.				
Structure ID: MH19				
P4 MH048CN42		ECC CONE w/ 24" HOLE F/G		
P6) 24" - CASTING HEIGHT - 7" P5) 24" - GRADE RING F/F - 4" P4) 48" - ECC CONE w/ 24" HOLE F/G - 42" P3) 48" - MH RISER w/DROP T/G - 36" P2) 48" - MH RISER w/DROP T/G - 36" P1) 48" - MH BASE w/DROP T/n - 30" 1) JOINT WRAP - 0.065"x6"x50' CONSEAL CS212 1) JOINT WRAP PRIMER - CONSEAL CS-75 (1 gal.) 1) 48" - MH INVERT CHANNEL - FULL HEIGHT 1) CASTING - HOE MC-375 F/C Sanitary 3) 48" - Conseal CS-102 1.00" (Double) 2) 24" - Conseal CS-102 1.00" (Double) 2) PSX - 12-08 NYLO 1) Drop Tee - 8" PVC 1) Drop Elbow - 8" PVC 12) MH Step ML-10-TDS-NCR - 10"		0 lb 270 lb 3200 lb 4039 lb 4063 lb 3306 lb 0 lb 0 lb 1440 lb 271 lb 0 lb 0 lb 16 lb 0 lb 0 lb 0 lb ----- 16605 lb	Structure Notes: . 1. PER ASTM C478 SPECIFICATIONS. 2. CONCRETE = 4,000 PSI AT 28 DAYS. 3. CASTING BY ICAST (HOE MC-375 F/C "SANITARY"). 4. EXTERNAL DROP @ 90 DEGREES. . REINFORCING PER ASTM A615 (GRADE 60). - CONE (As .12) - RISER/WALLS (As .12) - FLOOR (As .31) #5 BARS AT 12" C.C.E.W. . RFI: VERIFY ALL INVERT ELEVATIONS	
				
 48" - ECC CONE w/ 24" HOLE F/G - 42" - (P4)				
Coating (Int): Coating (Ext):	Seam Up: Flat Seam Dn: Groove	Wall Thickness: 5"	Height (Ext): 42"	Weight (Net): 3200 lb Volume (Net): 0.5cu.yd
