

Contractor: Lutgring Bros, Inc.

TECH: Jared - F

Plant: 100



Spec: Storm
Type: STM.MH
Size: 48"

Rim: 585'
Invert: 585'
Rim to Invert: 0'

Sump: 108"
Floor (Top): 576'
Floor Height: 6"

Floor (Bot): 575.5'
Overall Height: 9.5'
Slack: 0"

1. PER ASTM C478 SPECIFICATIONS.
2. CONCRETE = 4,000 PSI AT 28 DAYS.
3. NO STEPS AND NO INVERT CHANNEL.
4. CASTING BY ICAST (HOE 525 LV SET (F/G/H)).
5. PIPE OPENINGS TO BE CORED IN THE FIELD BY OTHERS.


REINFORCING PER ASTM A615 (GRADE 60).
 - TOP SLAB (As .62) #5 BARS AT 6" C.C.E.W.
 - RISER/WALLS (As .12)
 - FLOOR (As .12) #5 BARS AT 12" C.C.E.W.

P4) 24" x 36" - CASTING HEIGHT - 6"
P3) 48" - MH FLAT TOP w/24"x36" Hole - 12"
P2) 48" - MH RISER - 54"
P1) 48" - MH BASE - 36"


- 1) CASTING - HOE 525 LV SET (F/G/H)
- 1) SNOUT - BMP SNOUT 12R w/ KIT
- 2) 48" - Conseal CS-102 1.00"
- 1) 24" x 36" - Conseal CS-102 1.00"

0 lb
1300 lb
3772 lb
3845 lb
442 lb
25 lb
0 lb
0 lb


Structure Total: 9384 lb

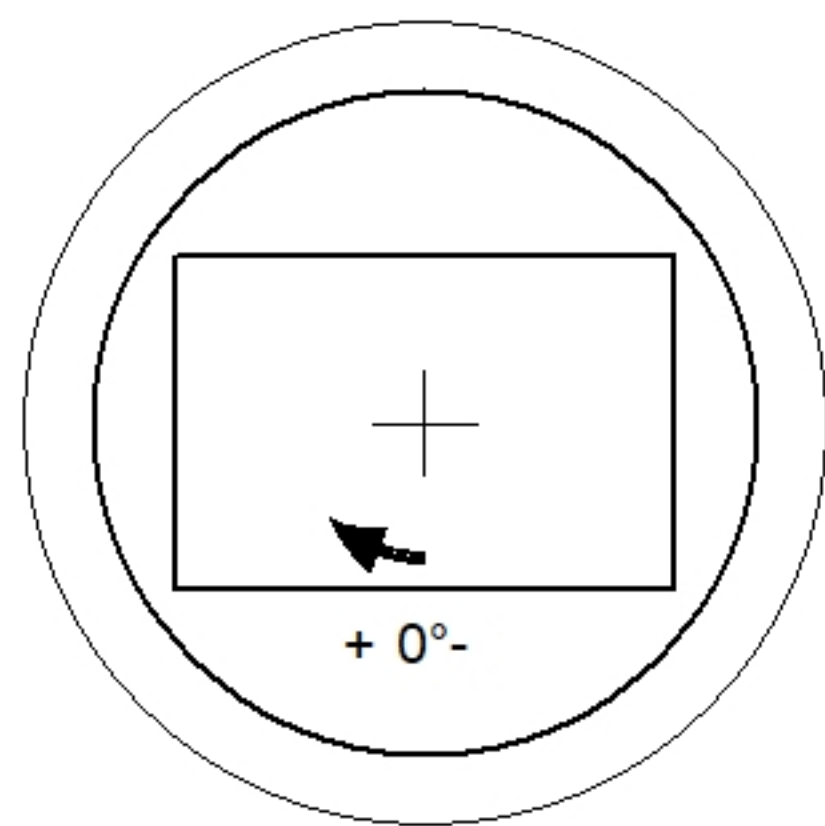

Position	Elev	Angle	Pipe	Pipe OD	Hole	Connector	Up ()	Ref
Rim	585'							
Reducer								
Invert 1								
Invert 2								
Invert 3								
Invert 4								
Invert 5								
Invert 6								
Invert 7								
Invert 8								

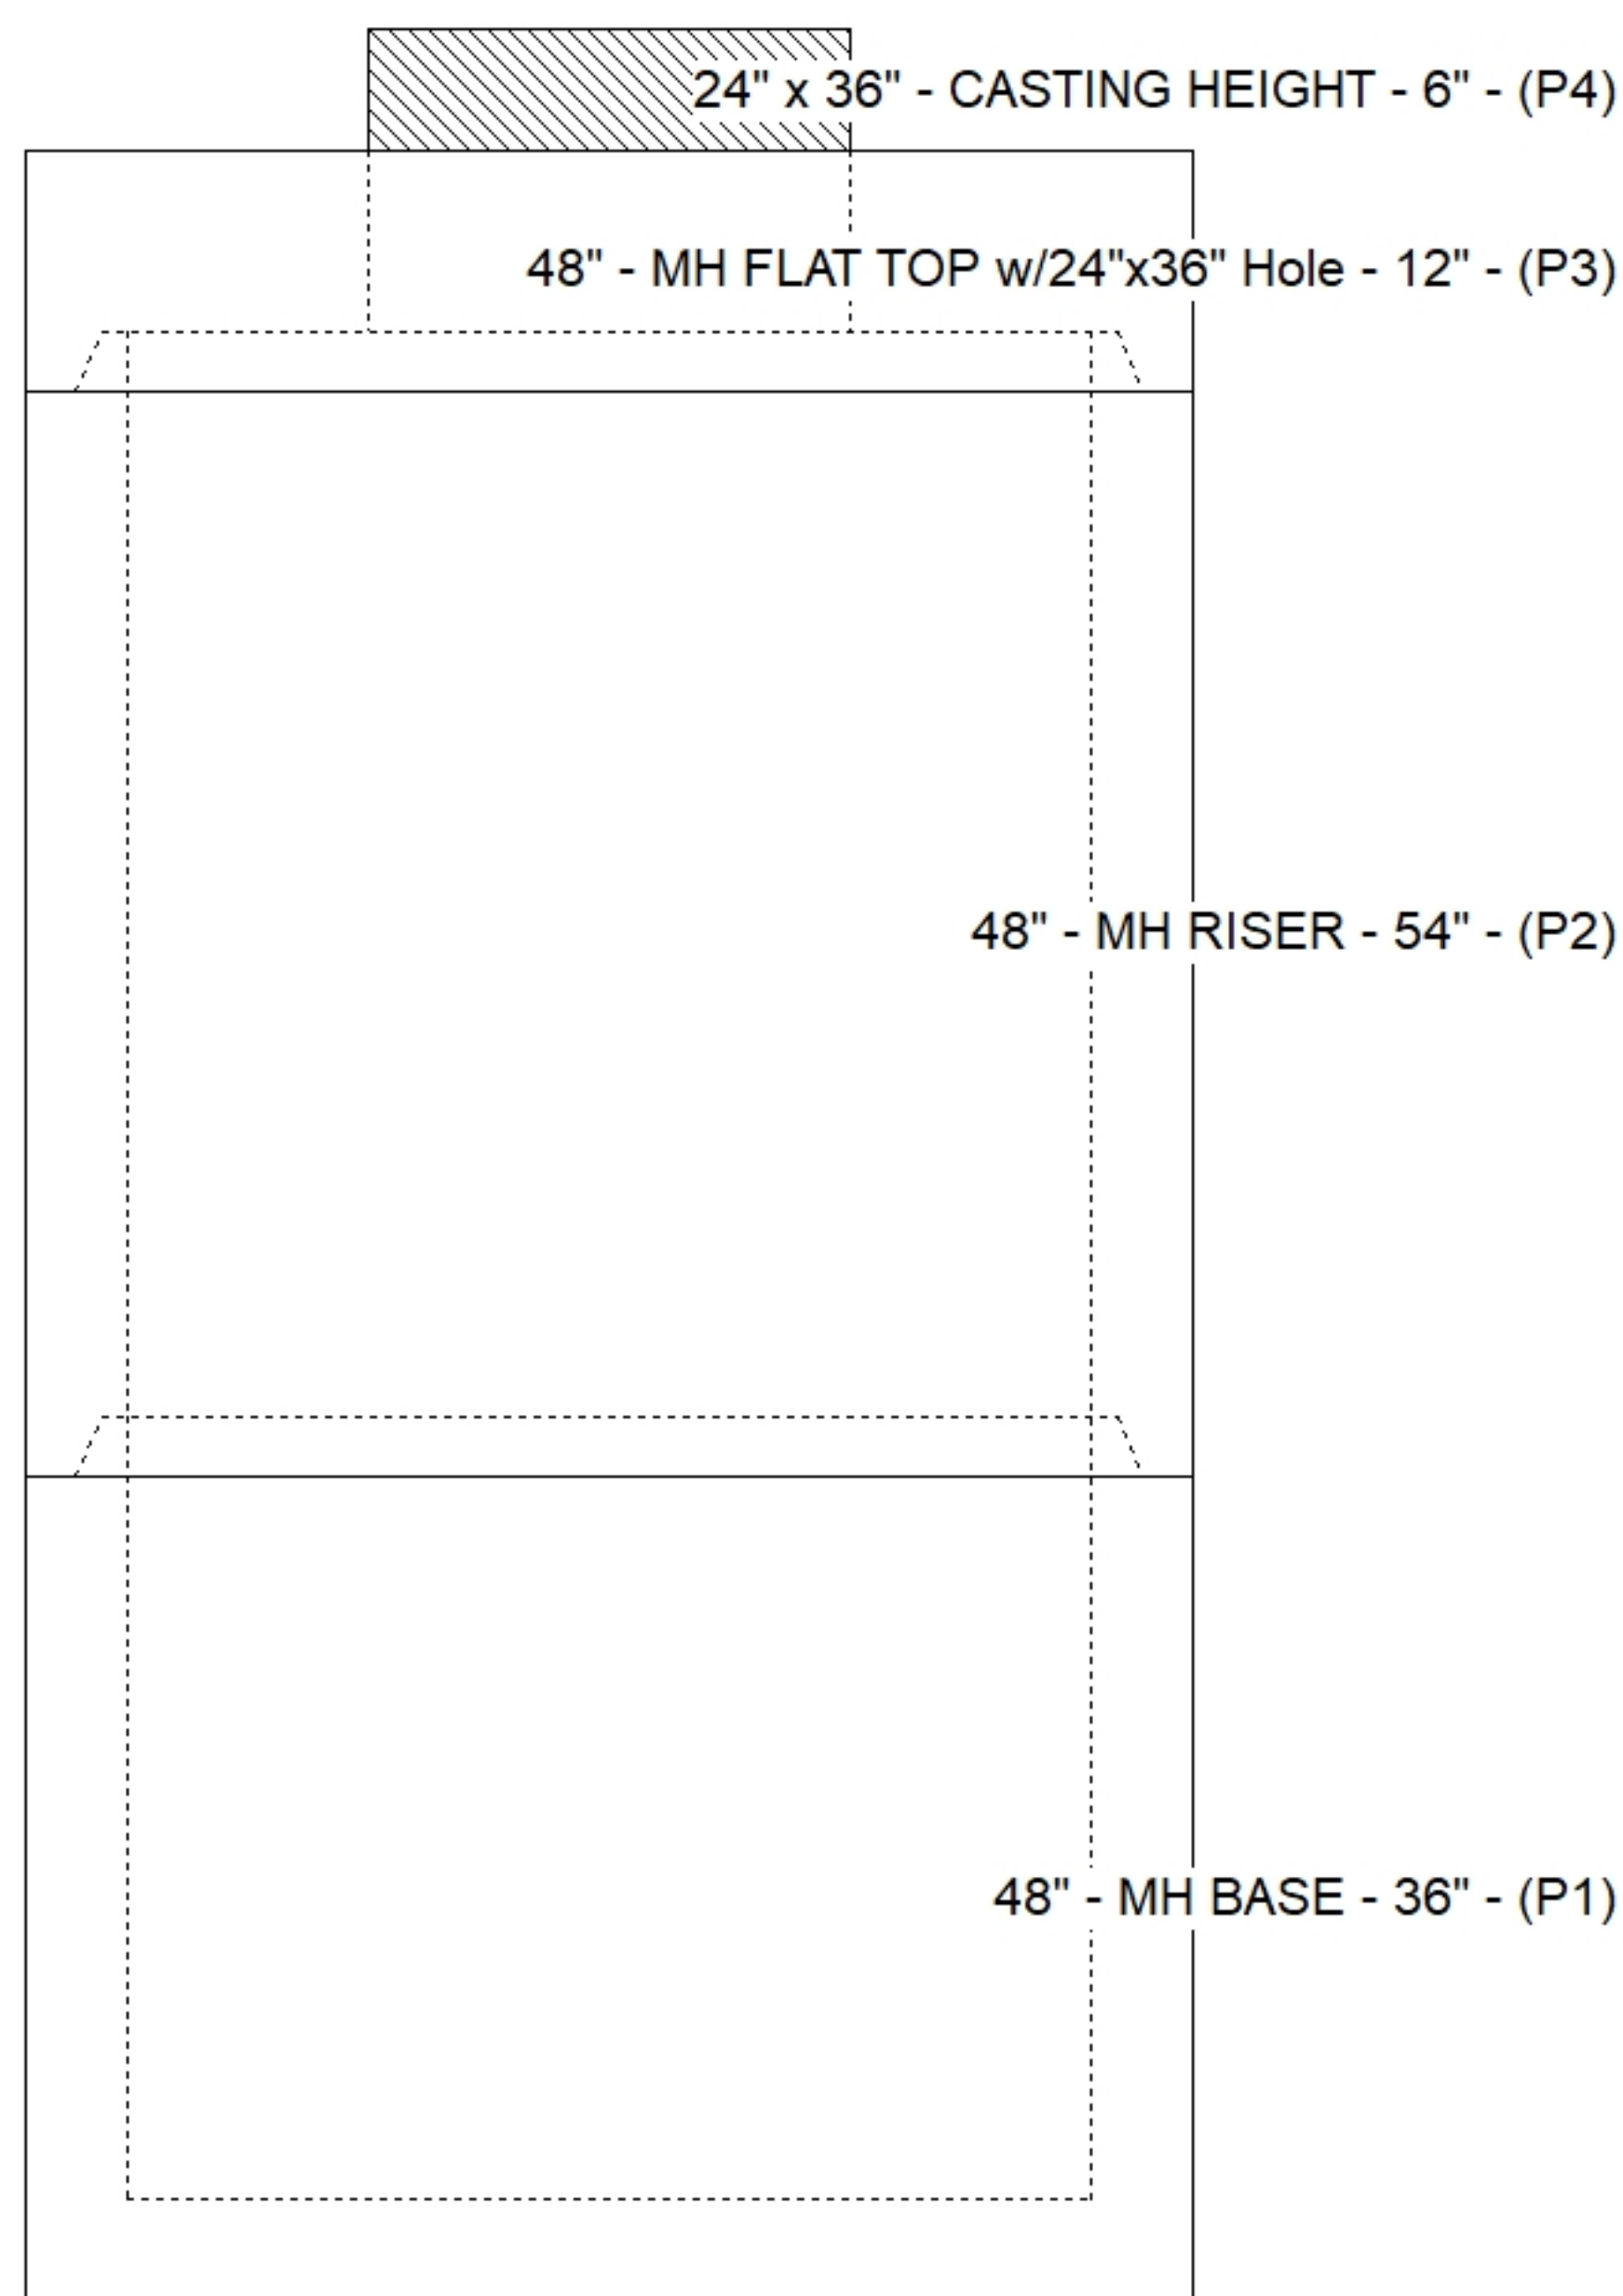

Default - Interior Dimensions

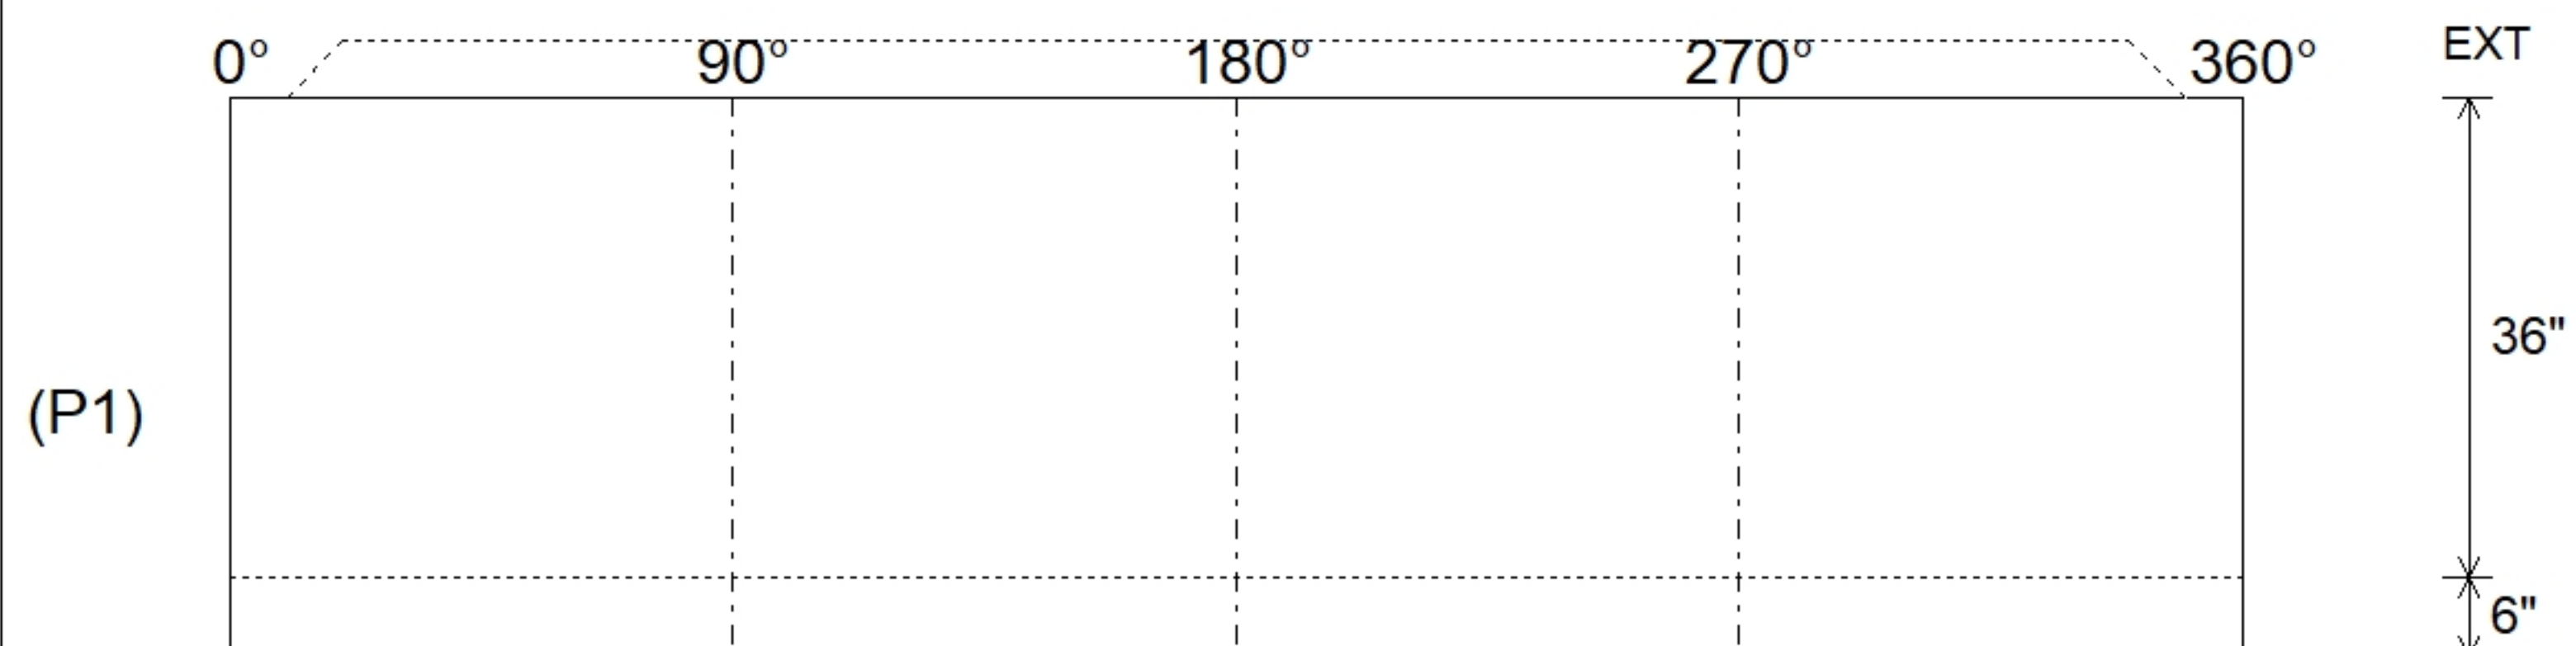

Submittal Drawing
10/1/2026 2:34:11 PM

SUBMITTAL
APPROVED BY:
