

Contractor: Lutgring Bros, Inc.

TECH: Jared - F

Plant: 100



Spec: Storm
Type: STM.MH
Size: 48"

Rim: 584.79'
Invert: 584.79'
Rim to Invert: 0'

Sump: 54"
Floor (Top): 580.29'
Floor Height: 6"

Floor (Bot): 579.79'
Overall Height: 5'
Slack: 0"

1. PER ASTM C478 SPECIFICATIONS.
2. CONCRETE = 4,000 PSI AT 28 DAYS.
3. NO STEPS AND NO INVERT CHANNEL.
4. CASTING BY ICAST (HOE 525 LV SET(F/G/H)).
5. PIPE OPENINGS TO BE CORED IN THE FIELD BY OTHERS.

REINFORCING PER ASTM A615 (GRADE 60).


- TOP SLAB (As .62) #5 BARS AT 6" C.C.E.W..
- RISER/WALLS (As .12)
- FLOOR (As .31) #5 BARS AT 12" C.C.E.W.

P3) 24" x 36" - CASTING HEIGHT - 6"
P2) 48" - MH FLAT TOP w/24"x36" Hole - 12"
P1) 48" - MH BASE - 36"


1) CASTING - HOE 525 LV SET (F/G/H)
1) 48" - Conseal CS-102 1.00"
1) 24" x 36" - Conseal CS-102 1.00"
3) MH Step ML-10-TDS-NCR - 10"

0 lb
1300 lb
3845 lb
442 lb
0 lb
0 lb
0 lb


Structure Total: 5587 lb

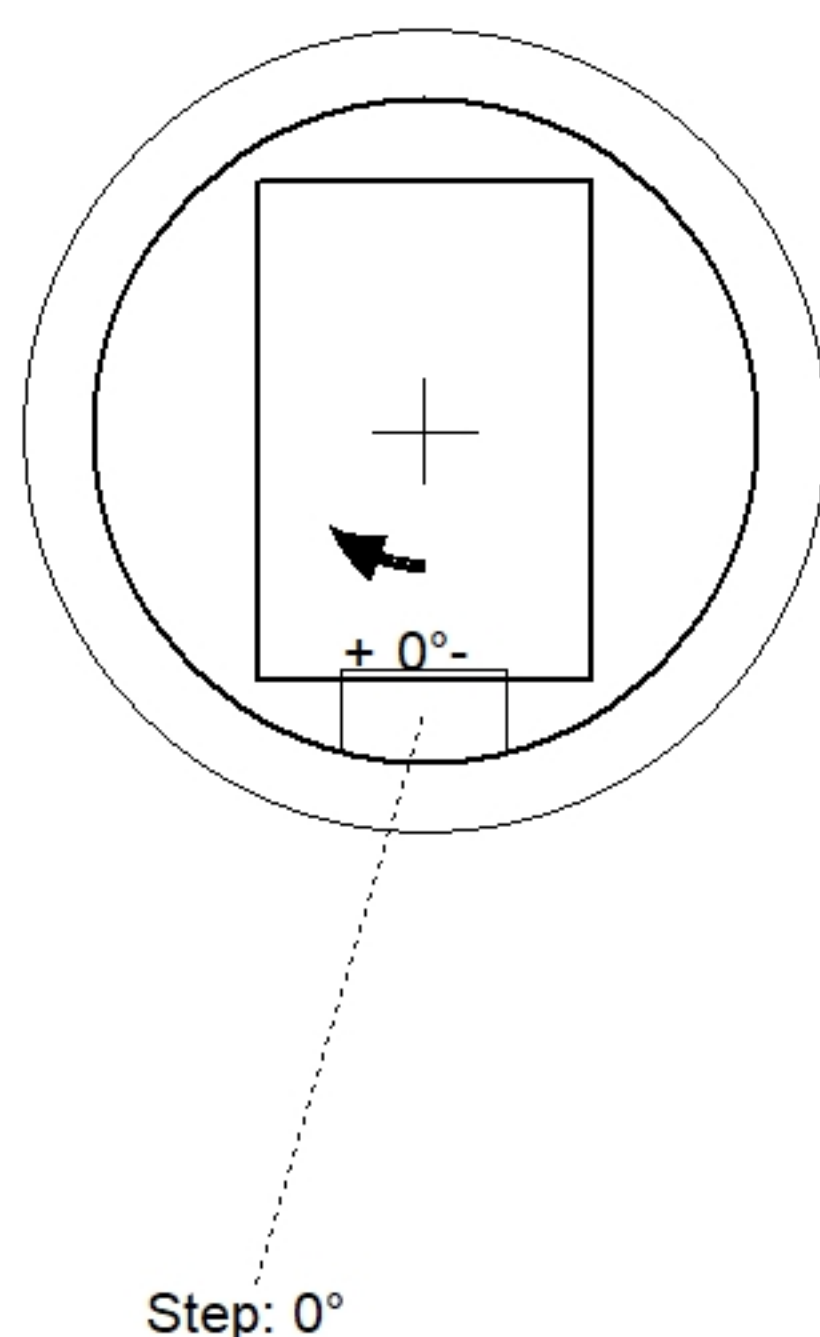

Position	Elev	Angle	Pipe	Pipe OD	Hole	Connector	Up ()	Ref
Rim	584.79'							
Reducer								
Invert 1								
Invert 2								
Invert 3								
Invert 4								
Invert 5								
Invert 6								
Invert 7								
Invert 8								

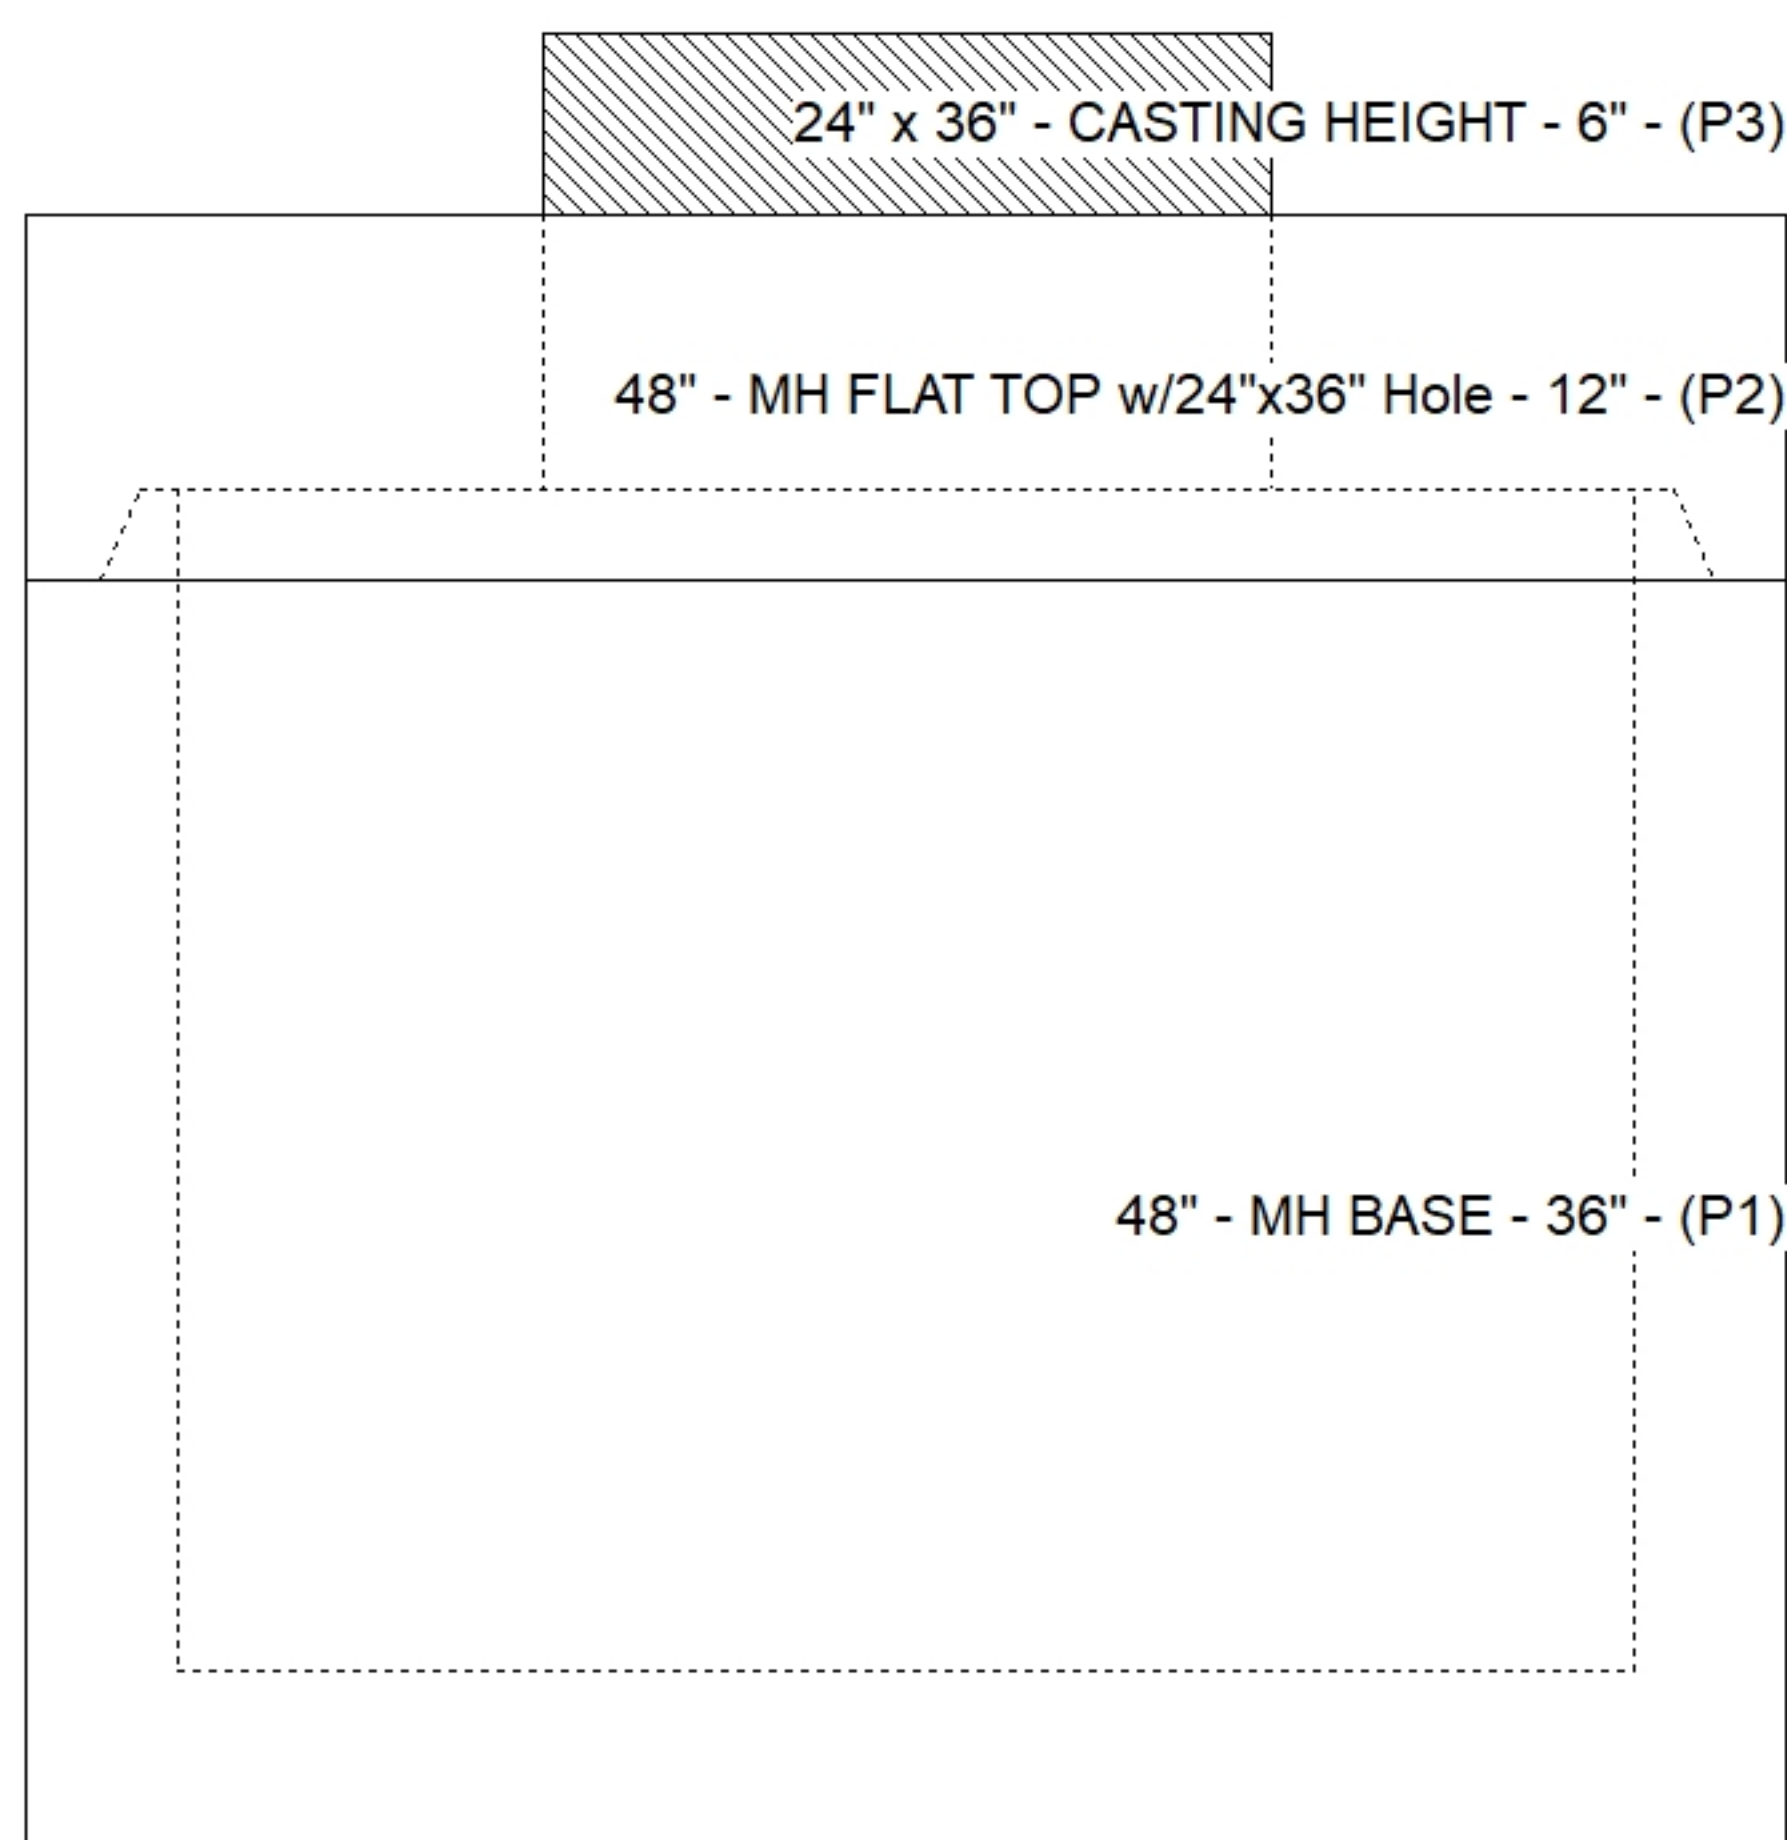

Default - Interior Dimensions

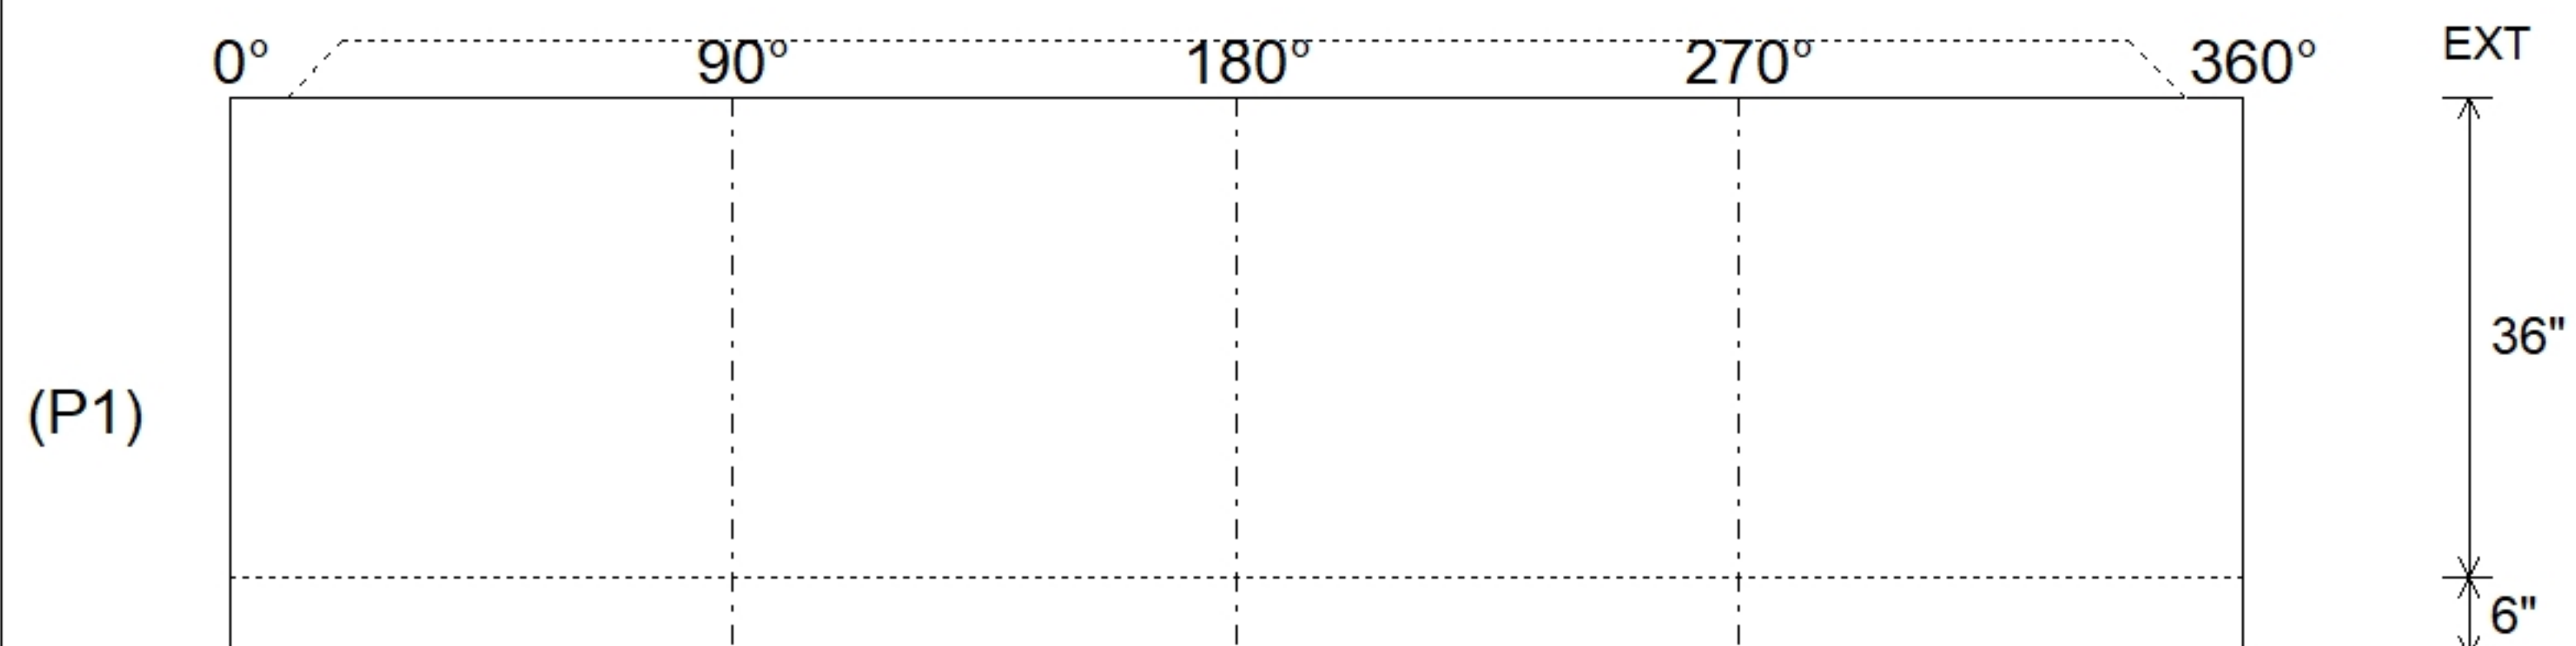

Submittal Drawing
10/1/2026 2:34:11 PM

SUBMITTAL
APPROVED BY:
