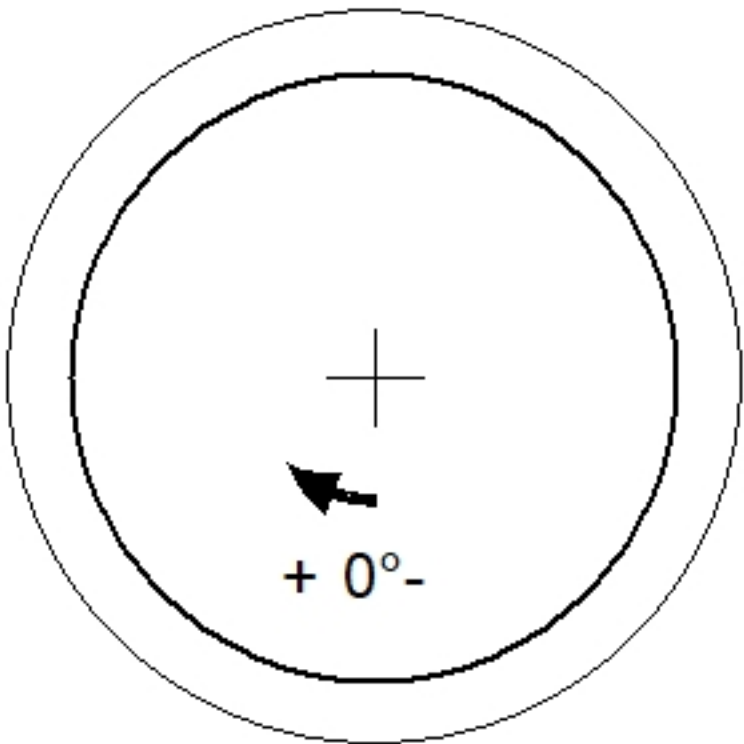
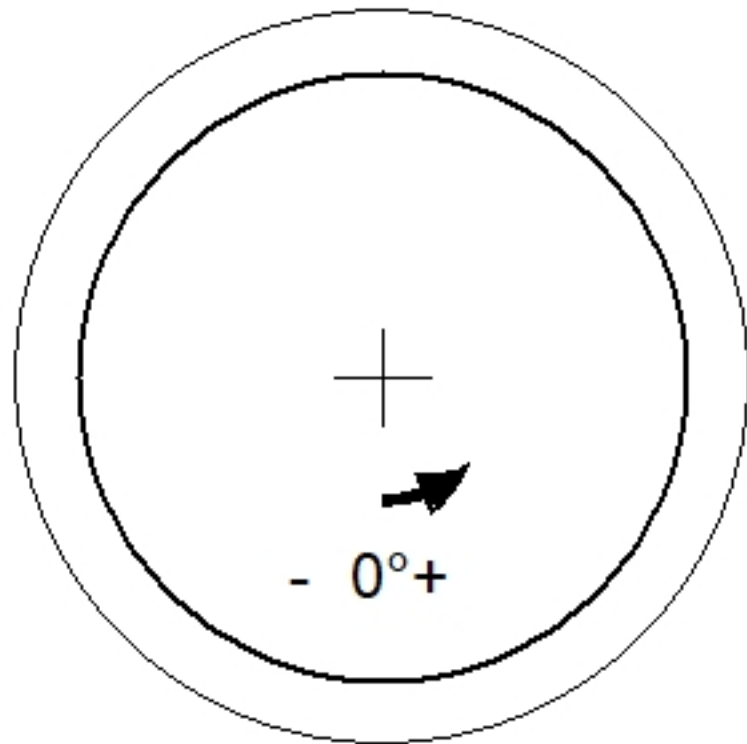
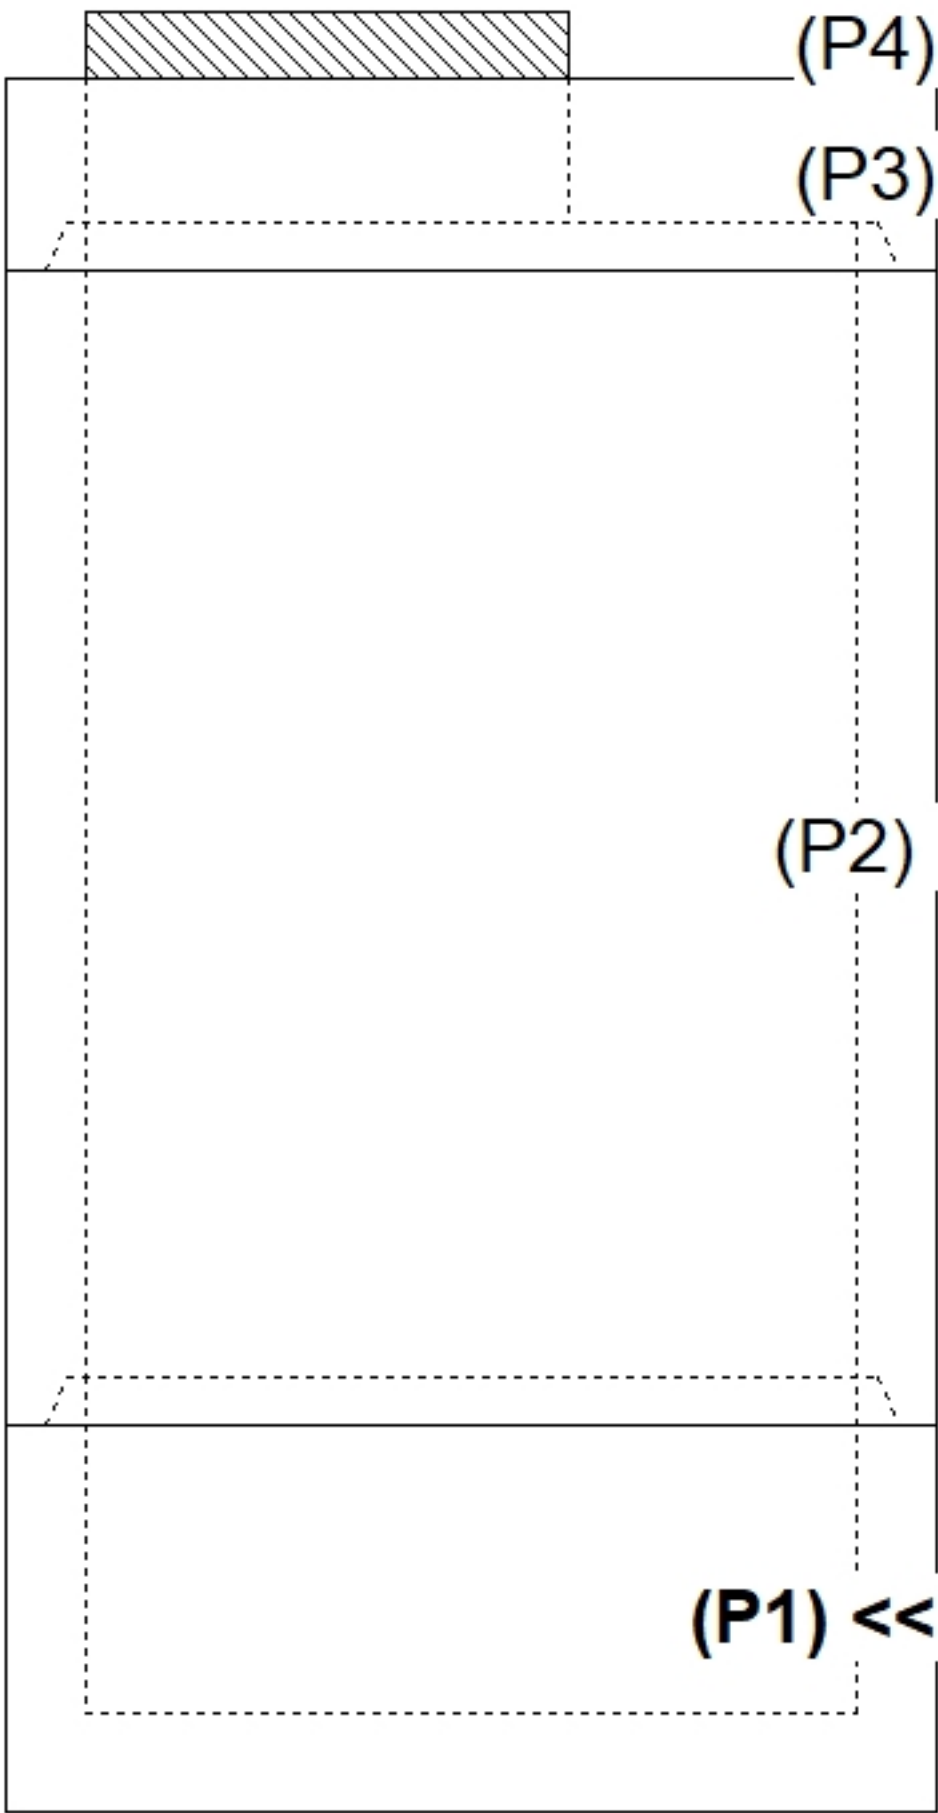
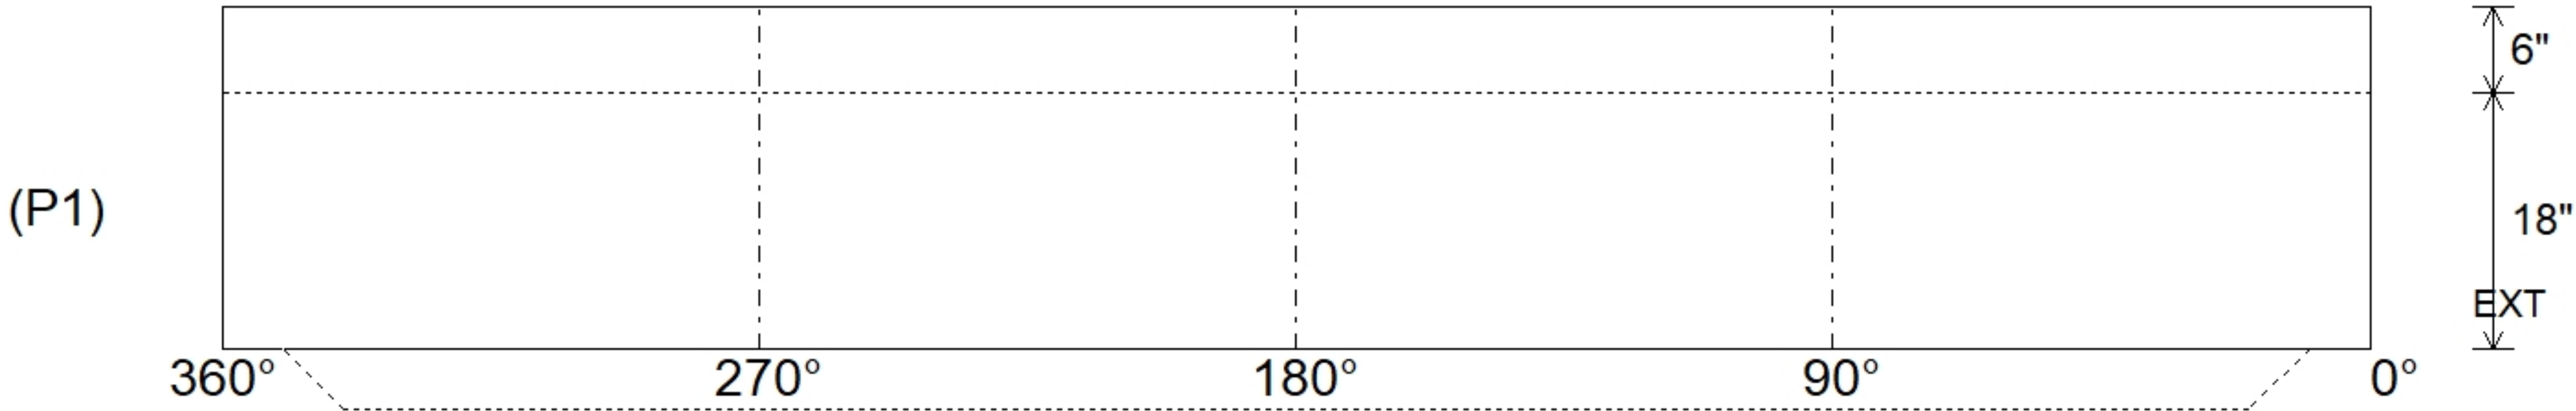


Job Name: 26-3575 902045 Old Jamestown Sidewalk PH III					Plant: Beaver Dam		Tech: S. Felletter				
Job Location: Florissant, MO					9/28/2026 1:23:25 PM		PC: C. Goff				
Contractor: Contech Engineering Solutions											
Structure ID: 10-CS-4											
P1		MH048BA18			MH BASE T/n						
P4) 30" - CASTING HEIGHT - 4" P3) 48" - MH FLAT LID w/30in ECC Hole F/G - 12" P2) 48" - MH RISER SPECIAL T/G - 72" P1) 48" - MH BASE T/n - 18" 1) ASSEMBLY REQUIRED 1) CVSTENCILING 2) 48" - Conseal CS-102 1.00" 2) Z-Lok - C107-8					0 lb 1413 lb 4899 lb 2588 lb 0 lb 0 lb 0 lb 2 lb Structure Total: 8902 lb		Structure Notes: 4" CASTING BY OTHERS LIFTING ANCHORS TO BE INSTALLED ON THE OUTSIDE OF THE STRUCTURE ICAST TO INSTALL THE INTERNALS CONTECH'S LOGO AS WELL AS THE INLET AND OUTLET MUST BE STENCILED ONTO THE STRUCTURE				
Rim: 500.04'					Rim to Invert: 5.14'		Slack: 6.68"		Sump: 51"		Step Position:
Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up (⌋)	Offset	
Invert 1											
Invert 2											
Invert 3											
Invert 4											
Invert 5											
Invert 6											
Invert 7											
Invert 8											
RIGHT-SIDE UP VIEW (int. dimensions) 					UPSIDE-DOWN VIEW (int. dimenions) 						
					INSIDE WALL DIMENSIONS 						
Coating (Int):			Seam Up: Tongue		Wall Thickness: 5"		Height (Int): 18"		Weight (Net): 2588 lb		
Coating (Ext):			Seam Dn: n/a		Floor Height: 6"		Height (Ext): 24"		Volume (Net): 0.66cu.yd		
