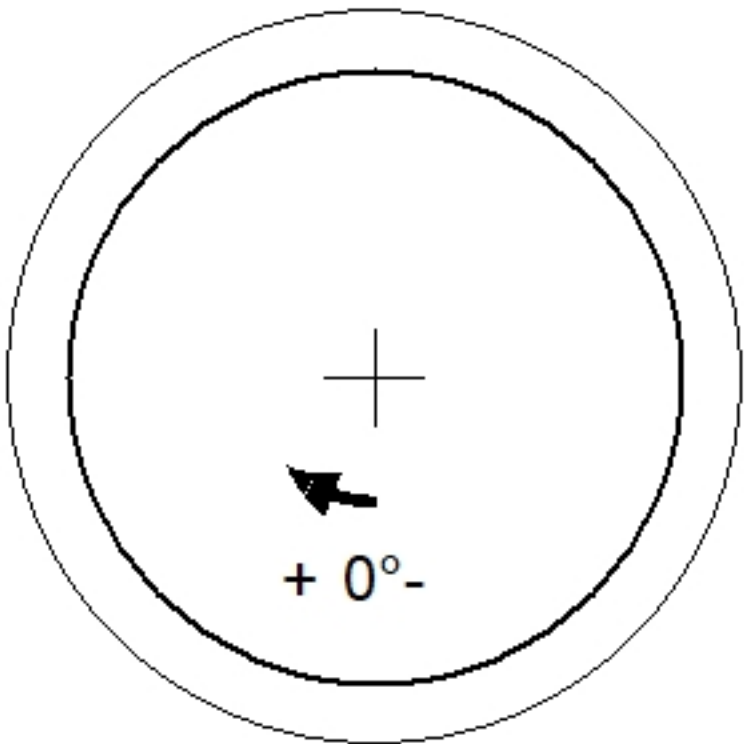
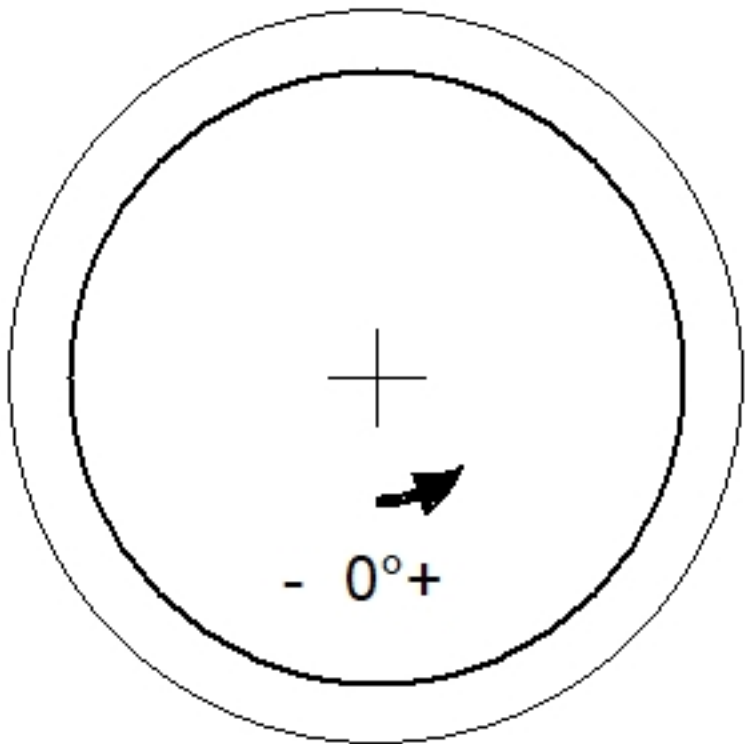
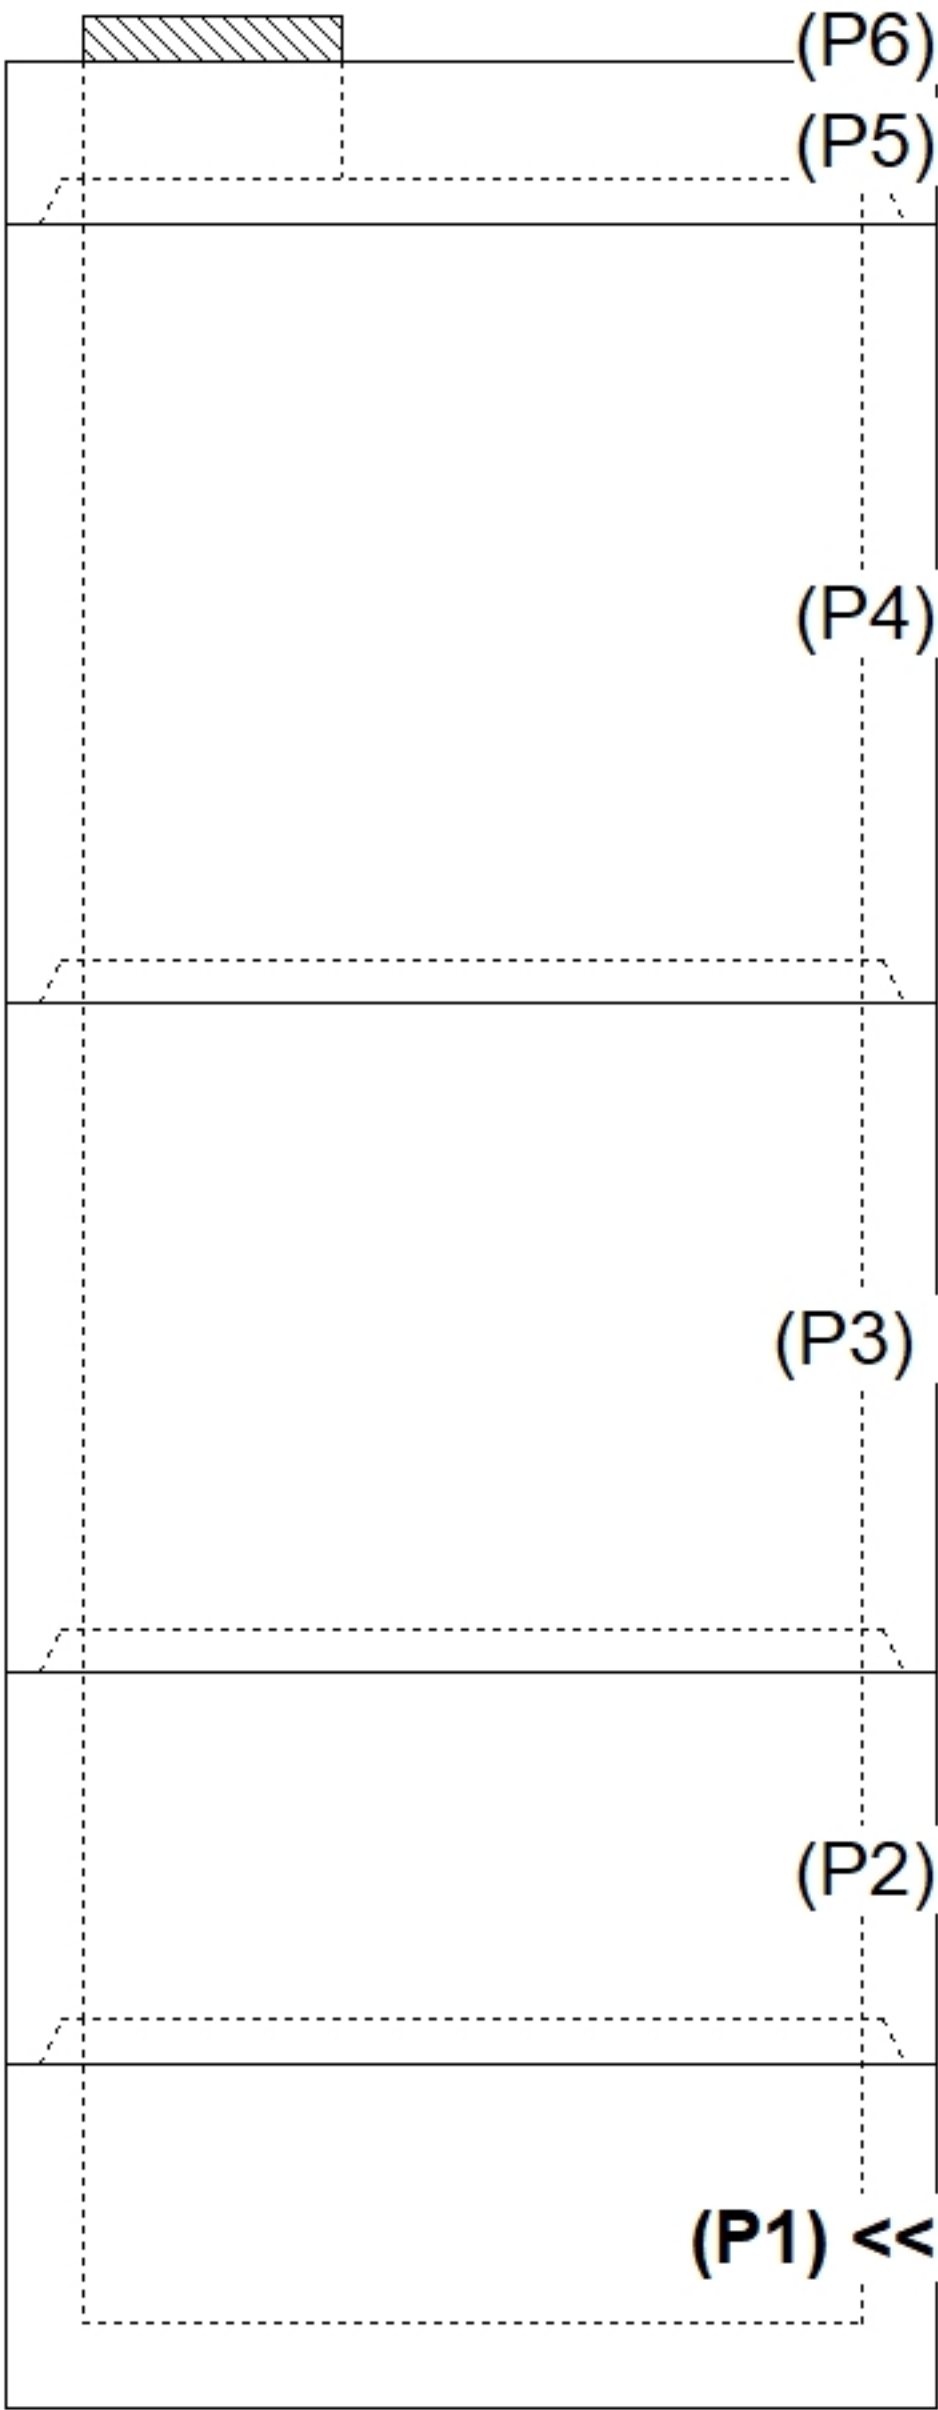
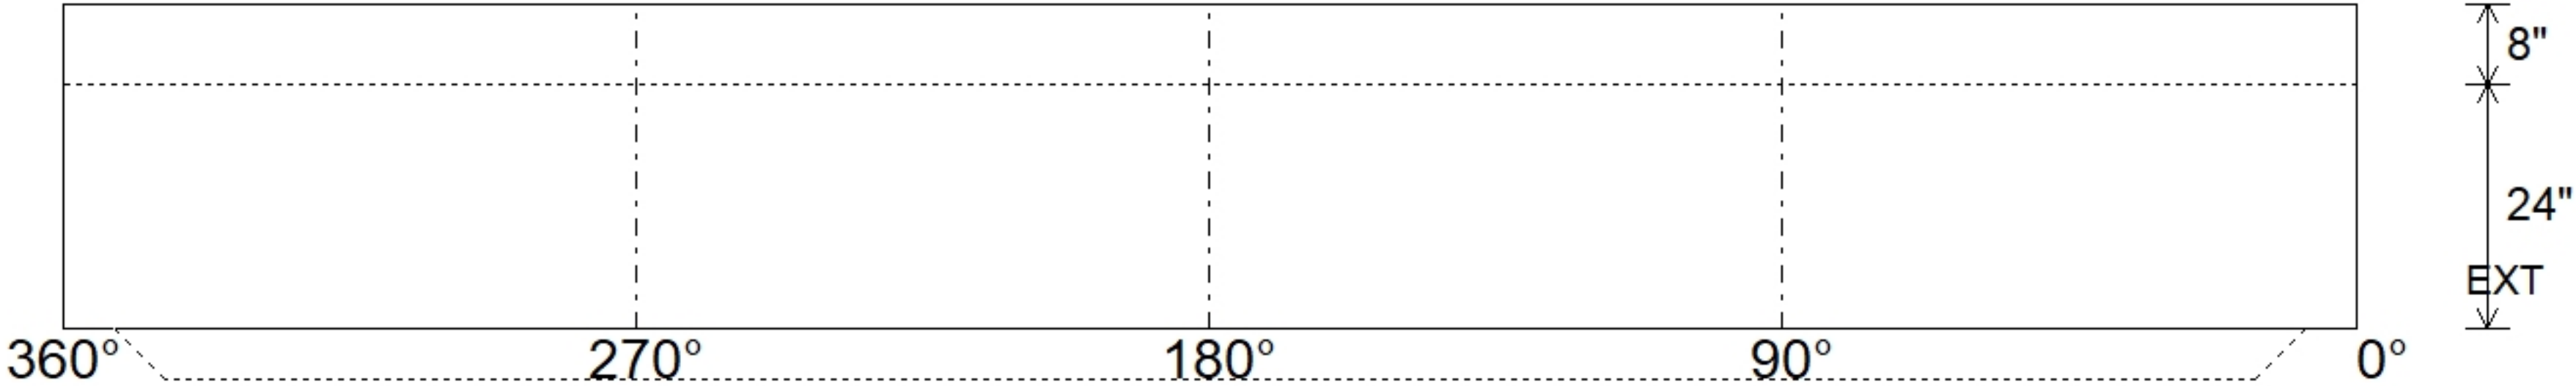


Job Name: 26-3623 905242 Dobbs Tire KCMO Job Location: Blue Springs, MO Contractor: Contech Engineering Solutions					Plant: Beaver Dam 9/9/2026 1:56:28 PM		Tech: S. Felletter PC: C. Goff						
Structure ID: 10-CDS3030-6-C													
P1 MH072BA24			MH BASE T/n										
P6) 24" - CASTING HEIGHT - 4" P5) 72" - MH FLAT TOP SPEC. (24" & 2x 12" HOLES) F/G - 15" P4) 72" - MH RISER SPECIAL T/G - 72" P3) 72" - MH RISER Custom Ht T/G - 62" P2) 72" - MH RISER SPECIAL T/G - 36" P1) 72" - MH BASE T/n - 24" 1) ASSEMBLY REQUIRED 1) CVSTENCILING 1) SECONDARY POUR - RISER SEPARATION SLAB 4) 72" - Conseal CS-102 1.00" 1) 24" - Conseal CS-102 1.00" 2) Hole - 24						0 lb 6742 lb 10496 lb 8498 lb 5248 lb 7398 lb 0 lb 0 lb 0 lb 3751 lb 0 lb 0 lb 0 lb ----- 42134 lb		Structure Notes: . 4" CASTING BY OTHERS . LIFTING ANCHORS TO BE INSTALLED ON THE OUTSIDE OF THE STRUCTURE . ICAST TO INSTALL THE INTERNALS . CONTECH'S LOGO AS WELL AS THE INLET AND OUTLET MUST BE STENCILED ONTO THE STRUCTURE . P2 & P3 RISERS TO BE MECHANICALLY ATTACHED PRIOR TO INSTALLATION OF INTERNALS					
Rim: 978'		Rim to Invert: 10.9'		Slack: 1.236"		Sump: 83.436"		Step Position: 0°					
Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up ()	Offset			
Invert 1													
Invert 2													
Invert 3													
Invert 4													
Invert 5													
Invert 6													
Invert 7													
Invert 8													
RIGHT-SIDE UP VIEW (int. dimensions)  UPSIDE-DOWN VIEW (int. dimenions) 													
 INSIDE WALL DIMENSIONS 													
Coating (Int): Coating (Ext):			Seam Up: Tongue Seam Dn: n/a		Wall Thickness: 7" Floor Height: 8"		Height (Int): 24" Height (Ext): 32"		Weight (Net): 7398 lb Volume (Net): 1.89cu.yd				
