

Job Name: 26-3703 Honeysuckle Way Sewer Ext
Job Location: Springfield, KY
Contractor: Hale Contracting

Plant: Beaver Dam
10/7/2026 4:02:14 PM

Tech: S. Felletter
PC: M. Sullivan



Structure ID: A10

P1 MH048BAEVF

MH BASE w/FLANGE T/n

- P3) 24" - CASTING HEIGHT - 7"
P2) 48" - ECC CONE w/ 24" HOLE F/G - 42"
P1) 48" - MH BASE w/FLANGE T/n - 36"
1) JOINT WRAP - 0.065"x6"x50' CONSEAL CS212
1) JOINT WRAP PRIMER - CONSEAL CS-75 (1 gal.)
1) 48" - MH INVERT CHANNEL - FULL HEIGHT
1) 48" - Conseal CS-102 1.00" (Double)
1) 24" - Conseal CS-102 1.00" (Double)
3) PSX - 12-08 NYLO
6) MH Step ML-10-TDS-NCR - 10"

0 lb
3200 lb
5258 lb
0 lb
0 lb
1440 lb
0 lb
0 lb
0 lb
24 lb
0 lb

Structure Total: 9922 lb

Structure Notes: 1. PER ASTM C478 SPECIFICATIONS.
2. CONCRETE = 4,000 PSI AT 28 DAYS.
3. CASTING PROVIDED BY OTHERS.



REINFORCING PER ASTM A615 (GRADE 60).
- CONE (As .12)
- RISER/WALLS (As .12)
- FLOOR (As .31) #5 BARS AT 12" C.C.E.W.

Rim: 788.49' Rim to Invert: 7.11' Slack: 2.32' Sump: 2" Step Position: 0°


Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up ()	Offset
Invert 1	781.38'	0°	0"	8" PVC SDR35	8.5"	PSX 12-08 NYLO	12"	12.129"	0"	0"
Invert 2	781.48'	212°	107.303"	8" PVC SDR35	8.5"	PSX 12-08 NYLO	12"	12.129"	1.2"	0"
Invert 3	781.48'	252°	127.549"	8" PVC SDR35	8.5"	PSX 12-08 NYLO	12"	12.129"	1.2"	0"
Invert 4										
Invert 5										
Invert 6										
Invert 7										
Invert 8										

RIGHT-SIDE UP VIEW (int. dimensions)

UPSIDE-DOWN VIEW (int. dimensions)

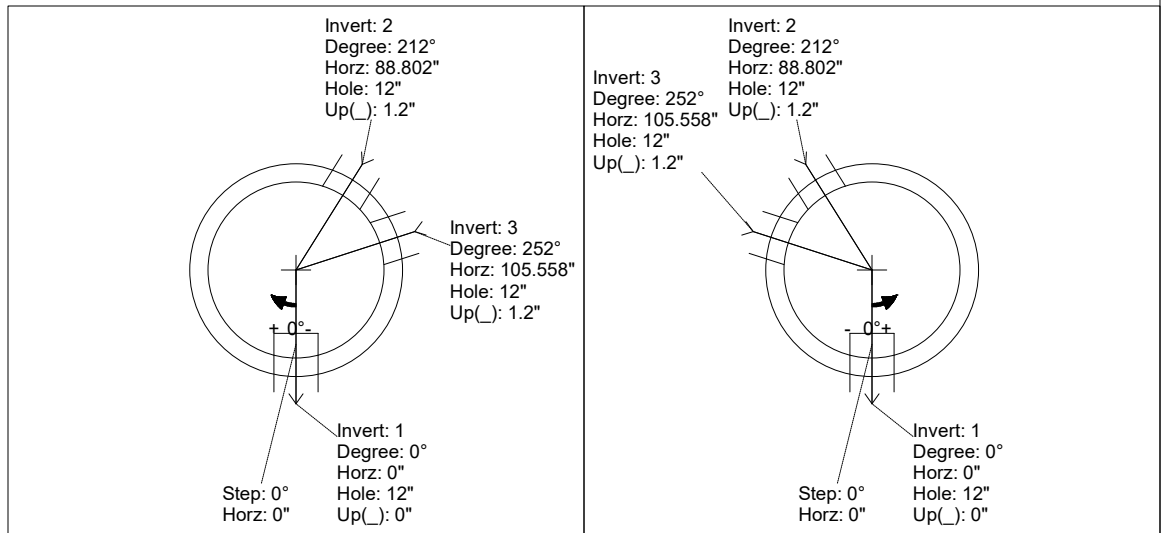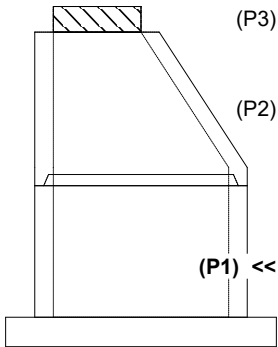

INSIDE WALL DIMENSIONS

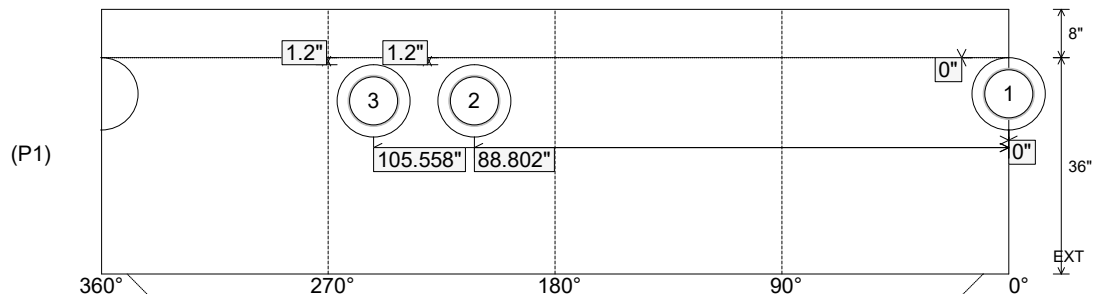

Coating (Int):
Coating (Ext):


Seam Up: Tongue
Seam Dn: n/a

Wall Thickness: 5"
Floor Height: 8"

Height (Int): 36"
Height (Ext): 44"


Weight (Net): 5258 lb
Volume (Net): 1.34cu.yd

Job Name: 26-3703 Honeysuckle Way Sewer Ext Job Location: Springfield, KY Contractor: Hale Contracting					Plant: Beaver Dam 10/7/2026 4:02:14 PM		Tech: S. Felletter PC: M. Sullivan				
Structure ID: A10											
P1 MH048BAEVF		MH BASE w/FLANGE T/n									
P3) 24" - CASTING HEIGHT - 7" P2) 48" - ECC CONE w/ 24" HOLE F/G - 42" P1) 48" - MH BASE w/FLANGE T/n - 36" 1) JOINT WRAP - 0.065"x6"x50' CONSEAL CS212 1) JOINT WRAP PRIMER - CONSEAL CS-75 (1 gal.) 1) 48" - MH INVERT CHANNEL - FULL HEIGHT 1) 48" - Conseal CS-102 1.00" (Double) 1) 24" - Conseal CS-102 1.00" (Double) 3) PSX - 12-08 NYLO 6) MH Step ML-10-TDS-NCR - 10"					0 lb 3200 lb 5258 lb 0 lb 0 lb 1440 lb 0 lb 0 lb 0 lb 24 lb 0 lb ----- Structure Total: 9922 lb		Structure Notes: 1. PER ASTM C478 SPECIFICATIONS. 2. CONCRETE = 4,000 PSI AT 28 DAYS. 3. CASTING PROVIDED BY OTHERS. REINFORCING PER ASTM A615 (GRADE 60). - CONE (As .12) - RISER/WALLS (As .12) - FLOOR (As .31) #5 BARS AT 12" C.C.E.W.				
Rim: 788.49' Rim to Invert: 7.11' Slack: 2.32' Sump: 2' Step Position: 0°					Invert channel drawing Full height invert						
Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up ()	Offset	
Invert 1	781.38'	0°	0"	8" PVC SDR35	8.5"	PSX 12-08 NYLO	12"	12.129"	0"	0"	
Invert 2	781.48'	212°	107.303"	8" PVC SDR35	8.5"	PSX 12-08 NYLO	12"	12.129"	1.2"	0"	
Invert 3	781.48'	252°	127.549"	8" PVC SDR35	8.5"	PSX 12-08 NYLO	12"	12.129"	1.2"	0"	
Invert 4											
Invert 5											
Invert 6											
Invert 7											
Invert 8											

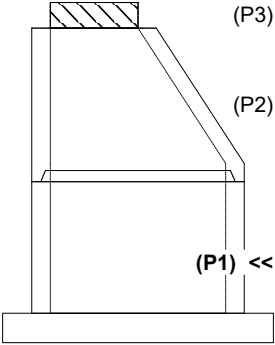


(P3)
(P2)
(P1) <<


RIGHT-SIDE UP VIEW (int. dimensions)

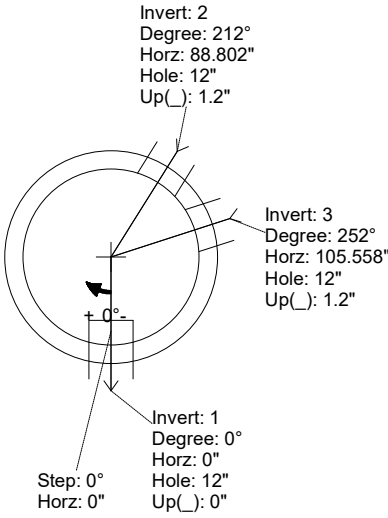

UPSIDE-DOWN VIEW (int. dimensions)

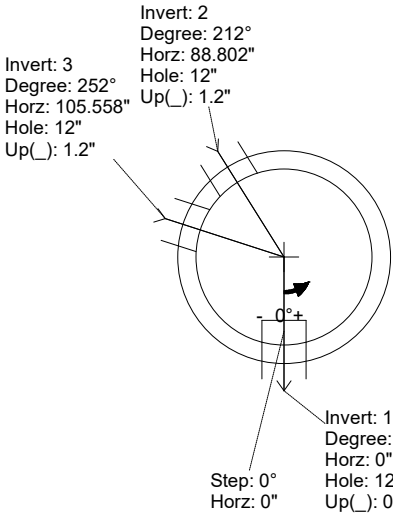

INSIDE WALL DIMENSIONS

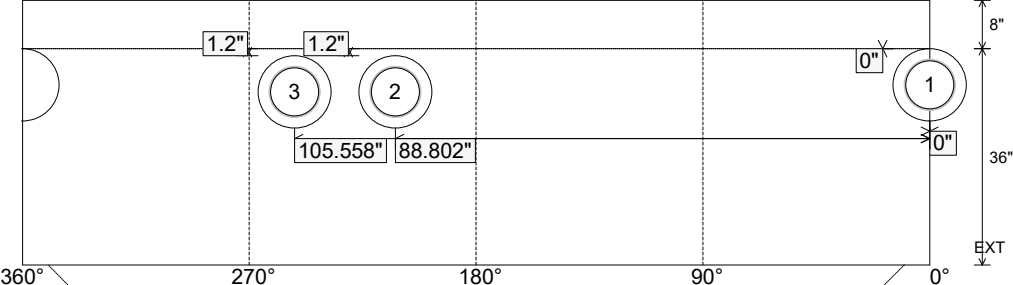

Coating (Int): Coating (Ext):	Seam Up: Tongue Seam Dn: n/a	Wall Thickness: 5" Floor Height: 8"	Height (Int): 36" Height (Ext): 44"	Weight (Net): 5258 lb Volume (Net): 1.34cu.yd
----------------------------------	---------------------------------	--	--	--
