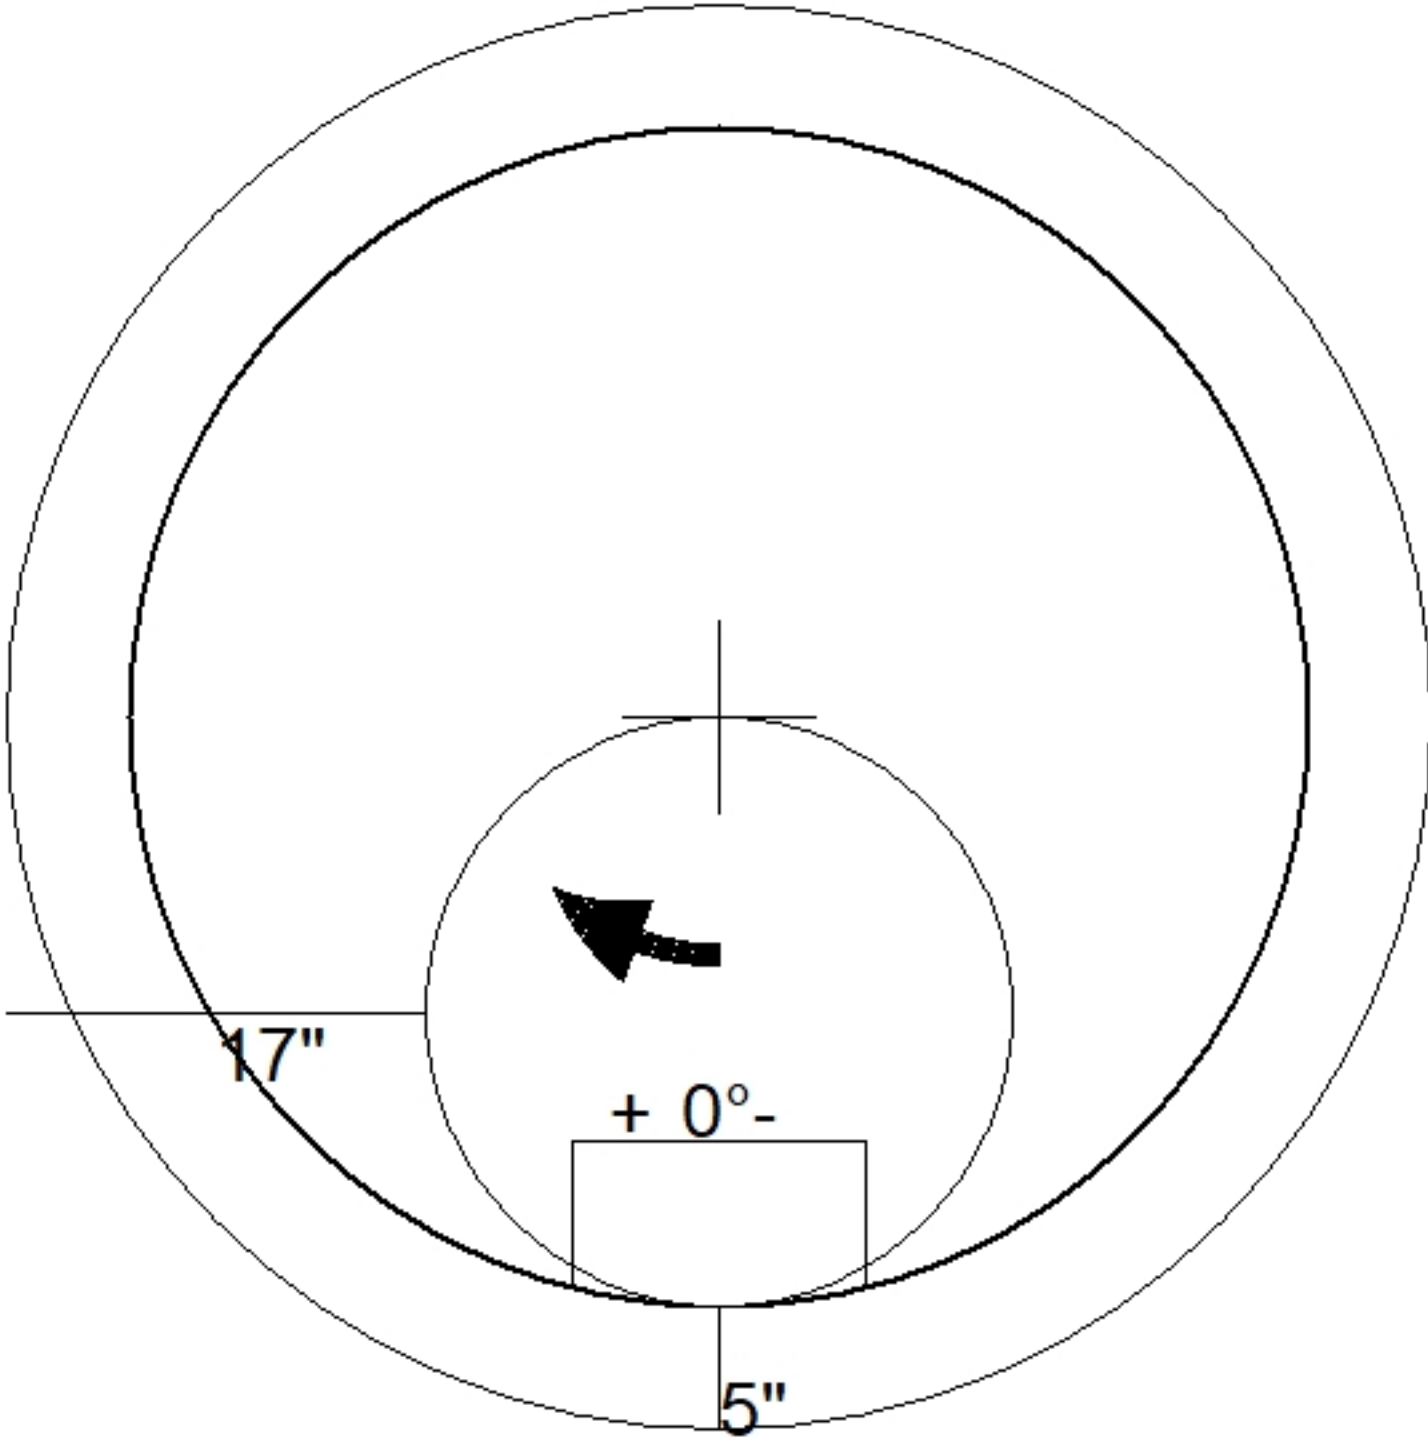
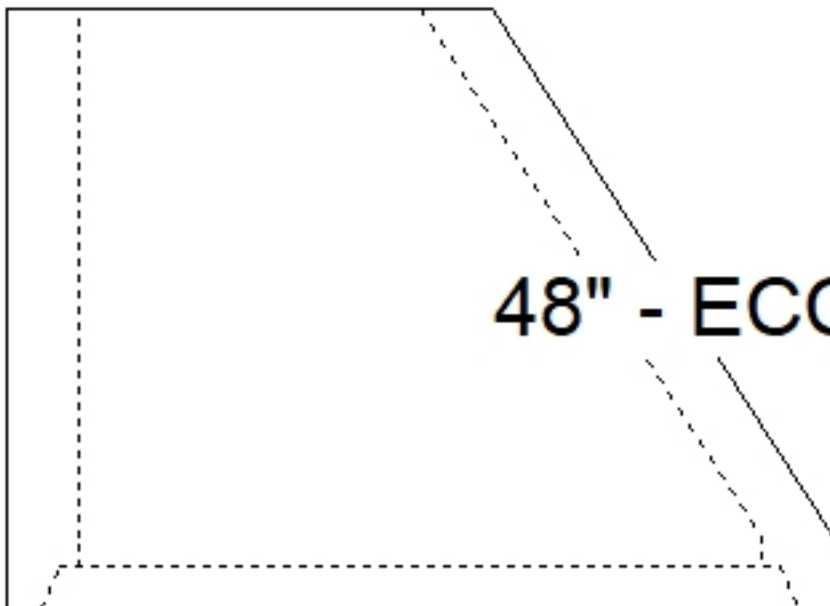


Job Name: 26-3703 Honeysuckle Way Sewer Ext Job Location: Springfield, KY Contractor: Hale Contracting		Plant: Beaver Dam 10/7/2026 4:03:56 PM	Tech: S. Felletter PC: M. Sullivan		
Structure ID: A10					
P2 MH048CN42		ECC CONE w/ 24" HOLE F/G			
P3) 24" - CASTING HEIGHT - 7" P2) 48" - ECC CONE w/ 24" HOLE F/G - 42" P1) 48" - MH BASE w/FLANGE T/n - 36" 1) JOINT WRAP - 0.065"x6"x50' CONSEAL CS212 1) JOINT WRAP PRIMER - CONSEAL CS-75 (1 gal.) 1) 48" - MH INVERT CHANNEL - FULL HEIGHT 1) 48" - Conseal CS-102 1.00" (Double) 1) 24" - Conseal CS-102 1.00" (Double) 3) PSX - 12-08 NYLO 6) MH Step ML-10-TDS-NCR - 10"		0 lb 3200 lb 5258 lb 0 lb 0 lb 1440 lb 0 lb 0 lb 0 lb 24 lb 0 lb ----- 9922 lb Structure Total:	Structure Notes: 1. PER ASTM C478 SPECIFICATIONS. 2. CONCRETE = 4,000 PSI AT 28 DAYS. 3. CASTING PROVIDED BY OTHERS. . REINFORCING PER ASTM A615 (GRADE 60). - CONE (As .12) - RISER/WALLS (As .12) - FLOOR (As .31) #5 BARS AT 12" C.C.E.W. . RFI: VERIFY IF DROP MH IS REQUIRED AND 8" INLET STUB PIPE ANGLE		
					
 48" - ECC CONE w/ 24" HOLE F/G - 42" - (P2)					
Coating (Int): Coating (Ext):		Seam Up: Flat Seam Dn: Groove	Wall Thickness: 5"	Height (Ext): 42"	Weight (Net): 3200 lb Volume (Net): 0.5cu.yd
