


Job Name: 26-3703 Honeysuckle Way Sewer Ext Job Location: Springfield, KY Contractor: Hale Contracting					Plant: Beaver Dam 10/7/2026 4:02:14 PM		Tech: S. Felletter PC: M. Sullivan				
Structure ID: A9											
P1		MH048BAEVF									
MH BASE w/FLANGE T/n											
P5) 24" - CASTING HEIGHT - 7" P4) 24" - GRADE RING F/F - 3" P3) 48" - ECC CONE w/ 24" HOLE F/G - 30" P2) 48" - MH RISER T/G - 36" P1) 48" - MH BASE w/FLANGE T/n - 24" 1) JOINT WRAP - 0.065"x6"x50' CONSEAL CS212 1) JOINT WRAP PRIMER - CONSEAL CS-75 (1 gal.) 1) 48" - MH INVERT CHANNEL - FULL HEIGHT 2) 48" - Conseal CS-102 1.00" (Double) 2) 24" - Conseal CS-102 1.00" (Double) 2) PSX - 12-08 NYLO 7) MH Step ML-10-TDS-NCR - 10"						0 lb 202 lb 2050 lb 2515 lb 4468 lb 0 lb 0 lb 1440 lb 0 lb 0 lb 16 lb 0 lb Structure Total: 10691 lb		Structure Notes: 1. PER ASTM C478 SPECIFICATIONS. 2. CONCRETE = 4,000 PSI AT 28 DAYS. 3. CASTING PROVIDED BY OTHERS. REINFORCING PER ASTM A615 (GRADE 60). - CONE (As .12) - RISER/WALLS (As .12) - FLOOR (As .31) #5 BARS AT 12" C.C.E.W.			
Rim: 787' Rim to Invert: 8.16' Slack: -0.08" Sump: 2" Step Position: 0°											
Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up ()	Offset	
Invert 1	778.84'	0°	0"	8" PVC SDR35	8.5"	PSX 12-08 NYLO	12"	12.129"	0"	0"	
Invert 2	778.94'	138°	69.848"	8" PVC SDR35	8.5"	PSX 12-08 NYLO	12"	12.129"	1.2"	0"	
Invert 3											
Invert 4											
Invert 5											
Invert 6											
Invert 7											
Invert 8											

RIGHT-SIDE UP VIEW (int. dimensions)

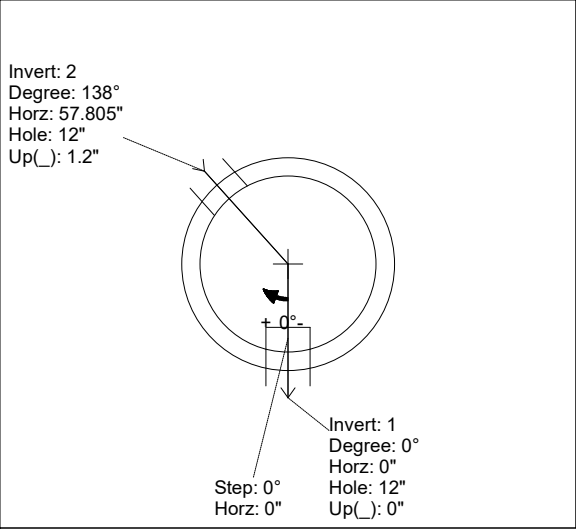


Invert: 2
Degree: 138°
Horz: 57.805"
Hole: 12"
Up(): 1.2"

Invert: 1
Degree: 0°
Horz: 0"
Hole: 12"
Up(): 0"

Step: 0°
Horz: 0"
Hole: 12"
Up(): 0"


UPSIDE-DOWN VIEW (int. dimensions)

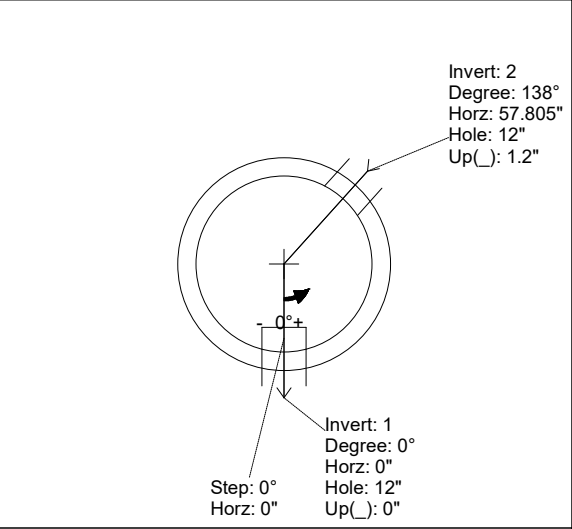

Invert: 2
Degree: 138°
Horz: 57.805"
Hole: 12"
Up(): 1.2"


Invert: 1
Degree: 0°
Horz: 0"
Hole: 12"
Up(): 0"

Step: 0°
Horz: 0"
Hole: 12"
Up(): 0"

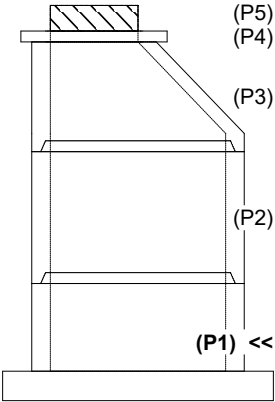

(P5)
(P4)
(P3)
(P2)
(P1) <<

INSIDE WALL DIMENSIONS



(P1)

360° 270° 180° 90° 0°

57.805"

24"

8"

1.2"

0"


EXT

Coating (Int): Coating (Ext):	Seam Up: Tongue Seam Dn: n/a	Wall Thickness: 5" Floor Height: 8"	Height (Int): 24" Height (Ext): 32"	Weight (Net): 4468 lb Volume (Net): 1.14cu.yd
----------------------------------	---------------------------------	--	--	--

Job Name: 26-3703 Honeysuckle Way Sewer Ext Job Location: Springfield, KY Contractor: Hale Contracting					Plant: Beaver Dam 10/7/2026 4:02:14 PM		Tech: S. Felletter PC: M. Sullivan				
Structure ID: A9											
P1		MH048BAEVF									
MH BASE w/FLANGE T/n											
P5) 24" - CASTING HEIGHT - 7" P4) 24" - GRADE RING F/F - 3" P3) 48" - ECC CONE w/ 24" HOLE F/G - 30" P2) 48" - MH RISER T/G - 36" P1) 48" - MH BASE w/FLANGE T/n - 24" 1) JOINT WRAP - 0.065"x6"x50' CONSEAL CS212 1) JOINT WRAP PRIMER - CONSEAL CS-75 (1 gal.) 1) 48" - MH INVERT CHANNEL - FULL HEIGHT 2) 48" - Conseal CS-102 1.00" (Double) 2) 24" - Conseal CS-102 1.00" (Double) 2) PSX - 12-08 NYLO 7) MH Step ML-10-TDS-NCR - 10"					0 lb 202 lb 2050 lb 2515 lb 4468 lb 0 lb 0 lb 1440 lb 0 lb 0 lb 16 lb 0 lb		Structure Notes: . 1. PER ASTM C478 SPECIFICATIONS. 2. CONCRETE = 4,000 PSI AT 28 DAYS. 3. CASTING PROVIDED BY OTHERS. REINFORCING PER ASTM A615 (GRADE 60). - CONE (As .12) - RISER/WALLS (As .12) - FLOOR (As .31) #5 BARS AT 12" C.C.E.W.				
Structure Total: 10691 lb					Invert channel drawing Full height invert						
Rim: 787' Rim to Invert: 8.16' Slack: -0.08" Sump: 2" Step Position: 0°											
Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up ()	Offset	
Invert 1	778.84'	0°	0"	8" PVC SDR35	8.5"	PSX 12-08 NYLO	12"	12.129"	0"	0"	
Invert 2	778.94'	138°	69.848"	8" PVC SDR35	8.5"	PSX 12-08 NYLO	12"	12.129"	1.2"	0"	
Invert 3											
Invert 4											
Invert 5											
Invert 6											
Invert 7											
Invert 8											

RIGHT-SIDE UP VIEW (int. dimensions)

Invert: 2
Degree: 138°
Horz: 57.805"
Hole: 12"
Up(): 1.2"

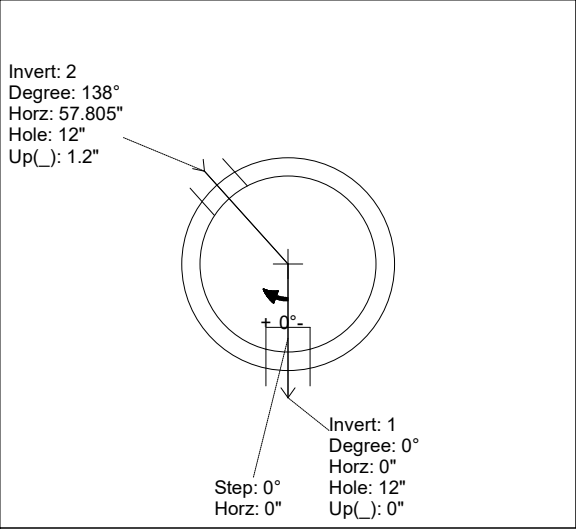


Invert: 1
Degree: 0°
Horz: 0"
Hole: 12"
Up(): 0"

Step: 0°
Horz: 0"

UPSIDE-DOWN VIEW (int. dimensions)


Invert: 2
Degree: 138°
Horz: 57.805"
Hole: 12"
Up(): 1.2"

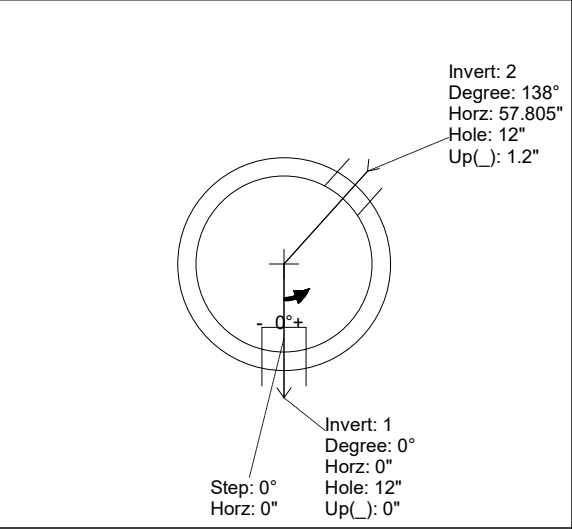

Invert: 1
Degree: 0°
Horz: 0"
Hole: 12"
Up(): 0"

Step: 0°
Horz: 0"

INSIDE WALL DIMENSIONS

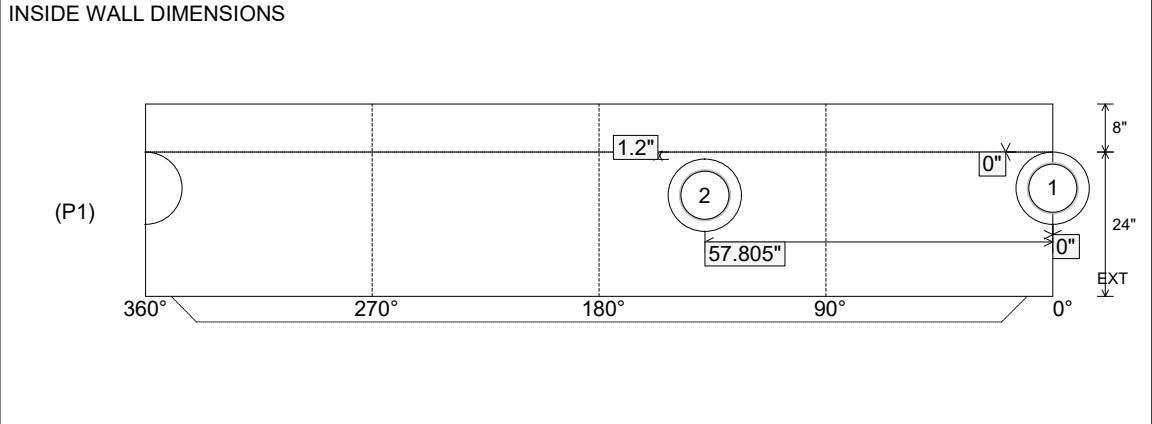

(P1)

360° 270° 180° 90° 0°

8" 24" EXT

1.2" 0" 57.805" 0"

Coating (Int):
Coating (Ext):

Seam Up: Tongue
Seam Dn: n/a

Wall Thickness: 5"
Floor Height: 8"

Height (Int): 24"
Height (Ext): 32"

Weight (Net): 4468 lb
Volume (Net): 1.14cu.yd
