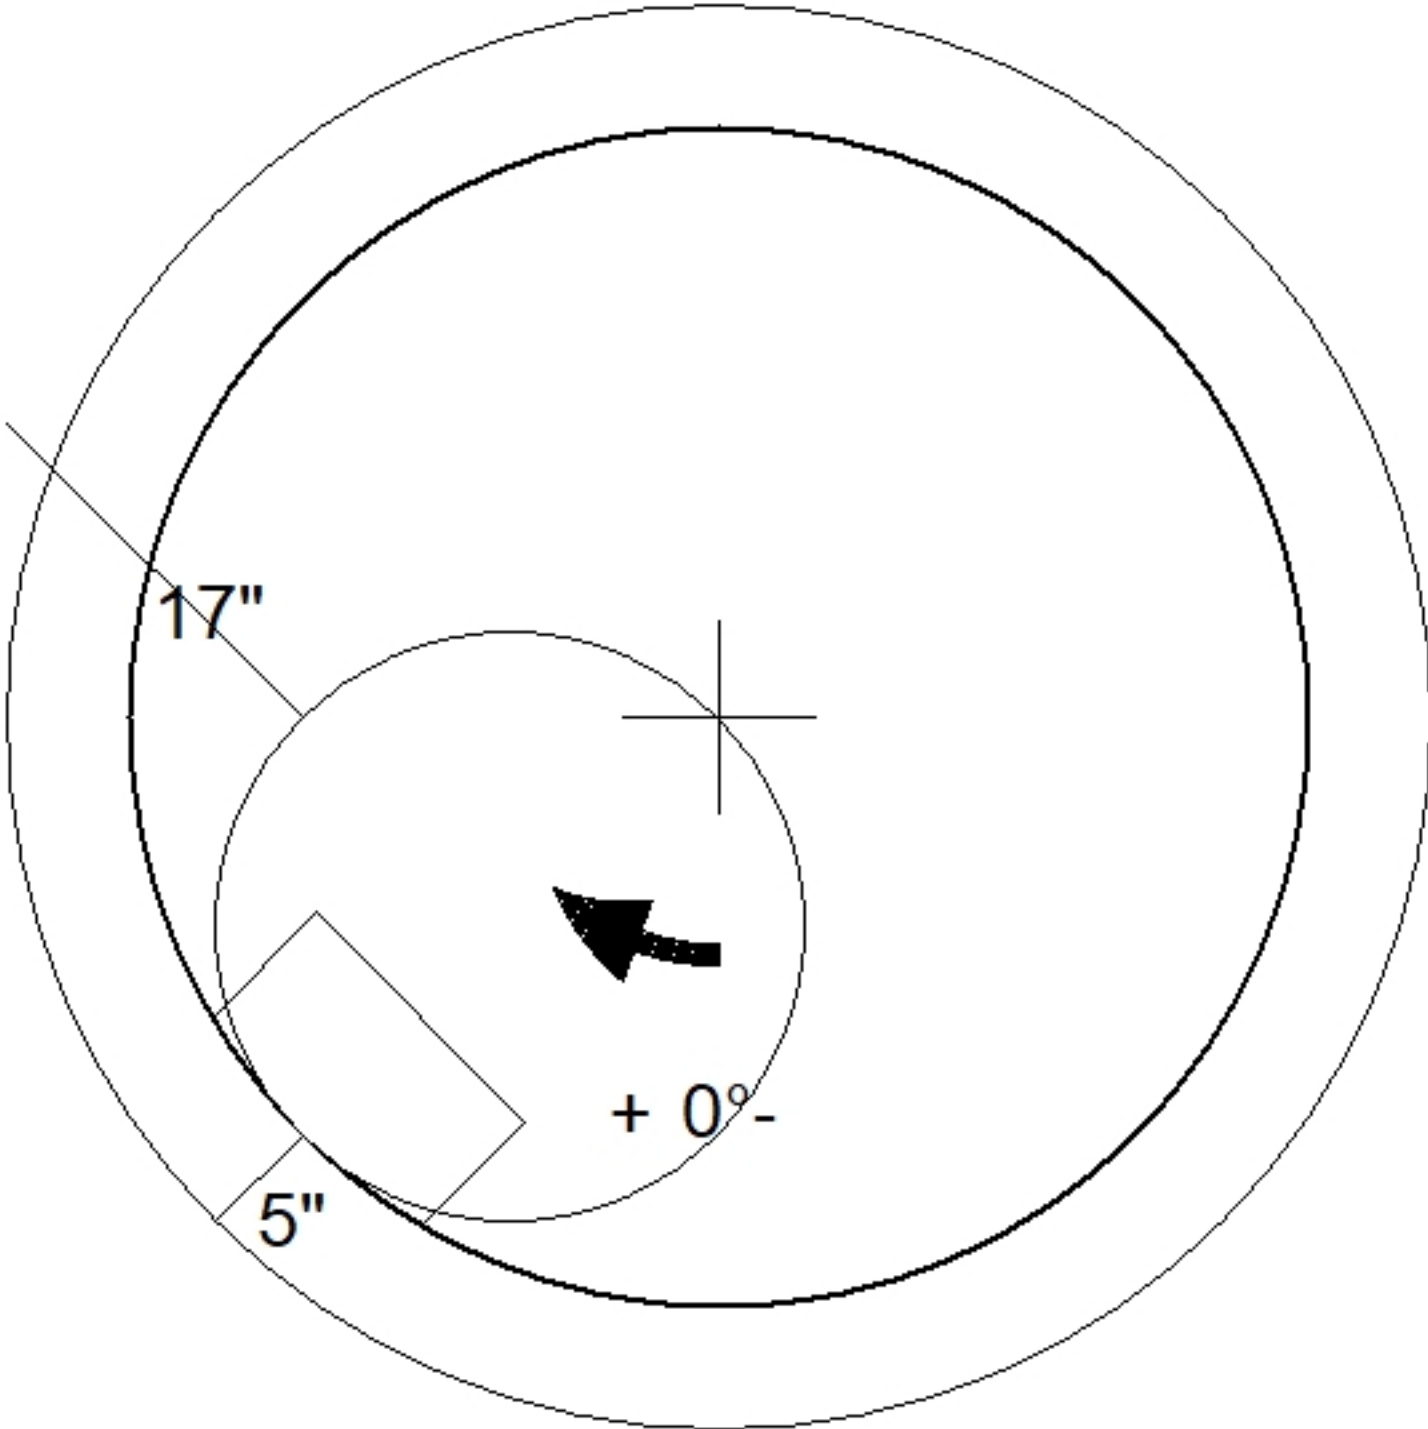
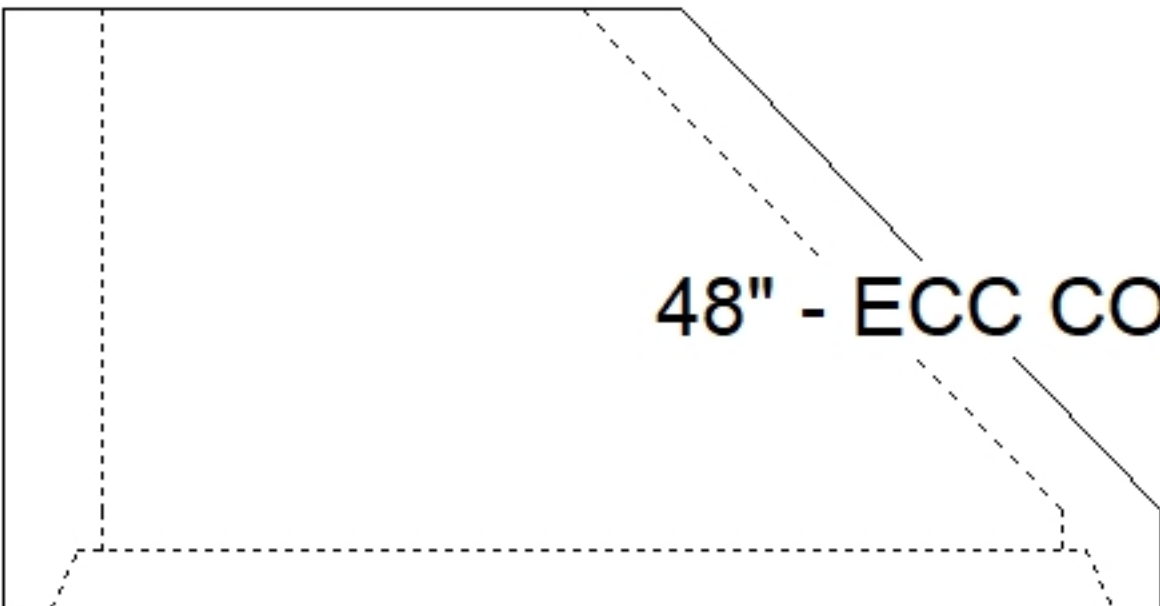


Job Name: 26-3734 Sandy Springs Sec. 2 Sanitary Manholes Job Location: Elizabethtown, KY Contractor: Gary Clifford		Plant: Beaver Dam 9/28/2026 3:26:29 PM	Tech: S. Felletter PC: T. Lewis	
Structure ID: 3 P2 MH048CN30		ECC CONE w/ 24" HOLE F/G		
P3) 24" - CASTING HEIGHT - 7" P2) 48" - ECC CONE w/ 24" HOLE F/G - 30" P1) 48" - MH BASE T/n - 24" 1) 48" - MH INVERT CHANNEL - FULL HEIGHT 1) JOINT WRAP - 0.065"x6"x50' CONSEAL CS212 1) JOINT WRAP PRIMER - CONSEAL CS-75 (1 gal.) 1) CASTING - HOE MC-375-WT F/C Sanitary 1) 48" - Conseal CS-102 1.00" (Double) 1) 24" - Conseal CS-102 1.00" (Double) 4) PSX - 12-08 NYLO 4) MH Step ML-10-TDS-NCR - 10"		0 lb 2050 lb 2815 lb 1440 lb 0 lb 0 lb 271 lb 0 lb 0 lb 32 lb 0 lb ----- 6608 lb Structure Total:	Structure Notes: . 1. PER ASTM C478 SPECIFICATIONS. 2. CONCRETE = 4,000 PSI AT 28 DAYS. 3. CASTING BY ICAST (HOE MC-375-WT F/C "SANITARY"). . REINFORCING PER ASTM A615 (GRADE 60). - CONE (As .12) - RISER/WALLS (As .12) - FLOOR (As .31) #5 BARS AT 12" C.C.E.W.	
				
				
Coating (Int): Coating (Ext):	Seam Up: Flat Seam Dn: Groove	Wall Thickness: 5"	Height (Ext): 30"	Weight (Net): 2050 lb Volume (Net): 0.41cu.yd
