

Job Name: 26-3781 ADS Warwick Park Ph. 2 & 3

Job Location: Louisville, KY

Contractor: ADS Advanced Drainage Systems, Inc.

Plant: Beaver Dam

10/1/2026 2:09:05 PM

Tech: S. Felletter

PC: M. Sullivan



Structure ID: S217

P3MH048RS24SMH RISER SPECIAL T/G

P5) 24" - CASTING HEIGHT - 7"

P4) 48" - MH FLAT LID w/24" Center Hole F/G - 12"

P3) 48" - MH RISER SPECIAL T/G - 24"

P2) 48" - MH RISER SPECIAL T/G - 72"

P1) 48" - MH BASE T/n - 24"

1) ASSEMBLY REQUIRED

1) JOINT WRAP - 0.065"x6"x50' CONSEAL CS212

1) JOINT WRAP PRIMER - CONSEAL CS-75 (1 gal.)

1) CASTING - HOE MC-375 F/C Storm

3) 48" - Conseal CS-102 1.00" (Double)

1) 24" - Conseal CS-102 1.00" (Double)

2) Hole - 12

0 lb

1580 lb

1677 lb

4934 lb

3007 lb

0 lb

0 lb

0 lb

271 lb

0 lb

0 lb

0 lb

11468 lb

Structure Total:

11468 lb

Structure Notes:

1. PER ASTM C478 SPECIFICATIONS.

2. CONCRETE = 4,000 PSI AT 28 DAYS.

3. CASTING BY ICAST (HOE MC-375 F/C "STORM").

4. LIFTING ANCHORS TO BE INSTALLED ON THE OUTSIDE OF THE STRUCTURE.

REINFORCING PER ASTM A615 (GRADE 60).

- TOP SLAB (As .62) #5 BARS AT 6" C.C.E.W.

- RISER/WALLS (As .12)

- FLOOR (As .31) #5 BARS AT 12" C.C.E.W.

Rim: 541.73'

Rim to Invert: 4.98'

Slack: 1.76"

Sump: 81"

Step Position: 0°

Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up ()	Offset
Invert 1										
Invert 2										
Invert 3										
Invert 4										
Invert 5										
Invert 6										
Invert 7										
Invert 8										

(P5)


(P4)

(P3) <<

(P2)

(P1)

RIGHT-SIDE UP VIEW (int. dimensions)

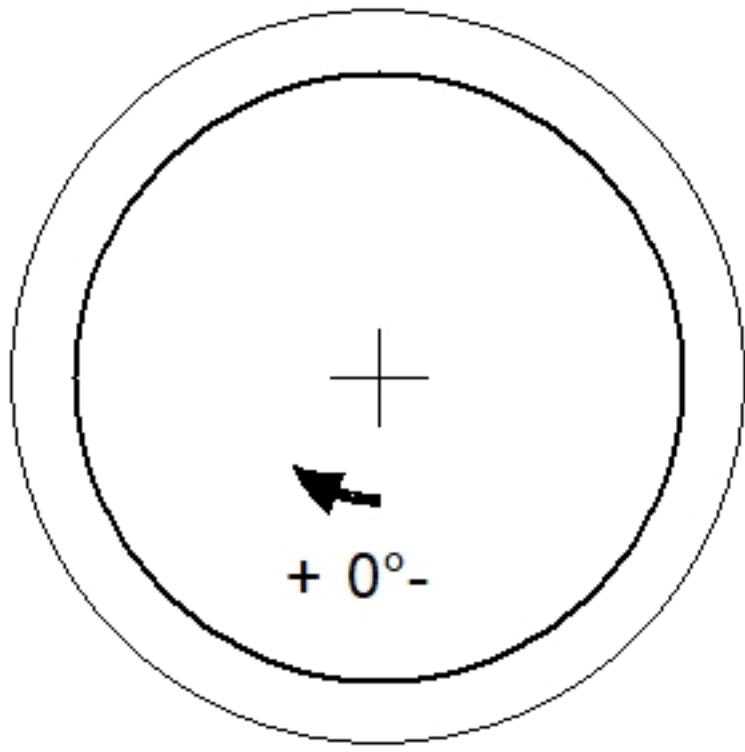

INSIDE WALL DIMENSIONS

0°


90°

180°

270°

360°

(P3)

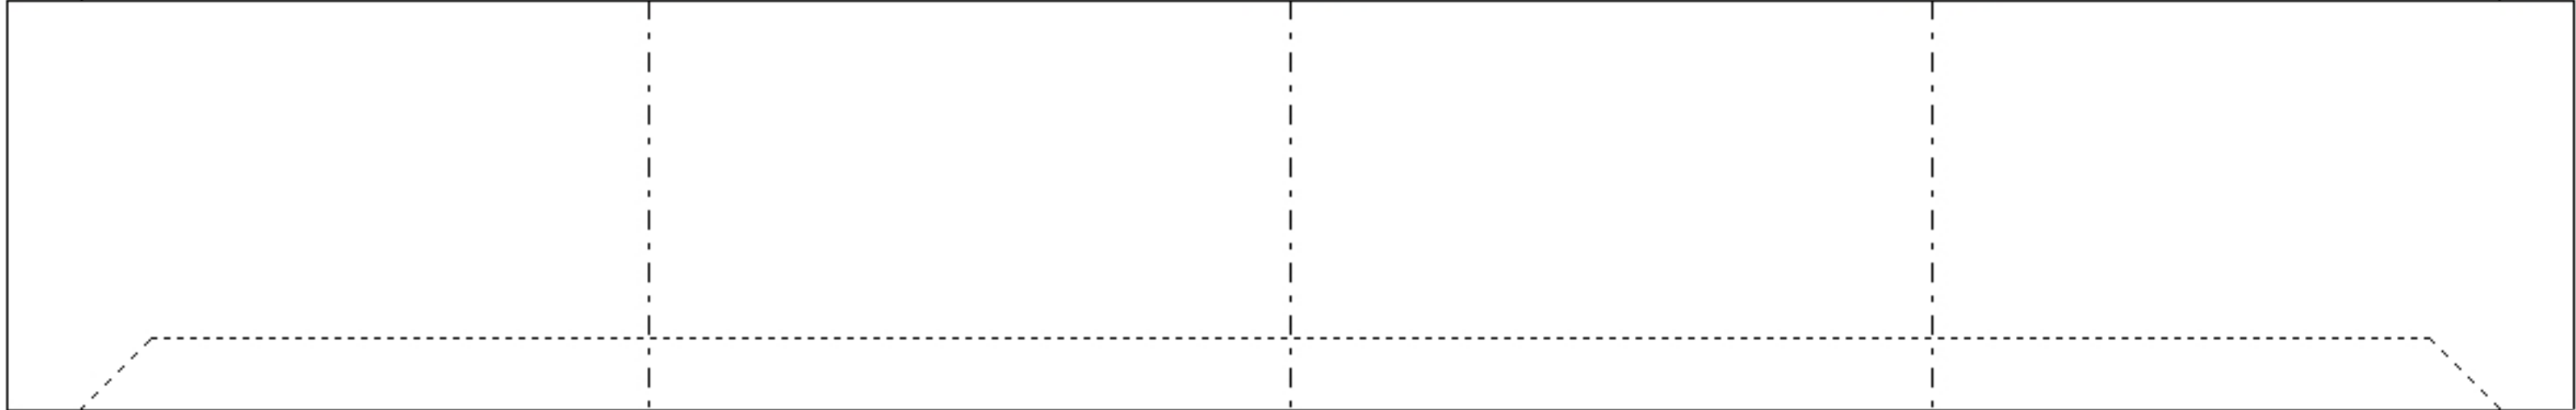

EXT

24"

Coating (Int):

Coating (Ext):

Seam Up: Tongue

Seam Dn: Groove

Wall Thickness: 5"

Floor Height: 0"

Height (Int): 24"

Height (Ext): 24"

Weight (Net): 1677 lb

Volume (Net): 0.43cu.yd
