



Job Name: 26-3805 - Goldfinch Sewer Ph.3 Job Location: Evansville, IN Contractor: CAC Custom Homes					Plant: 100 9/29/2026 7:43:03 AM		Tech: J. Horsley PC: T. Lewis				
Structure ID: SSMH 723											
P1 MH048BA30X		MH BASE w/XYPEX T/n									
P5) 24" - CASTING HEIGHT - 7" P4) 48" - ECC XYPEX CONE w/ 24" HOLE F/G - 24" P3) 48" - MH RISER w/XYPEX/NO STEP T/G - 36" P2) 48" - MH RISER w/XYPEX/NO STEP T/G - 60" P1) 48" - MH BASE w/XYPEX T/n - 30" 1) 48" - MH INVERT CHANNEL EWSU w/XYPEX - FULL HEIGHT 1) JOINT WRAP - 0.065"x6"x50' CONSEAL CS212 1) JOINT WRAP PRIMER - CONSEAL CS-75 (1 gal.) 1) CASTING - HOE MC-315 F/C Sanitary 3) 48" - Conseal CS-102 1.00" (Double) 1) 24" - Conseal CS-102 1.00" (Double) 2) PSX - 12-08 NYLO						0 lb 1738 lb 2515 lb 4192 lb 3330 lb 1440 lb 0 lb 0 lb 0 lb 258 lb 0 lb 0 lb 0 lb 16 lb		Structure Notes: 1. PER ASTM C478 SPECIFICATIONS. 2. CONCRETE = 4,000 PSI AT 28 DAYS. 3. ADMIX = XYPEX C500-NF-RED 4. CASTING BY ICAST (HOE MC-315 F/C "SANITARY") REINFORCING PER ASTM A615 (GRADE 60). - CONE (As .12) - RISER (As .12) - FLOOR (As .31) #5 BARS AT 12" C.C.E.W.			
Rim: 386.4' Rim to Invert: 13.12' Slack: 2.44" Sump: 2" Step Position:						Structure Total: 13489 lb					
Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up ()	Offset	
Invert 1	373.28'	0°	0"	8" PVC SDR26	8.5"	PSX 12-08 NYLO	12"	12.129"	0"	0"	
Invert 2	373.38'	180°	91.125"	8" PVC SDR26	8.5"	PSX 12-08 NYLO	12"	12.129"	1.25"	0"	
Invert 3											
Invert 4											
Invert 5											
Invert 6											
Invert 7											
Invert 8											


RIGHT-SIDE UP VIEW (int. dimensions)

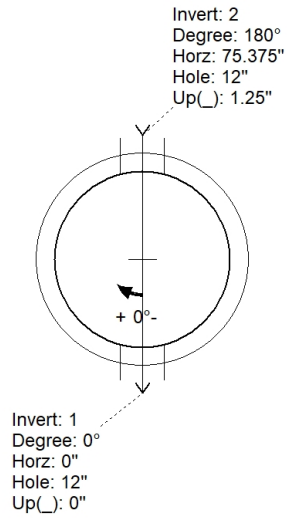


UPSIDE-DOWN VIEW (int. dimensions)

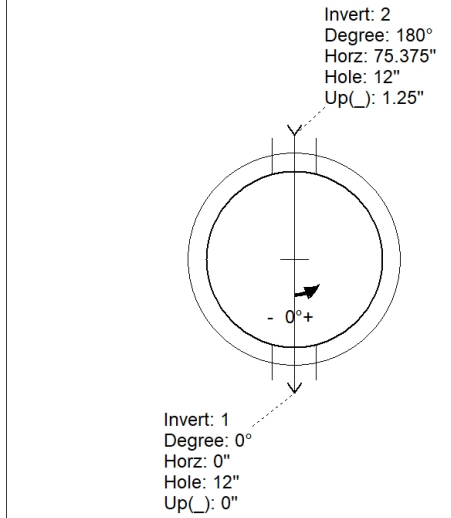

INSIDE WALL DIMENSIONS

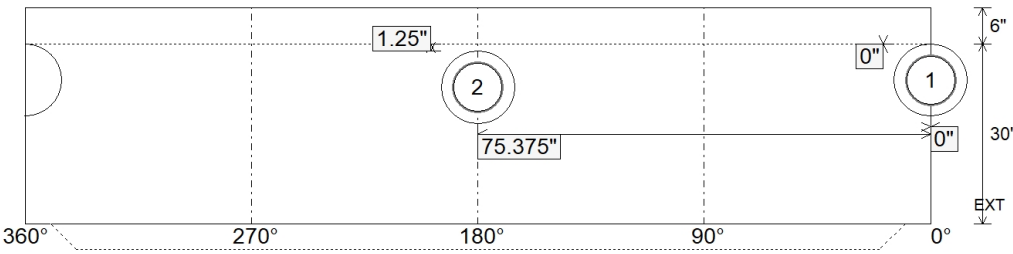

Coating (Int): Coating (Ext):	Seam Up: Tongue Seam Dn: n/a	Wall Thickness: 5" Floor Height: 6"	Height (Int): 30" Height (Ext): 36"	Weight (Net): 3330 lb Volume (Net): 0.85cu.yd
----------------------------------	---------------------------------	--	--	--



Weight (Net): 3330 lb
Volume (Net): 0.85cu.yd
