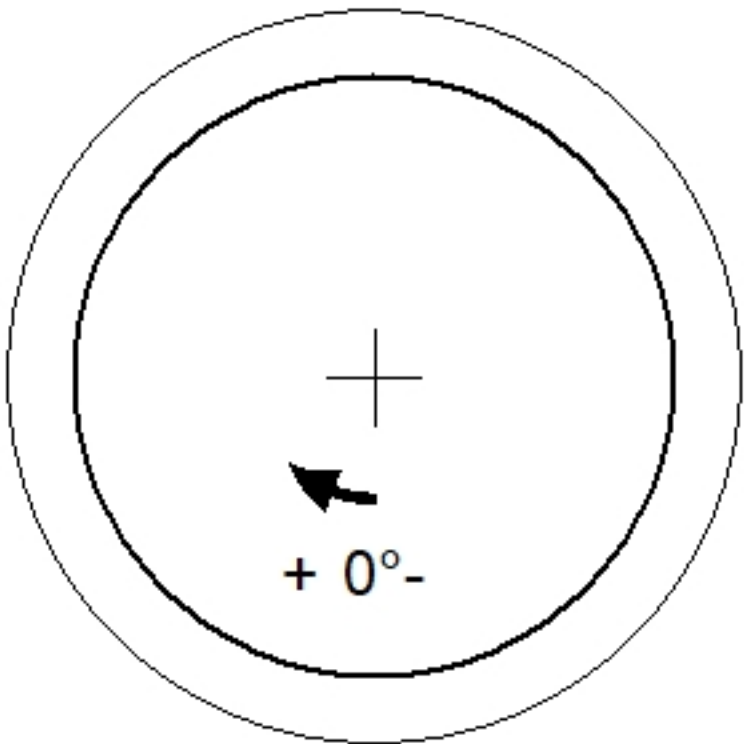
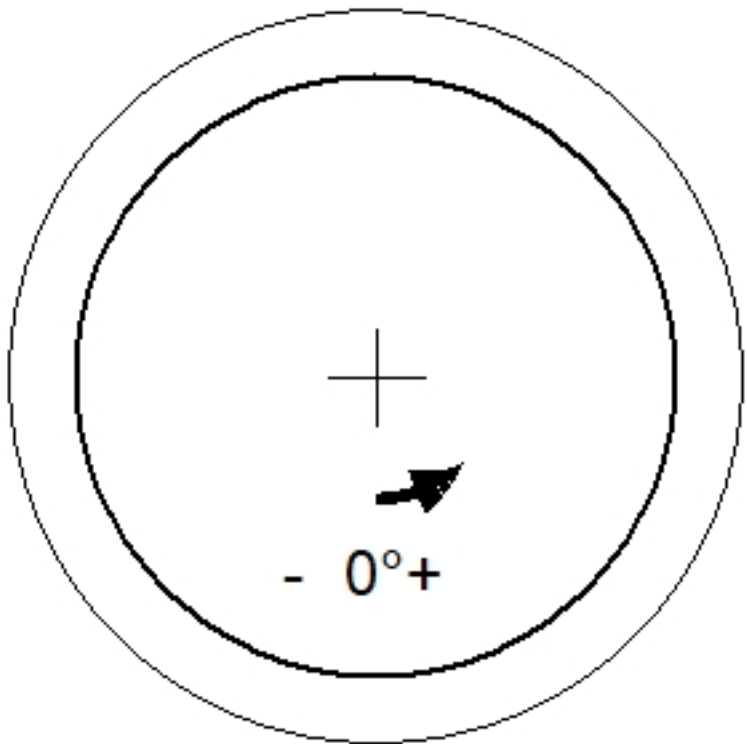
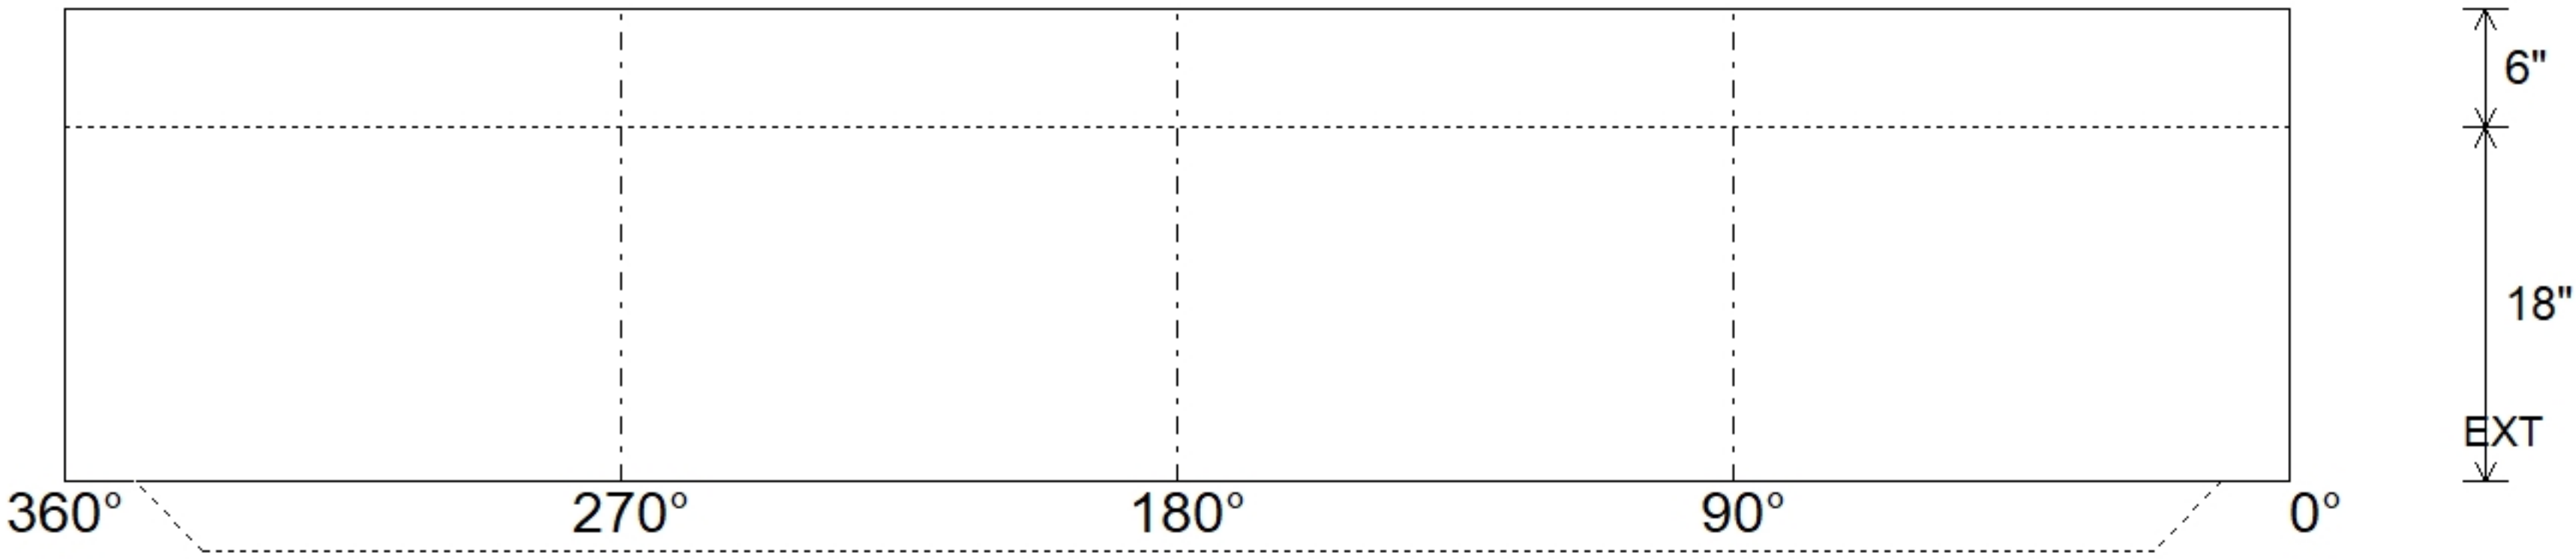


Job Name: 26-3824 ADS LivSmart Job Location: Florence, KY Contractor: ADS Advanced Drainage Systems, Inc.					Plant: Beaver Dam 10/9/2026 1:21:05 PM		Tech: S. Felletter PC: M. Sullivan																
Structure ID: WQMH 2																							
P1		MH036BA18		MH BASE T/n																			
P6) 24" - CASTING HEIGHT - 7" P5) 24" - GRADE RING F/F - 3" P4) 36" - MH FLAT TOP w/ 24" Ctr. Hole F/G - 10" P3) 36" - MH RISER T/G - 48" P2) 36" - MH RISER T/G - 72" P1) 36" - MH BASE T/n - 18" 1) ASSEMBLY REQUIRED 1) JOINT WRAP - 0.065"x6"x50' CONSEAL CS212 1) JOINT WRAP PRIMER - CONSEAL CS-75 (1 gal.) 1) CASTING - HOE MC-375 F/C Storm 3) 36" - Conseal CS-102 1.00" 2) 24" - Conseal CS-102 1.00" 2) Hole - 20						0 lb 202 lb 896 lb 2025 lb 2816 lb 1525 lb 0 lb 0 lb 0 lb 271 lb 0 lb 0 lb 0 lb ----- 7735 lb		Structure Notes: . 1. PER ASTM C478 SPECIFICATIONS. 2. CONCRETE = 4,000 PSI AT 28 DAYS. 3. CASTING BY ICAST (HOE MC-375 F/C "STORM"). 4. LIFTING ANCHORS TO BE INSTALLED ON THE OUTSIDE OF THE STRUCTURE. . REINFORCING PER ASTM A615 (GRADE 60). - TOP SLAB (As .62) #5 BARS AT 6" C.C.E.W. - RISER/WALLS (As .12) - FLOOR (As .31) #5 BARS AT 12" C.C.E.W.															
Rim: 876.89' Rim to Invert: 8.61' Slack: 0.28" Sump: 54.96" Step Position: 0°																							
Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up (⌋)	Offset													
Invert 1																							
Invert 2																							
Invert 3																							
Invert 4																							
Invert 5																							
Invert 6																							
Invert 7																							
Invert 8																							
(P6) (P5) (P4) (P3) (P2) (P1) << RIGHT-SIDE UP VIEW (int. dimensions)  UPSIDE-DOWN VIEW (int. dimenions)  INSIDE WALL DIMENSIONS (P1)  <tr><td colspan="3">Coating (Int): Coating (Ext):</td><td colspan="2">Seam Up: Tongue Seam Dn: n/a</td><td colspan="2">Wall Thickness: 4" Floor Height: 6"</td><td colspan="2">Height (Int): 18" Height (Ext): 24"</td><td colspan="3">Weight (Net): 1525 lb Volume (Net): 0.39cu.yd</td></tr>												Coating (Int): Coating (Ext):			Seam Up: Tongue Seam Dn: n/a		Wall Thickness: 4" Floor Height: 6"		Height (Int): 18" Height (Ext): 24"		Weight (Net): 1525 lb Volume (Net): 0.39cu.yd		
Coating (Int): Coating (Ext):			Seam Up: Tongue Seam Dn: n/a		Wall Thickness: 4" Floor Height: 6"		Height (Int): 18" Height (Ext): 24"		Weight (Net): 1525 lb Volume (Net): 0.39cu.yd														
