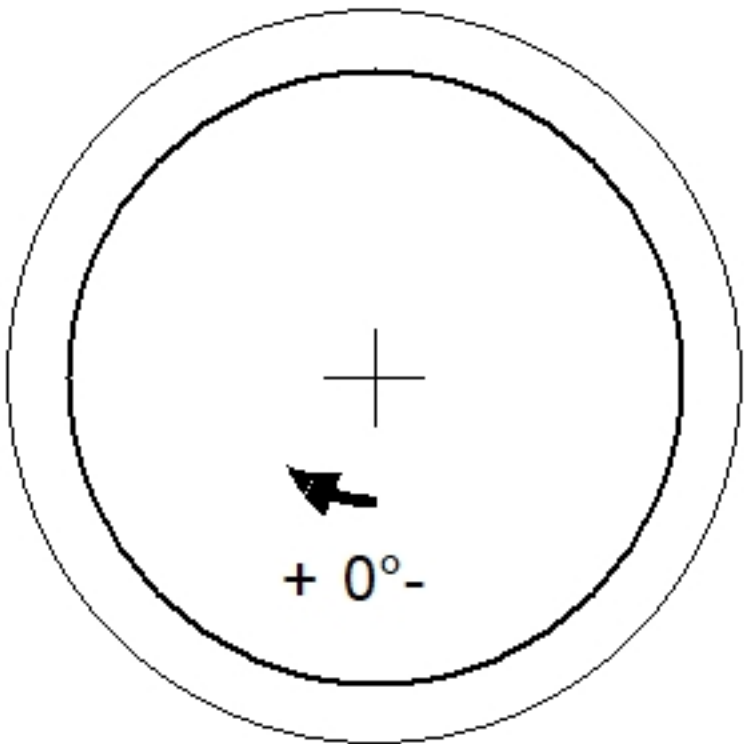
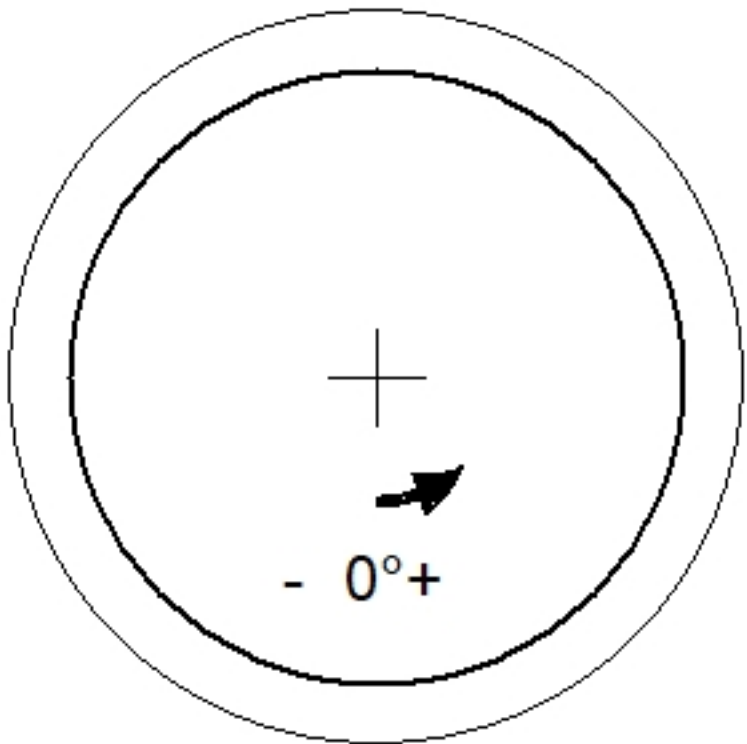
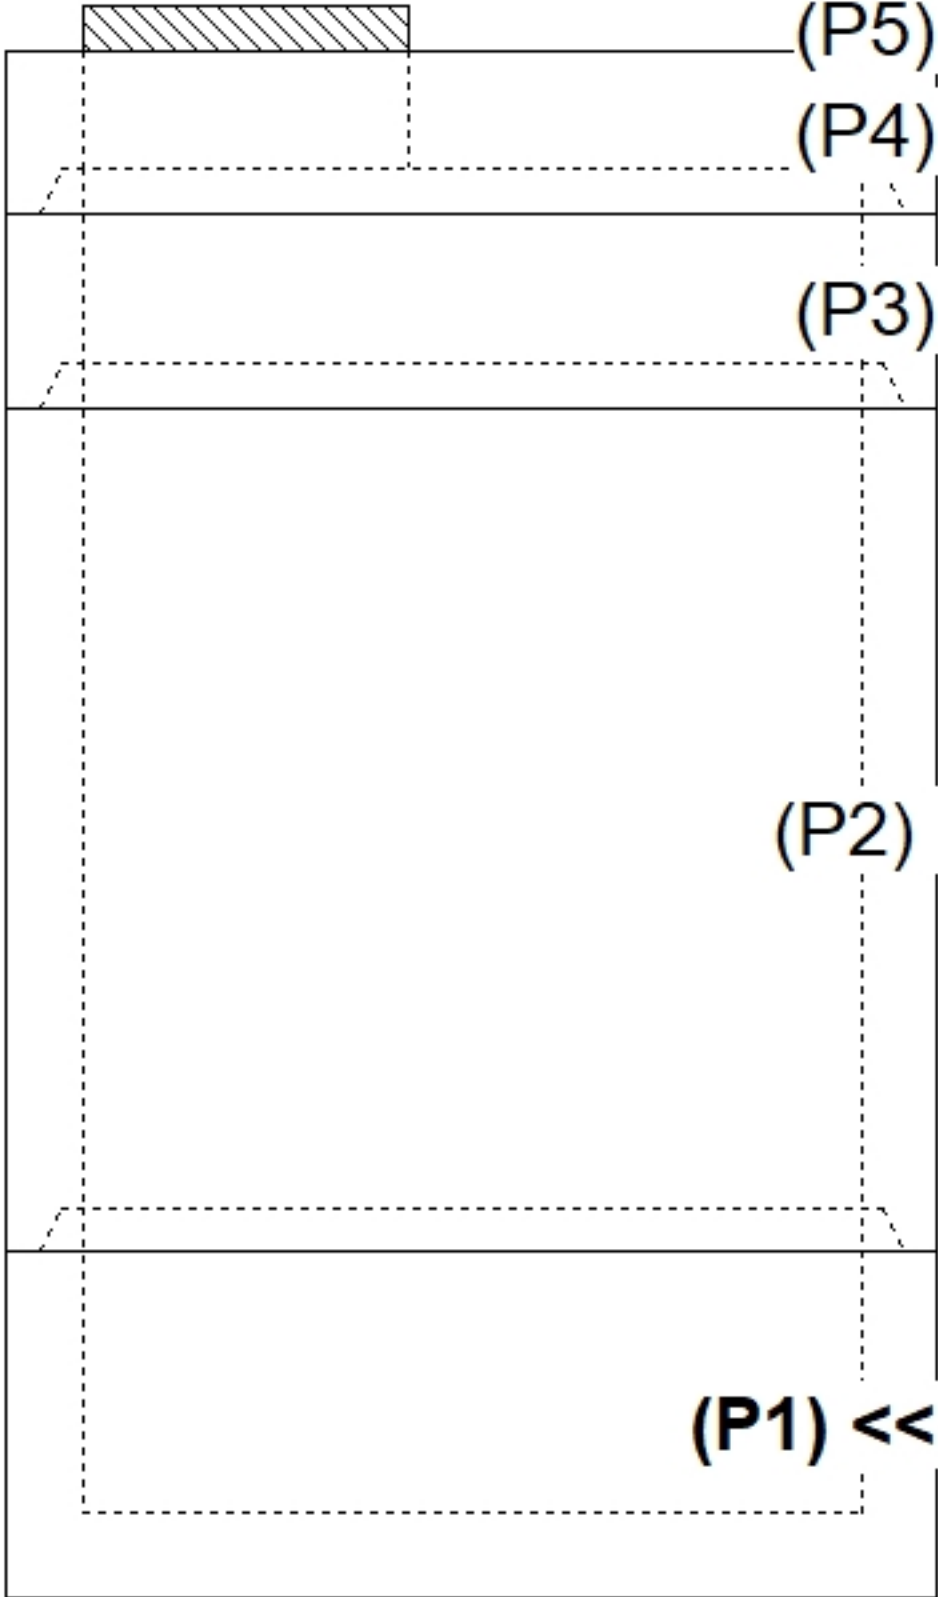
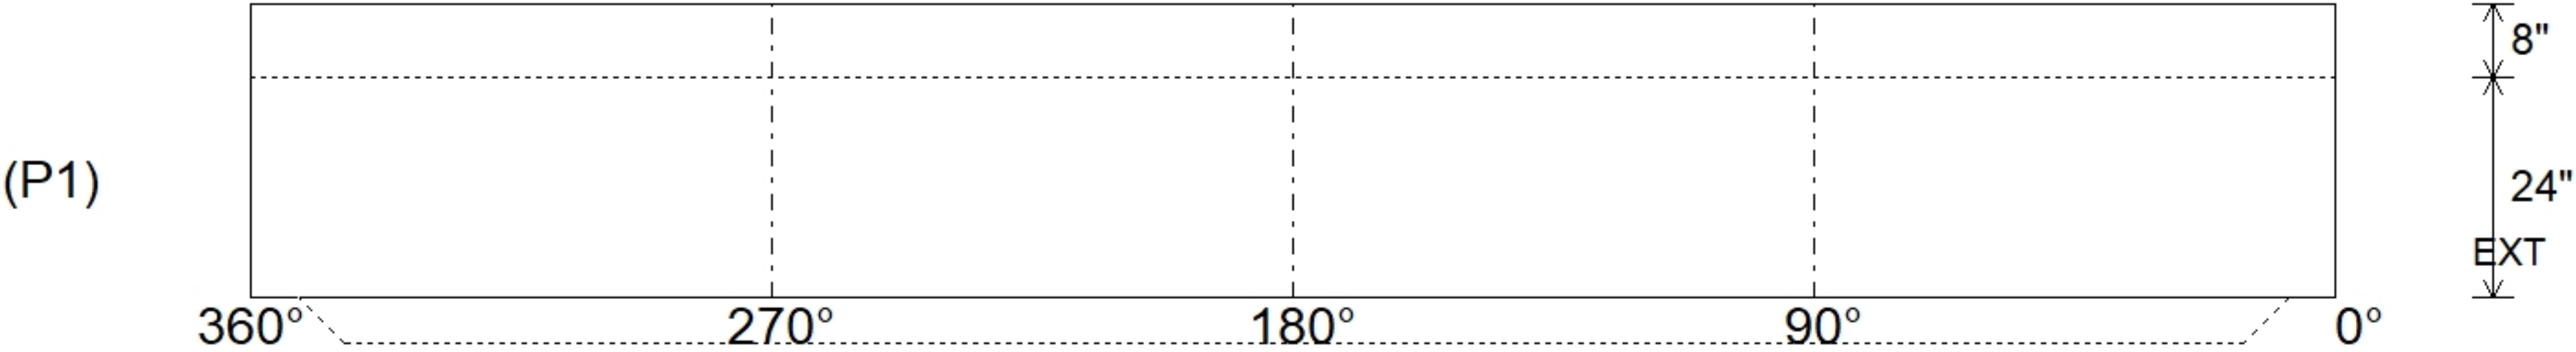


Job Name: 26-3879 905509 Kroger Store L966 Job Location: Nicholasville, KY Contractor: Contech Engineering Solutions					Plant: Beaver Dam 10/1/2026 3:11:18 PM		Tech: S. Felletter PC: C. Goff						
Structure ID: 10-CS-6													
P1			MH072BA24			MH BASE T/n							
P5) 30" - CASTING HEIGHT - 4" P4) 72" - MH FLAT TOP SPEC. (30" ECC HOLE) F/G - 15" P3) 72" - MH RISER SPECIAL T/G - 18" P2) 72" - MH RISER SPECIAL T/G - 78" P1) 72" - MH BASE T/n - 24" 1) ASSEMBLY REQUIRED 1) CVSTENCILING 3) 72" - Conseal CS-102 1.00" 1) Hole - 36 1) Hole - 32						0 lb 4661 lb 2624 lb 10263 lb 7398 lb 0 lb 0 lb 0 lb 0 lb 0 lb ----- 24946 lb		Structure Notes: . 4" CASTING BY OTHERS . LIFTING ANCHORS TO BE INSTALLED ON THE OUTSIDE OF THE STRUCTURE . ICAST TO INSTALL THE INTERNALS . CONTECH'S LOGO AS WELL AS THE INLET AND OUTLET MUST BE STENCILED ONTO THE STRUCTURE					
Rim: 1025.71' Rim to Invert: 6.33' Slack: 7.04" Sump: 70.08" Step Position: 0°													
Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up (⌋)	Offset			
Invert 1													
Invert 2													
Invert 3													
Invert 4													
Invert 5													
Invert 6													
Invert 7													
Invert 8													
RIGHT-SIDE UP VIEW (int. dimensions)  UPSIDE-DOWN VIEW (int. dimenions)   INSIDE WALL DIMENSIONS 													
Coating (Int): Coating (Ext):			Seam Up: Tongue Seam Dn: n/a		Wall Thickness: 7" Floor Height: 8"		Height (Int): 24" Height (Ext): 32"		Weight (Net): 7398 lb Volume (Net): 1.89cu.yd				
