

Job Name: 26-3879 905509 Kroger Store L966

Job Location: Nicholasville, KY

Contractor: Contech Engineering Solutions

Plant: Beaver Dam

10/1/2026 3:12:37 PM

Tech: S. Felletter

PC: C. Goff



Structure ID: 10-CS-6

P3 MH072RS18S

MH RISER SPECIAL T/G

P5) 30" - CASTING HEIGHT - 4"

P4) 72" - MH FLAT TOP SPEC. (30" ECC HOLE) F/G - 15"

P3) 72" - MH RISER SPECIAL T/G - 18"

P2) 72" - MH RISER SPECIAL T/G - 78"

P1) 72" - MH BASE T/n - 24"

1) ASSEMBLY REQUIRED

1) CVSTENCILING

3) 72" - Conseal CS-102 1.00"

1) Hole - 36

1) Hole - 32

0 lb

4661 lb

2624 lb

10263 lb

7398 lb

0 lb

0 lb

0 lb

0 lb

0 lb

Structure Total: 24946 lb

Structure Notes:

4" CASTING BY OTHERS

.

LIFTING ANCHORS TO BE INSTALLED ON THE OUTSIDE OF THE STRUCTURE

.

ICAST TO INSTALL THE INTERNALS

.

CONTECH'S LOGO AS WELL AS THE INLET AND OUTLET MUST BE STENCILED ONTO THE STRUCTURE

Rim: 1025.71'

Rim to Invert: 6.33'

Slack: 7.04"

Sump: 70.08"

Step Position: 0°

Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up (┘)	Offset
Invert 1										
Invert 2										
Invert 3										
Invert 4										
Invert 5										
Invert 6										
Invert 7										
Invert 8										

(P5)


(P4)

(P3) <<

(P2)


(P1)

RIGHT-SIDE UP VIEW (int. dimensions)

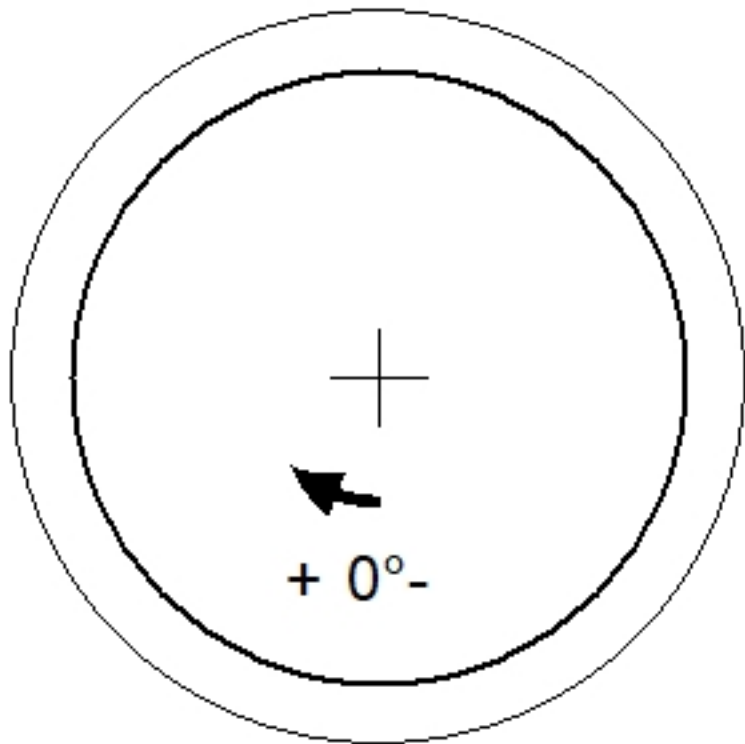

INSIDE WALL DIMENSIONS

(P3)

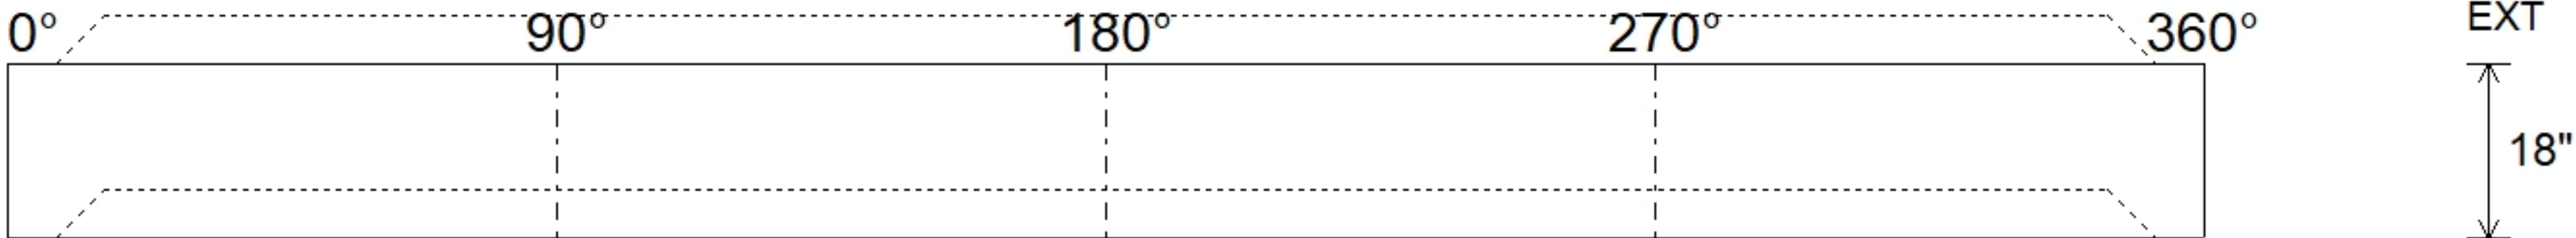

Coating (Int):

Coating (Ext):

Seam Up: Tongue

Seam Dn: Groove

Wall Thickness: 7"

Floor Height: 0"

Height (Int): 18"

Height (Ext): 18"

Weight (Net): 2624 lb

Volume (Net): 0.67cu.yd
