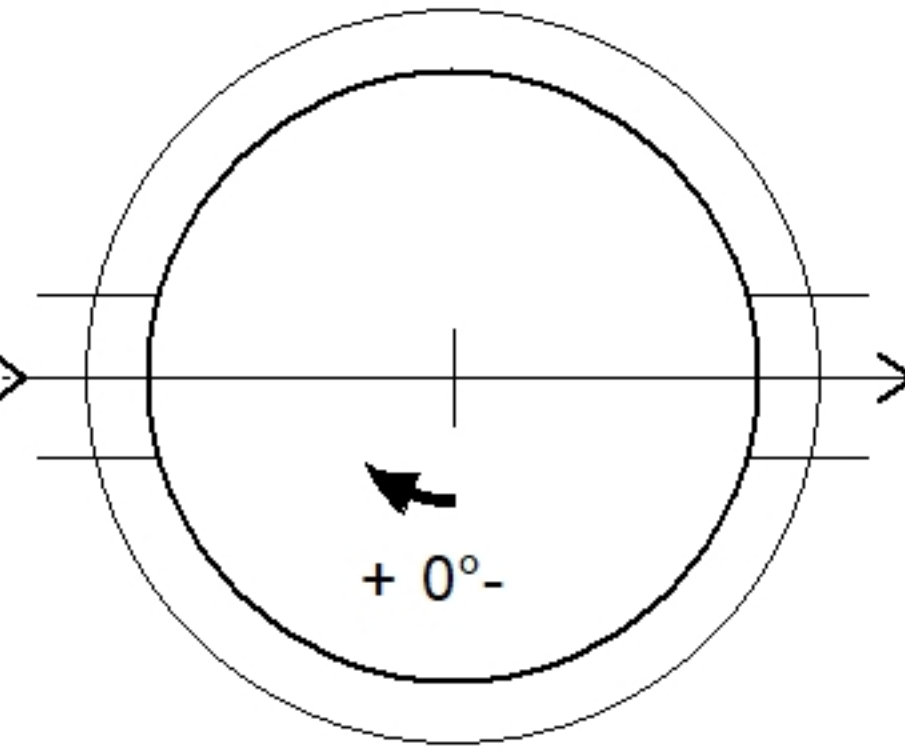


Job Name: 26-3923 913209 Pleasant Valley Reserve Job Location: Owensboro, KY Contractor: Contech Engineering Solutions					Plant: Beaver Dam 10/8/2026 9:23:11 AM		Tech: S. Felletter PC: C. Goff				
Structure ID: 10-CS-5											
P2		MH060RS66S		MH RISER SPECIAL T/G							
P4) 30" - CASTING HEIGHT - 4" P3) 60" - MH FLAT TOP SPEC. (30" ECC HOLE) F/G - 13" P2) 60" - MH RISER SPECIAL T/G - 66" P1) 60" - MH BASE T/n - 18" 1) ASSEMBLY REQUIRED 1) CVSTENCILING 2) 60" - Conseal CS-102 1.00" 2) Hole - 16						0 lb 2589 lb 6685 lb 4612 lb 0 lb 0 lb 0 lb 0 lb ----- Structure Total: 13887 lb		Structure Notes: 4" CASTING BY OTHERS LIFTING ANCHORS TO BE INSTALLED ON THE OUTSIDE OF THE STRUCTURE ICAST TO INSTALL THE INTERNALS CONTECH'S LOGO AS WELL AS THE INLET AND OUTLET MUST BE STENCILED ONTO THE STRUCTURE			
Rim: 440'		Rim to Invert: 4.08'		Slack: 6.04"		Sump: 58.08"		Step Position:			
Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up ()	Offset	
Invert 1	435.92'	270°	169.646"	12" PVC SDR35	12.5"	Hole 16	16"	16.196"	33.33"	0"	
Invert 2	435.92'	90°	56.549"	12" PVC SDR35	12.5"	Hole 16	16"	16.196"	33.33"	0"	
Invert 3											
Invert 4											
Invert 5											
Invert 6											
Invert 7											
Invert 8											
RIGHT-SIDE UP VIEW (int. dimensions) Invert: 2 Degree: 90° Horz: 47.124" Hole: 16" Up(): 33.33"  Invert: 1 Degree: 270° Horz: 141.372" Hole: 16" Up(): 33.33" INSIDE WALL DIMENSIONS											
Coating (Int): Coating (Ext):			Seam Up: Tongue Seam Dn: Groove		Wall Thickness: 6" Floor Height: 0"		Height (Int): 66" Height (Ext): 66"		Weight (Net): 6685 lb Volume (Net): 1.71cu.yd		
