




Job Name: 25-1401 Irwin Landing Ph. 1 Job Location: Murfreesboro, TN Contractor: Bear Construction LLC				Plant: Beaver Dam 6/9/2026 10:37:13 AM		Tech: S. Felletter PC: Erica Bradley				
Structure ID: R26										
P1 BX28280606VH				BOX BASE 6inW, 6inF, Variable Ht F/n						
P2) 28" x 28" - CASTING HEIGHT - 5" P1) 28" x 28" - BOX BASE 6inW, 6inF, Variable Ht F/n - 41" 1) 28" x 28" - STORM INVERT CHANNEL (FLAT) - 4" THK 1) CASTING - JBS 3104-V SINGLE SET 1) 28" x 28" - Conseal CS-102 1.00" 1) Hole - 26"				0 lb 3346 lb 450 lb 250 lb 0 lb 0 lb ----- 4046 lb Structure Total:		Structure Notes: 1. PER ASTM C913 SPECIFICATIONS. 2. CONCRETE = 4,000 PSI AT 28 DAYS. 3. CASTING BY ICAST (JBS-3104 SINGLE SET). REINFORCING PER ASTM A615 (GRADE 60). - WALLS (As .31) #5 BARS AT 12" C.C.E.W. - FLOOR (As .31) #5 BARS AT 12" C.C.E.W.				
Rim: 575.67' Rim to Invert: 3.67' Slack: 0.54" Sump: 2.5" Step Position:										
Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up ()	Offset
Invert 1	572'	0°	20"	18" RCP B WALL	23"	Hole 26	26"	26"	0"	0"
Invert 2										
Invert 3										
Invert 4										
Invert 5										
Invert 6										
Invert 7										
Invert 8										



RIGHT-SIDE UP VIEW (int. dimensions)



UPSIDE-DOWN VIEW (int. dimensions)

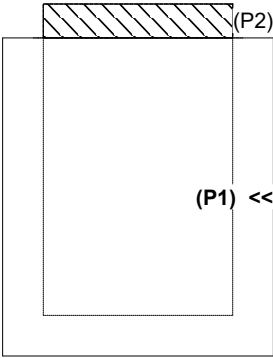

(P1) << (P2)

INSIDE WALL DIMENSIONS

(P1)	Left	Back (28")	Right (28")	Front	EXT 41" 6"
					

Coating (Int): Coating (Ext):	Seam Up: Flat Seam Dn: n/a	Wall Thickness: 6" Floor Height: 6"	Height (Int): 41" Height (Ext): 47"	Weight (Net): 3346 lb Volume (Net): 0.86cu.yd
----------------------------------	-------------------------------	--	--	--

Job Name: 25-1401 Irwin Landing Ph. 1

Job Location: Murfreesboro, TN

Contractor: Bear Construction LLC

Plant: Beaver Dam

6/9/2026 10:37:13 AM

Tech: S. Felletter

PC: Erica Bradley



Structure ID: R26

P1 BX28280606VH

BOX BASE 6inW, 6inF, Variable Ht F/n

P2) 28" x 28" - CASTING HEIGHT - 5"

P1) 28" x 28" - BOX BASE 6inW, 6inF, Variable Ht F/n - 41"

1) 28" x 28" - STORM INVERT CHANNEL (FLAT) - 4" THK

1) CASTING - JBS 3104-V SINGLE SET

1) 28" x 28" - Conseal CS-102 1.00"

1) Hole - 26

0 lb

3346 lb

450 lb

250 lb

0 lb

0 lb

Structure Total: 4046 lb

Structure Notes:

1. PER ASTM C913 SPECIFICATIONS.

2. CONCRETE = 4,000 PSI AT 28 DAYS.

3. CASTING BY ICAST (JBS-3104 SINGLE SET).

REINFORCING PER ASTM A615 (GRADE 60).

- WALLS (As .31) #5 BARS AT 12" C.C.E.W.

- FLOOR (As .31) #5 BARS AT 12" C.C.E.W.

Invert channel drawing

4" Thick flat storm invert

Rim: 575.67'

Rim to Invert: 3.67'

Slack: 0.54"


Sump: 2.5"

Step Position:


Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up ()	Offset
Invert 1	572'	0°	20"	18" RCP B WALL	23"	Hole 26	26"	26"	0"	0"
Invert 2										
Invert 3										
Invert 4										
Invert 5										
Invert 6										
Invert 7										
Invert 8										

RIGHT-SIDE UP VIEW (int. dimensions)

UPSIDE-DOWN VIEW (int. dimenions)



Invert: 1
Degree: 0°
Horz: 14"
Hole: 26"
Up(): 0"



Invert: 1
Degree: 0°
Horz: 14"
Hole: 26"
Up(): 0"

INSIDE WALL DIMENSIONS



LeftBack (28")Right (28")Front

Coating (Int):

Coating (Ext):

Seam Up: Flat

Seam Dn: n/a

Wall Thickness: 6"

Floor Height: 6"

Height (Int): 41"

Height (Ext): 47"

Weight (Net): 3346 lb

Volume (Net): 0.86cu.yd
