




Job Name: 25-1401 Irwin Landing Ph. 1 Job Location: Murfreesboro, TN Contractor: Bear Construction LLC					Plant: Beaver Dam 6/9/2026 10:37:13 AM		Tech: S. Felletter PC: Erica Bradley				
Structure ID: R27											
P1		BX28280606VH		BOX BASE 6inW, 6inF, Variable Ht F/n							
P2) 28" x 28" - CASTING HEIGHT - 5" P1) 28" x 28" - BOX BASE 6inW, 6inF, Variable Ht F/n - 43" 1) 28" x 28" - STORM INVERT CHANNEL (FLAT) - 4" THK 1) CASTING - JBS 3104-V SINGLE SET 1) 28" x 28" - Conseal CS-102 1.00" 1) Hole - 26"					0 lb 3483 lb 450 lb 250 lb 0 lb 0 lb ----- 4183 lb Structure Total:		Structure Notes: 1. PER ASTM C913 SPECIFICATIONS. 2. CONCRETE = 4,000 PSI AT 28 DAYS. 3. CASTING BY ICAST (JBS-3104 SINGLE SET). REINFORCING PER ASTM A615 (GRADE 60). - WALLS (As .31) #5 BARS AT 12" C.C.E.W. - FLOOR (As .31) #5 BARS AT 12" C.C.E.W.				
Rim: 576.81' Rim to Invert: 3.83' Slack: 0.46" Sump: 2.5" Step Position:											
Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up ()	Offset	
Invert 1	572.98'	0°	20"	18" RCP B WALL	23"	Hole 26	26"	26"	0"	0"	
Invert 2											
Invert 3											
Invert 4											
Invert 5											
Invert 6											
Invert 7											
Invert 8											




Invert: 1
Degree: 0°
Horz: 14"
Hole: 26"
Up(): 0"



Invert: 1
Degree: 0°
Horz: 14"
Hole: 26"
Up(): 0"


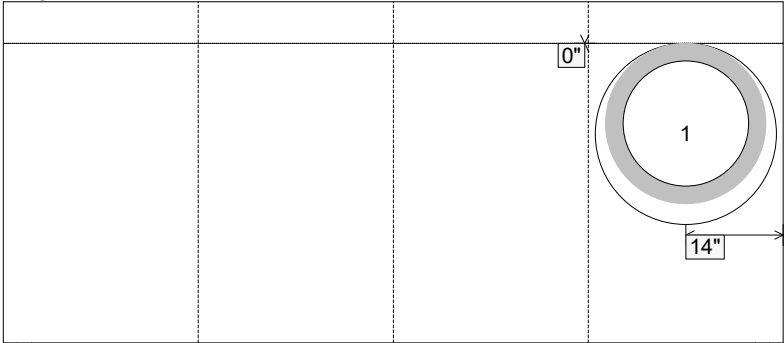


Left Back (28") Right (28") Front

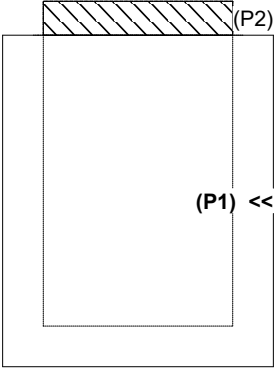

(P1) << (P2)

Coating (Int): Coating (Ext):	Seam Up: Flat Seam Dn: n/a	Wall Thickness: 6" Floor Height: 6"	Height (Int): 43" Height (Ext): 49"	Weight (Net): 3483 lb Volume (Net): 0.89cu.yd
----------------------------------	-------------------------------	--	--	--

Job Name: 25-1401 Irwin Landing Ph. 1 Job Location: Murfreesboro, TN Contractor: Bear Construction LLC					Plant: Beaver Dam 6/9/2026 10:37:13 AM		Tech: S. Felletter PC: Erica Bradley				
Structure ID: R27											
P1 BX28280606VH			BOX BASE 6inW, 6inF, Variable Ht F/n								
P2) 28" x 28" - CASTING HEIGHT - 5" P1) 28" x 28" - BOX BASE 6inW, 6inF, Variable Ht F/n - 43" 1) 28" x 28" - STORM INVERT CHANNEL (FLAT) - 4" THK 1) CASTING - JBS 3104-V SINGLE SET 1) 28" x 28" - Conseal CS-102 1.00" 1) Hole - 26"					0 lb 3483 lb 450 lb 250 lb 0 lb 0 lb ----- 4183 lb Structure Total:		Structure Notes: 1. PER ASTM C913 SPECIFICATIONS. 2. CONCRETE = 4,000 PSI AT 28 DAYS. 3. CASTING BY ICAST (JBS-3104 SINGLE SET). REINFORCING PER ASTM A615 (GRADE 60). - WALLS (As .31) #5 BARS AT 12" C.C.E.W. - FLOOR (As .31) #5 BARS AT 12" C.C.E.W.				
Invert channel drawing 4" Thick flat storm invert											
Rim: 576.81' Rim to Invert: 3.83' Slack: 0.46" Sump: 2.5" Step Position:											
Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up (_)	Offset	
Invert 1	572.98'	0°	20"	18" RCP B WALL	23"	Hole 26	26"	26"	0"	0"	
Invert 2											
Invert 3											
Invert 4											
Invert 5											
Invert 6											
Invert 7											
Invert 8											
RIGHT-SIDE UP VIEW (int. dimensions) UPSIDE-DOWN VIEW (int. dimenions)											
 Invert: 1 Degree: 0 Horz: 14" Hole: 26" Up(_): 0"  Invert: 1 Degree: 0 Horz: 14" Hole: 26" Up(_): 0"											
INSIDE WALL DIMENSIONS  6" 43" EXT											
Coating (Int): Coating (Ext):			Seam Up: Flat Seam Dn: n/a		Wall Thickness: 6" Floor Height: 6"		Height (Int): 43" Height (Ext): 49"		Weight (Net): 3483 lb Volume (Net): 0.89cu.yd		
