



Job Name: 25-4490P1 Heartland Meadows Subdivision Job Location: Elizabethtown, KY 40165 Contractor: Kauffeld Brothers Construction					Plant: 100 7/23/2026 12:03:41 PM		Tech: Jared - A PC: Celina Goff			
Structure ID: MH 2-9 (10)										
P1 MH048BAVF		MH BASE Custom Ht								
P3) 24" - CASTING HEIGHT - 7" P2) 48" - MH FLAT TOP w/ 24" ECC Hole - 12" P1) 48" - MH BASE Custom Ht - 23" 1) 48" - MH INVERT CHANNEL - FULL HEIGHT 1) JOINT WRAP - 0.065"x6"x50' CONSEAL CS212 1) JOINT WRAP PRIMER - CONSEAL CS-75 (1 gal.) 1) CASTING - HOE MC-375 F/C Sanitary 1) 48" - Conseal CS-102 1.00" (Double) 1) 24" - Conseal CS-102 1.00" (Double) 1) PSX - 12-08 NYLO 2) PSX - 12-06 NYLO 1) MH Step ML-10-TDS-NCR - 10"					0 lb 1561 lb 2793 lb 1440 lb 0 lb 0 lb 271 lb 0 lb 0 lb 8 lb 16 lb 0 lb ----- Structure Total: 6089 lb		Structure Notes: 1. HOE MC-375 F/C "SANITARY" PROVIDED BY ICAST. 2. PER ASTM C478 SPECIFICATIONS. 3. CONCRETE = 4,000 PSI AT 28 DAYS. 4. REINFORCING PER ASTM A615 (GRADE 60). - TOP SLAB (As .62) #5 BARS AT 6" C.C.E.W.. - RISER/WALLS (As .12) - FLOOR (As .31) #5 BARS AT 12" C.C.E.W.			
Rim: 866.81' Rim to Invert: 3.41' Slack: 0.92' Sump: 2' Step Position: 187°										
Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up ()	Offset
Invert 1	863.4'	0°	0"	8" PVC SDR35	8.5"	PSX 12-08 NYLO	12"	12.129"	0"	0"
Invert 2	863.5'	108°	54.664"	6" PVC SDR35	6.25"	PSX 12-06 NYLO	12"	12.129"	0.2"	0"
Invert 3	863.5'	266°	134.635"	6" PVC SDR35	6.25"	PSX 12-06 NYLO	12"	12.129"	0.2"	0"
Invert 4										
Invert 5										
Invert 6										
Invert 7										
Invert 8										


RIGHT-SIDE UP VIEW (int. dimensions)

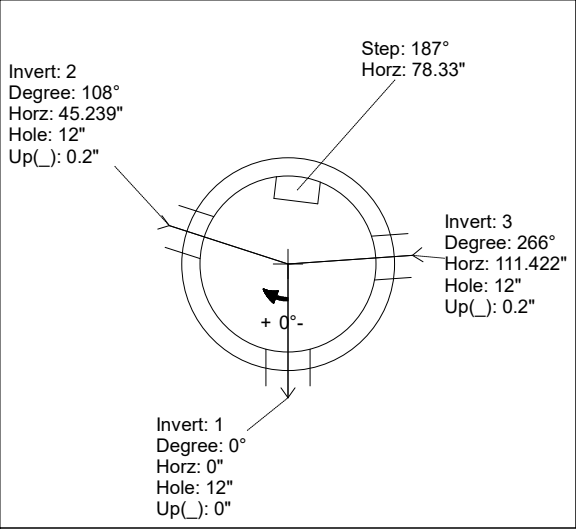


UPSIDE-DOWN VIEW (int. dimensions)

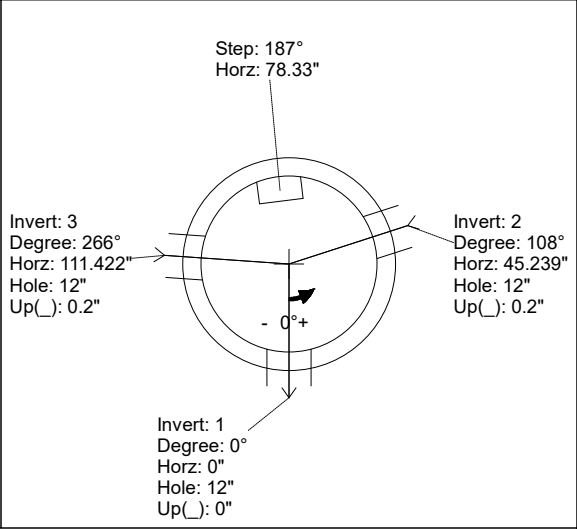

INSIDE WALL DIMENSIONS

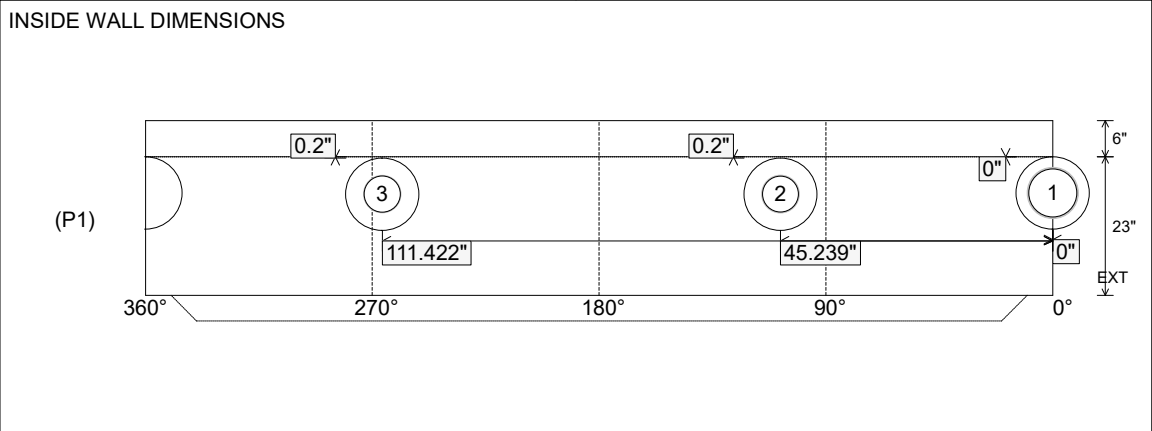

Coating (Int): Coating (Ext):	Seam Up: Tongue Seam Dn: n/a	Wall Thickness: 5" Floor Height: 6"	Height (Int): 23" Height (Ext): 29"	Weight (Net): 2793 lb Volume (Net): 0.71cu.yd
----------------------------------	---------------------------------	--	--	--



Weight (Net): 2793 lb
Volume (Net): 0.71cu.yd
