



Floor (Bot): 1020.333'
Overall Height: 8.583'
Slack: 1"


P4) 24" - CASTING HEIGHT - 7"	0 lb
P3) 48" - ECC CONE w/ 24" HOLE - 36"	3000 lb
P2) 48" - MH RISER - 24"	1677 lb
P1) 48" - MH BASE - 30"	3121 lb
1) JOINT WRAP - 0.065"x6"x50' CONSEAL CS212	0 lb
1) JOINT WRAP PRIMER - CONSEAL CS-75 (1 gal.)	0 lb
1) 48" - MH INVERT CHANNEL - FULL HEIGHT	1440 lb
2) 48" - Conseal CS-102 1.00" (Double)	0 lb
1) 24" - Conseal CS-102 1.00" (Double)	0 lb
3) PSX - 16M NYLO	24 lb
1) PSX - 12-08 NYLO	8 lb
6) MH Step ML-10-TDS-NCR - 10"	0 lb
Structure Total:	9269 lb

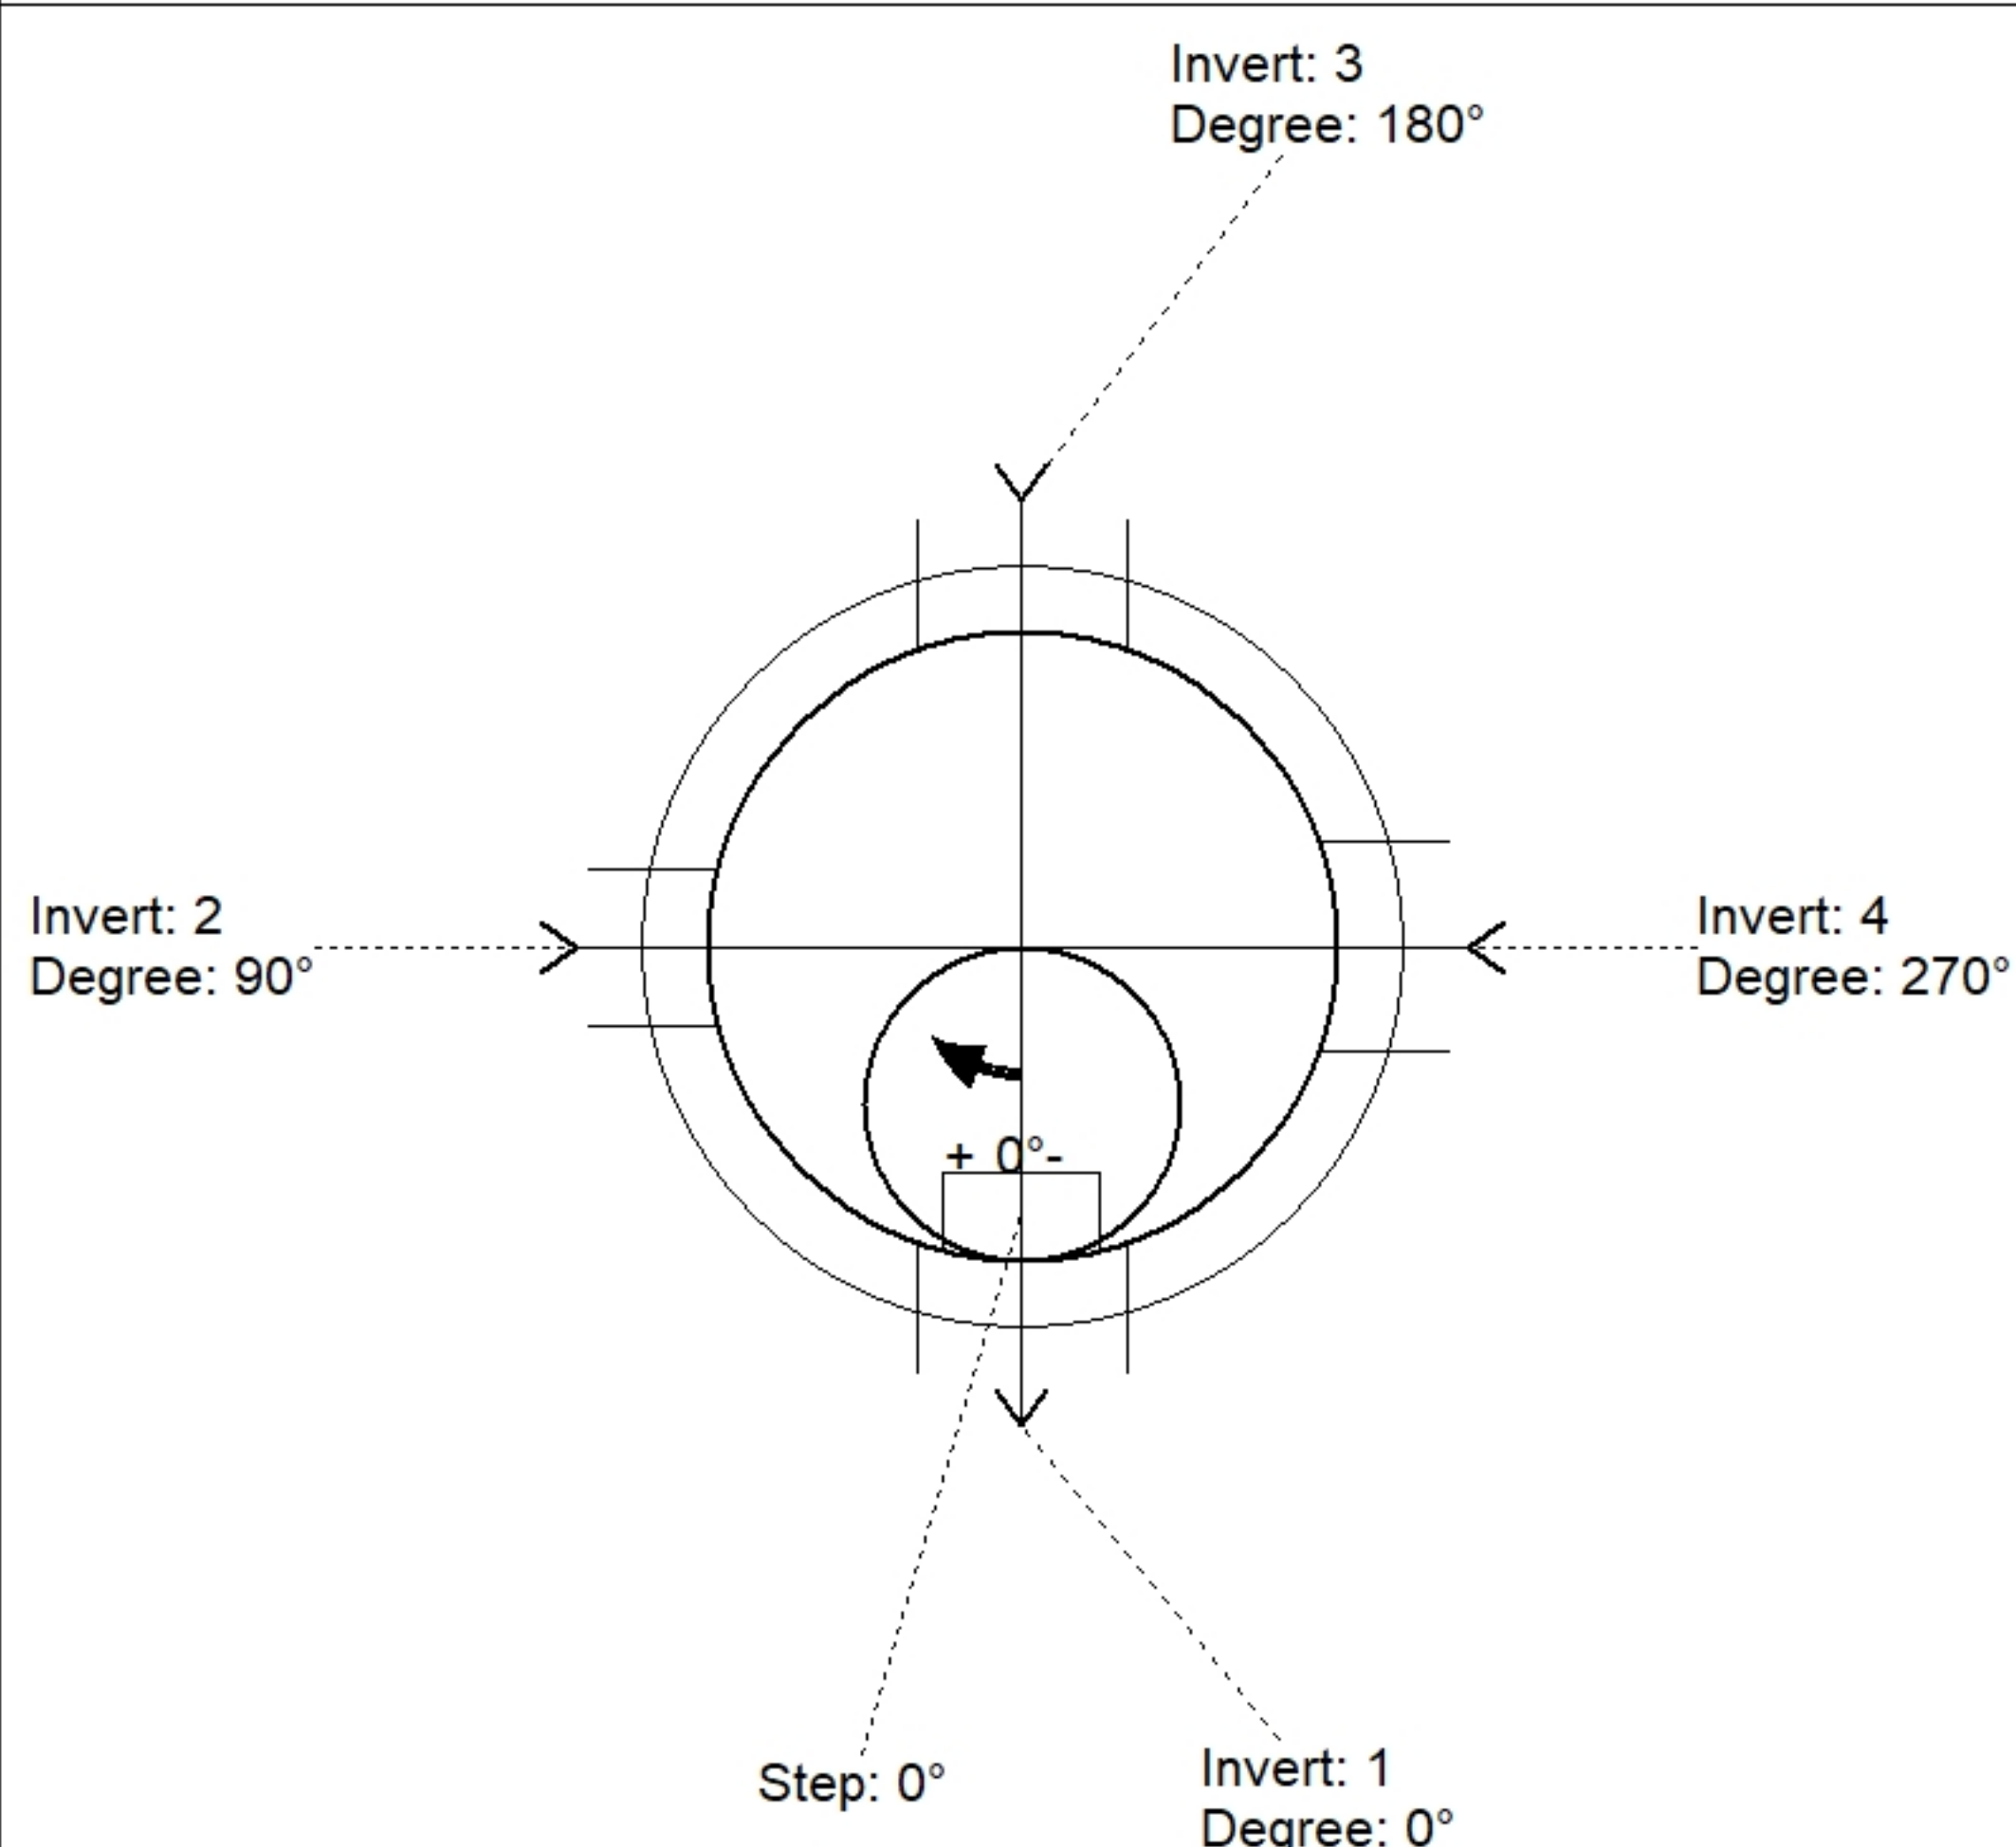

Position	Elev	Angle	Pipe	Pipe OD	Hole	Connector	Up (')	Rel
Rim	1029'							
Reducer								
Invert 1	1021'	0°	12" PVC SDR35	12.5"	16"	PSX 16M NYLO	0"	P1
Invert 2	1021.33'	90°	8" PVC SDR35	8.5"	12"	PSX 12-08 NYLO	3.96"	P1
Invert 3	1021.1'	180°	12" PVC SDR35	12.5"	16"	PSX 16M NYLO	1.2"	P1
Invert 4	1021.1'	270°	12" PVC SDR35	12.5"	16"	PSX 16M NYLO	1.2"	P1
Invert 5								
Invert 6								
Invert 7								
Invert 8								

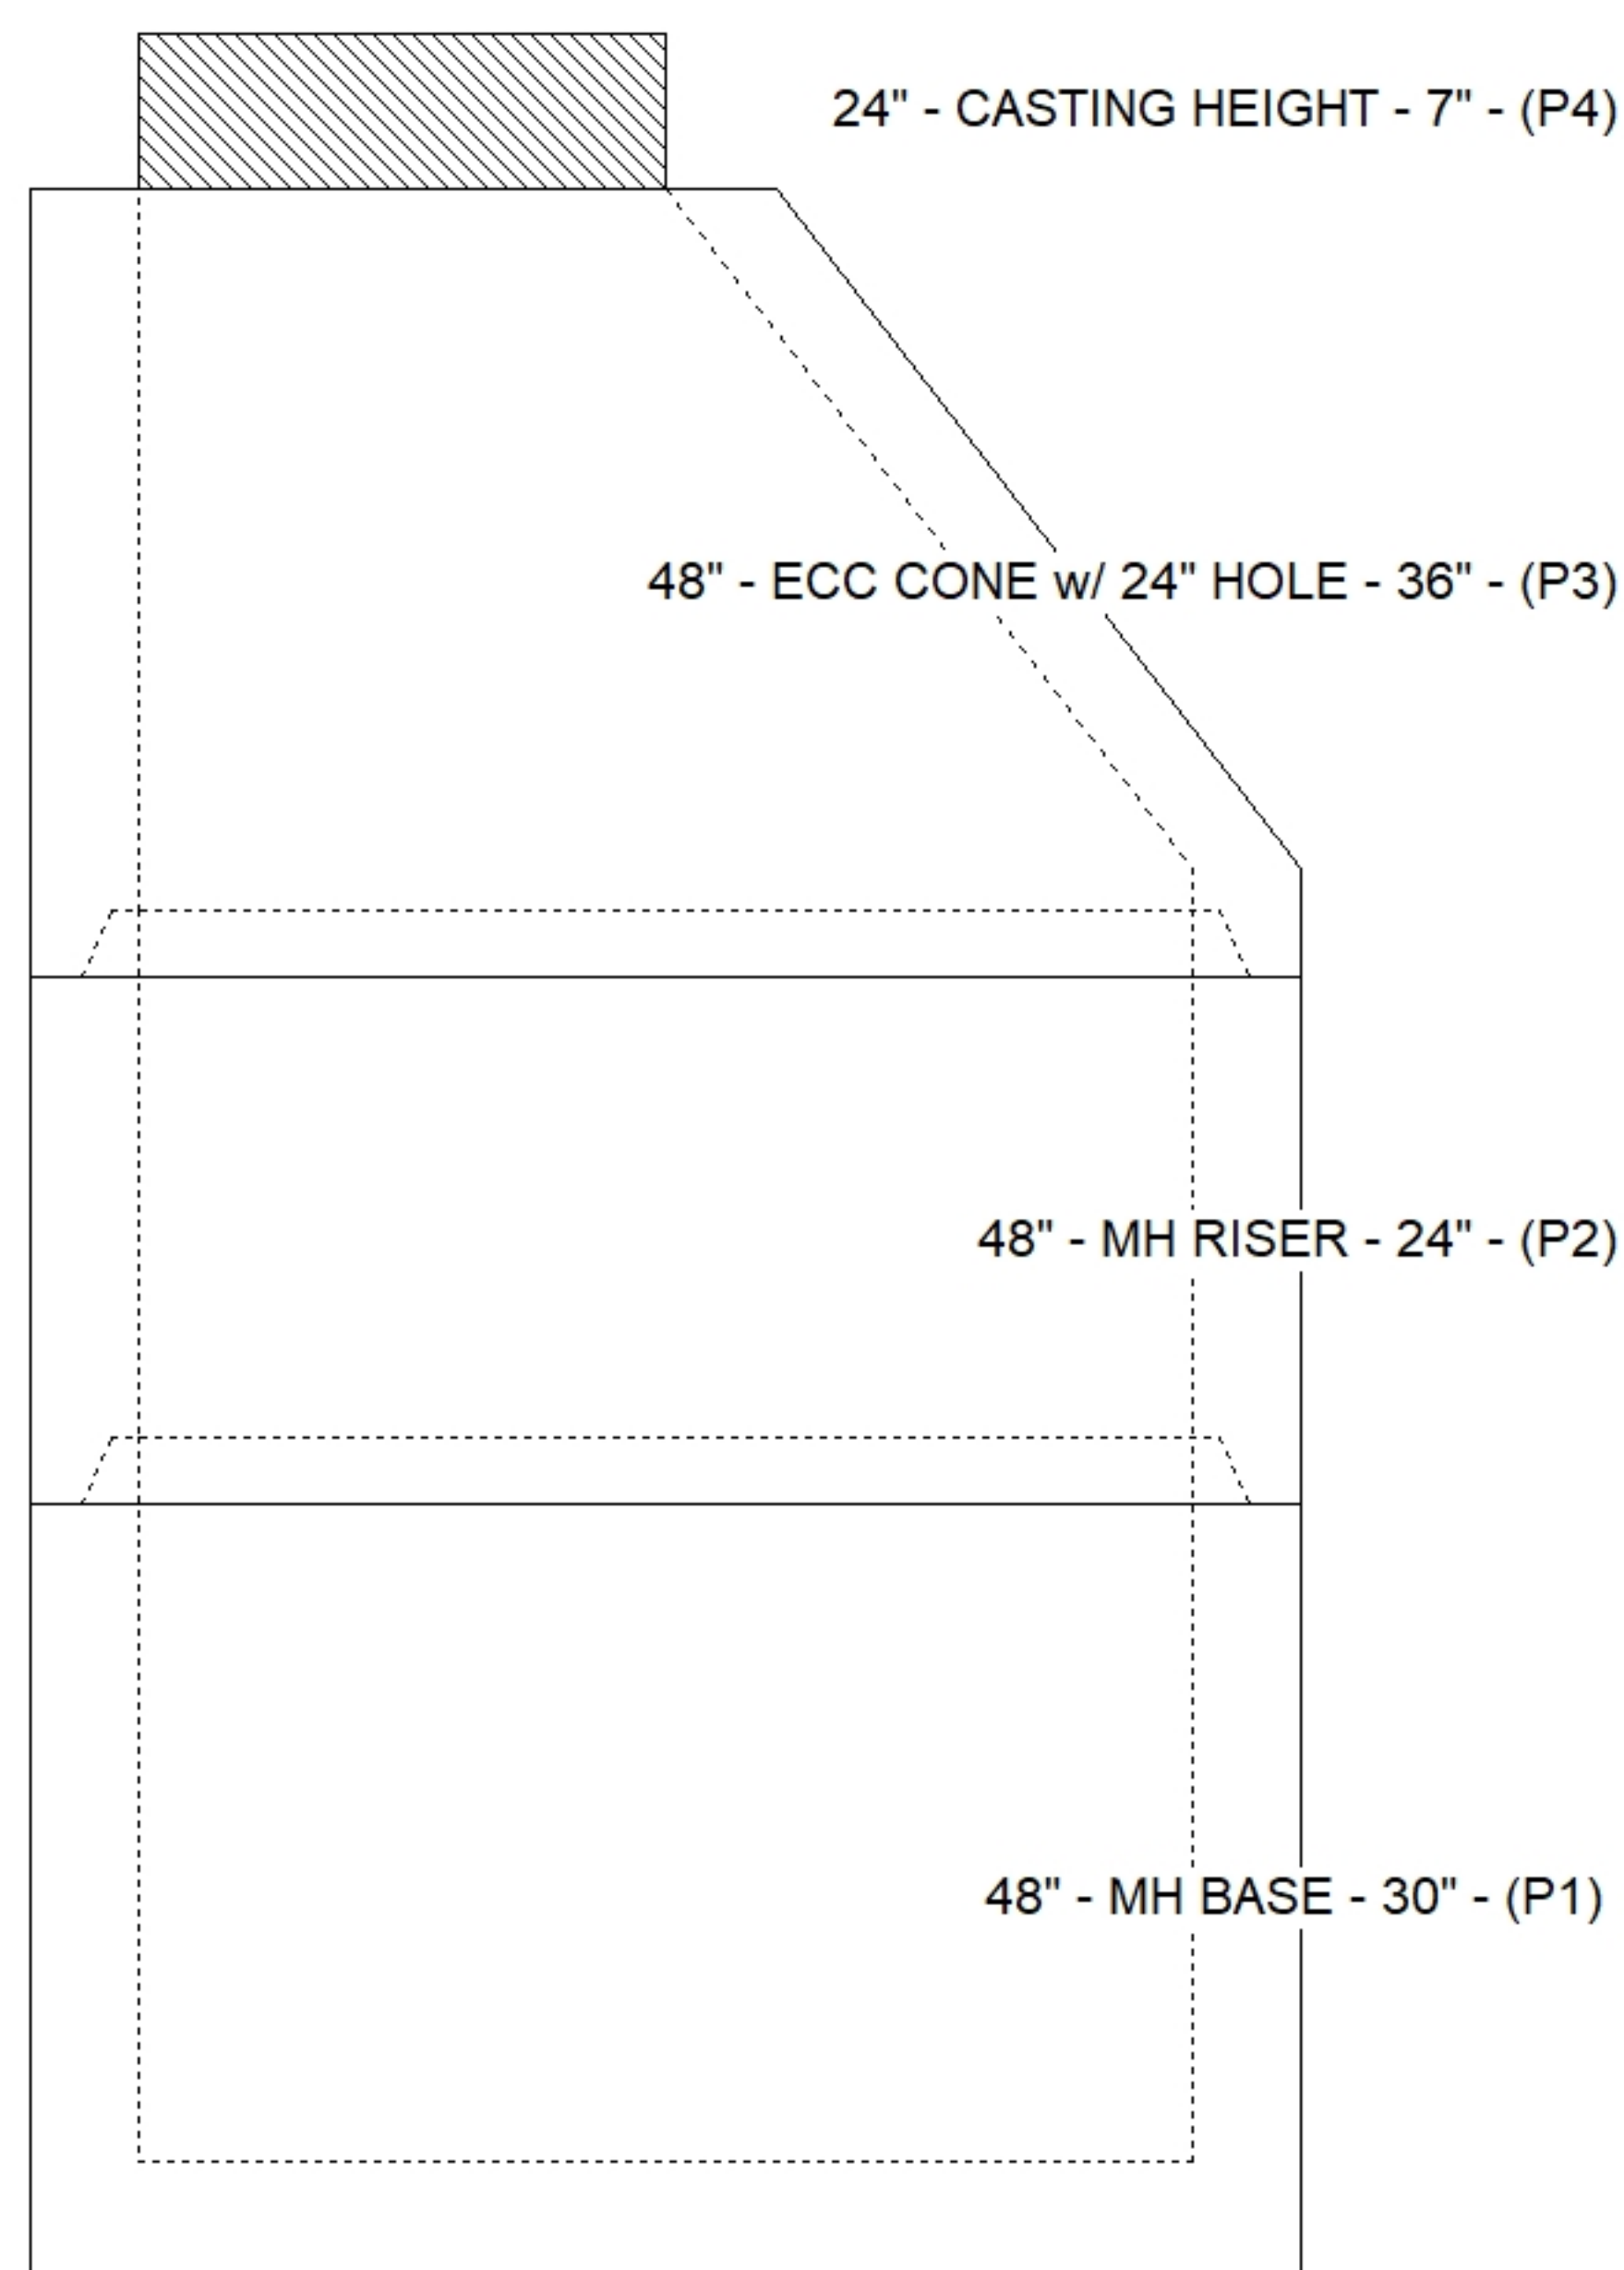

Default - Interior Dimensions

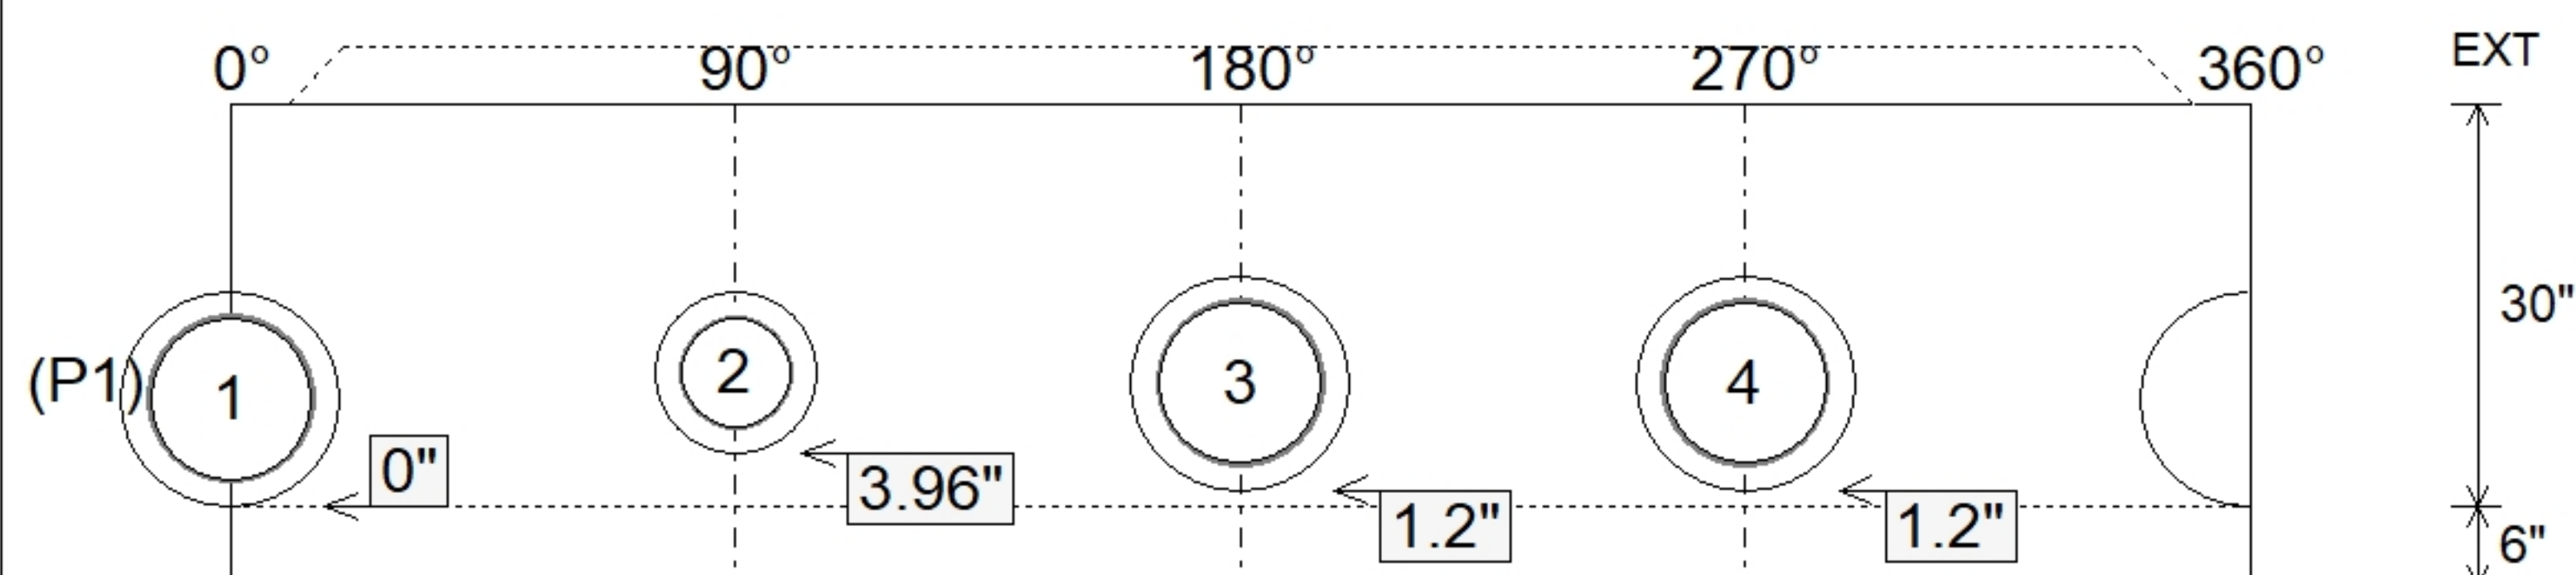

SUBMITTAL
APPROVED BY:
