

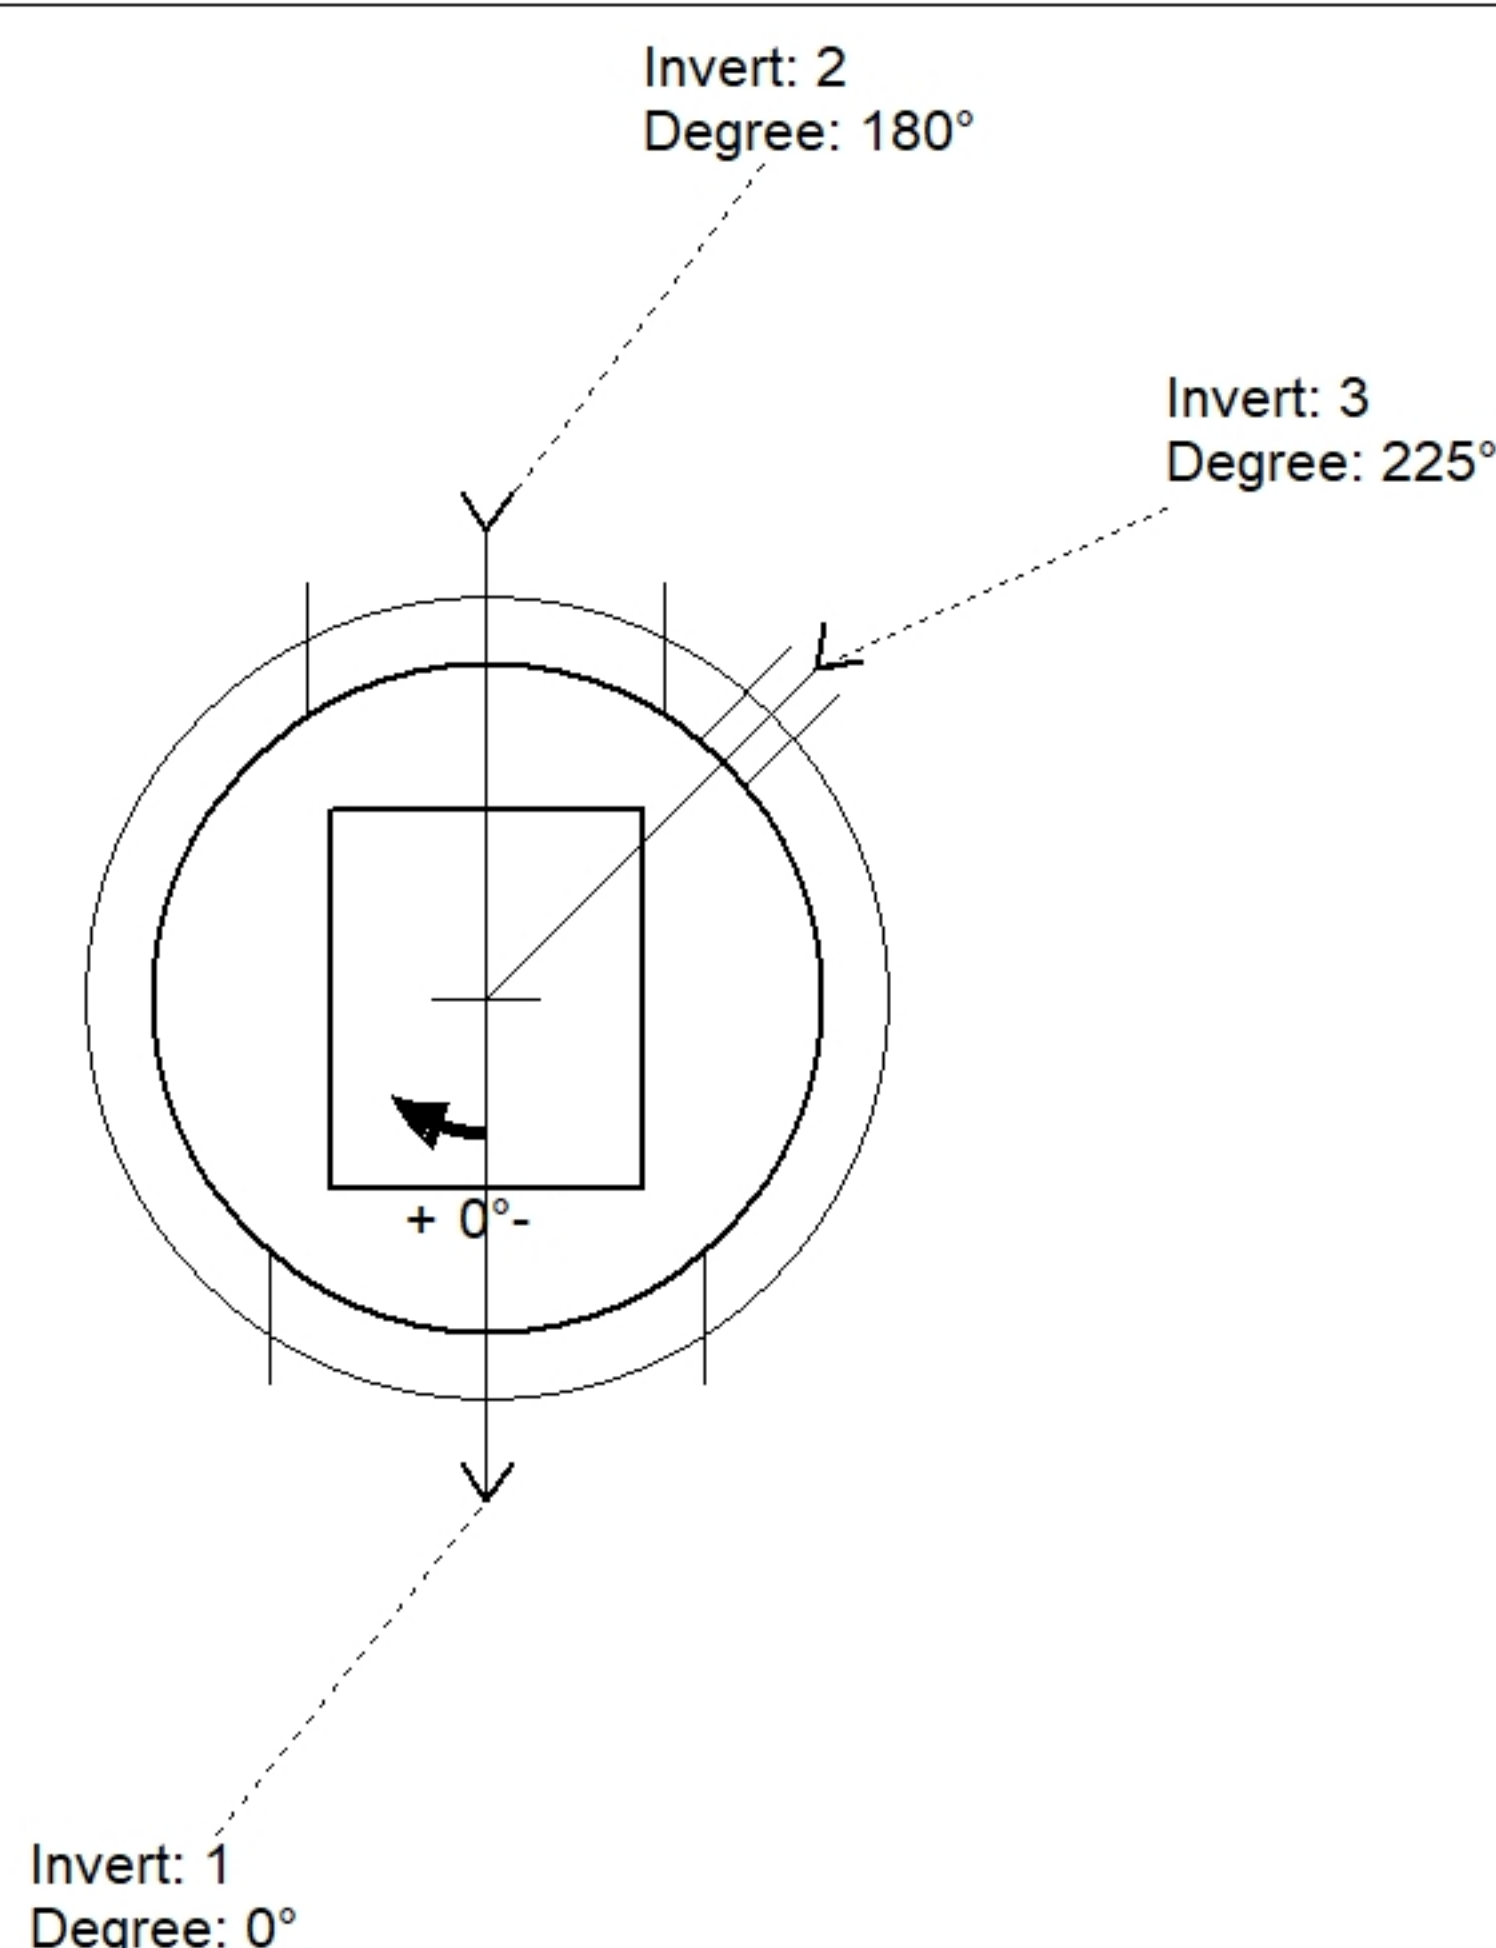


STRUCTURE SUMMARY:	
P3) 28" x 34" - CASTING HEIGHT - 7"	0 lb
P2) 60" - MH FLAT TOP - TDOT NO 12 (28"x34" Hole) - 10"	3417 lb
P1) 60" - MH BASE Custom Ht - 44"	6244 lb
1) CASTING - JBS-3123 MODIFIED SET	250 lb
1) 60" - Conseal CS-102 1.00"	0 lb
1) 28" x 34" - Conseal CS-102 1.00"	0 lb
1) Hole - 39	0 lb
1) Hole - 32	0 lb
1) Hole - 6	0 lb

Structure Total:	9911 lb

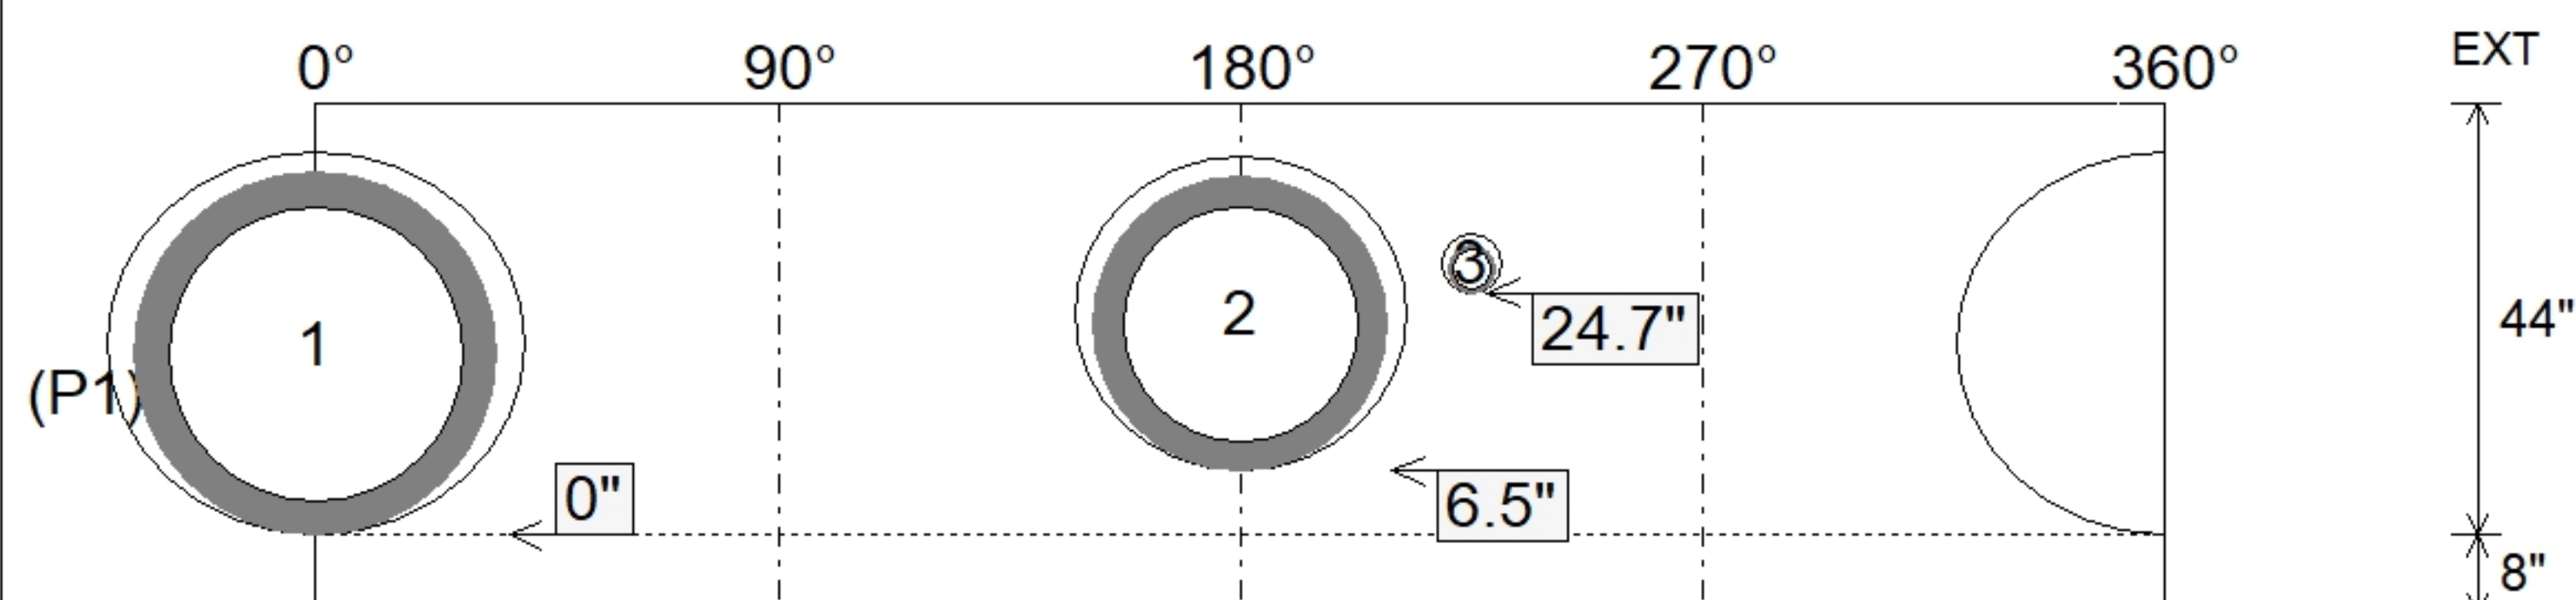

Position	Elev	Angle	Pipe	Pipe OD	Hole	Connector	Up (⌵)	Ref
Rim	796.4'							
Reducer								
Invert 1	791.6'	0°	30" RCP B WALL	37"	39"	Hole 39	0"	P1
Invert 2	792.1'	180°	24" RCP B WALL	30"	32"	Hole 32	6.5"	P1
Invert 3	793.4'	225°	4" HDPE (perf pipe)	4.8"	6"	Hole 6	24.7"	P1
Invert 4								
Invert 5								
Invert 6								
Invert 7								
Invert 8								

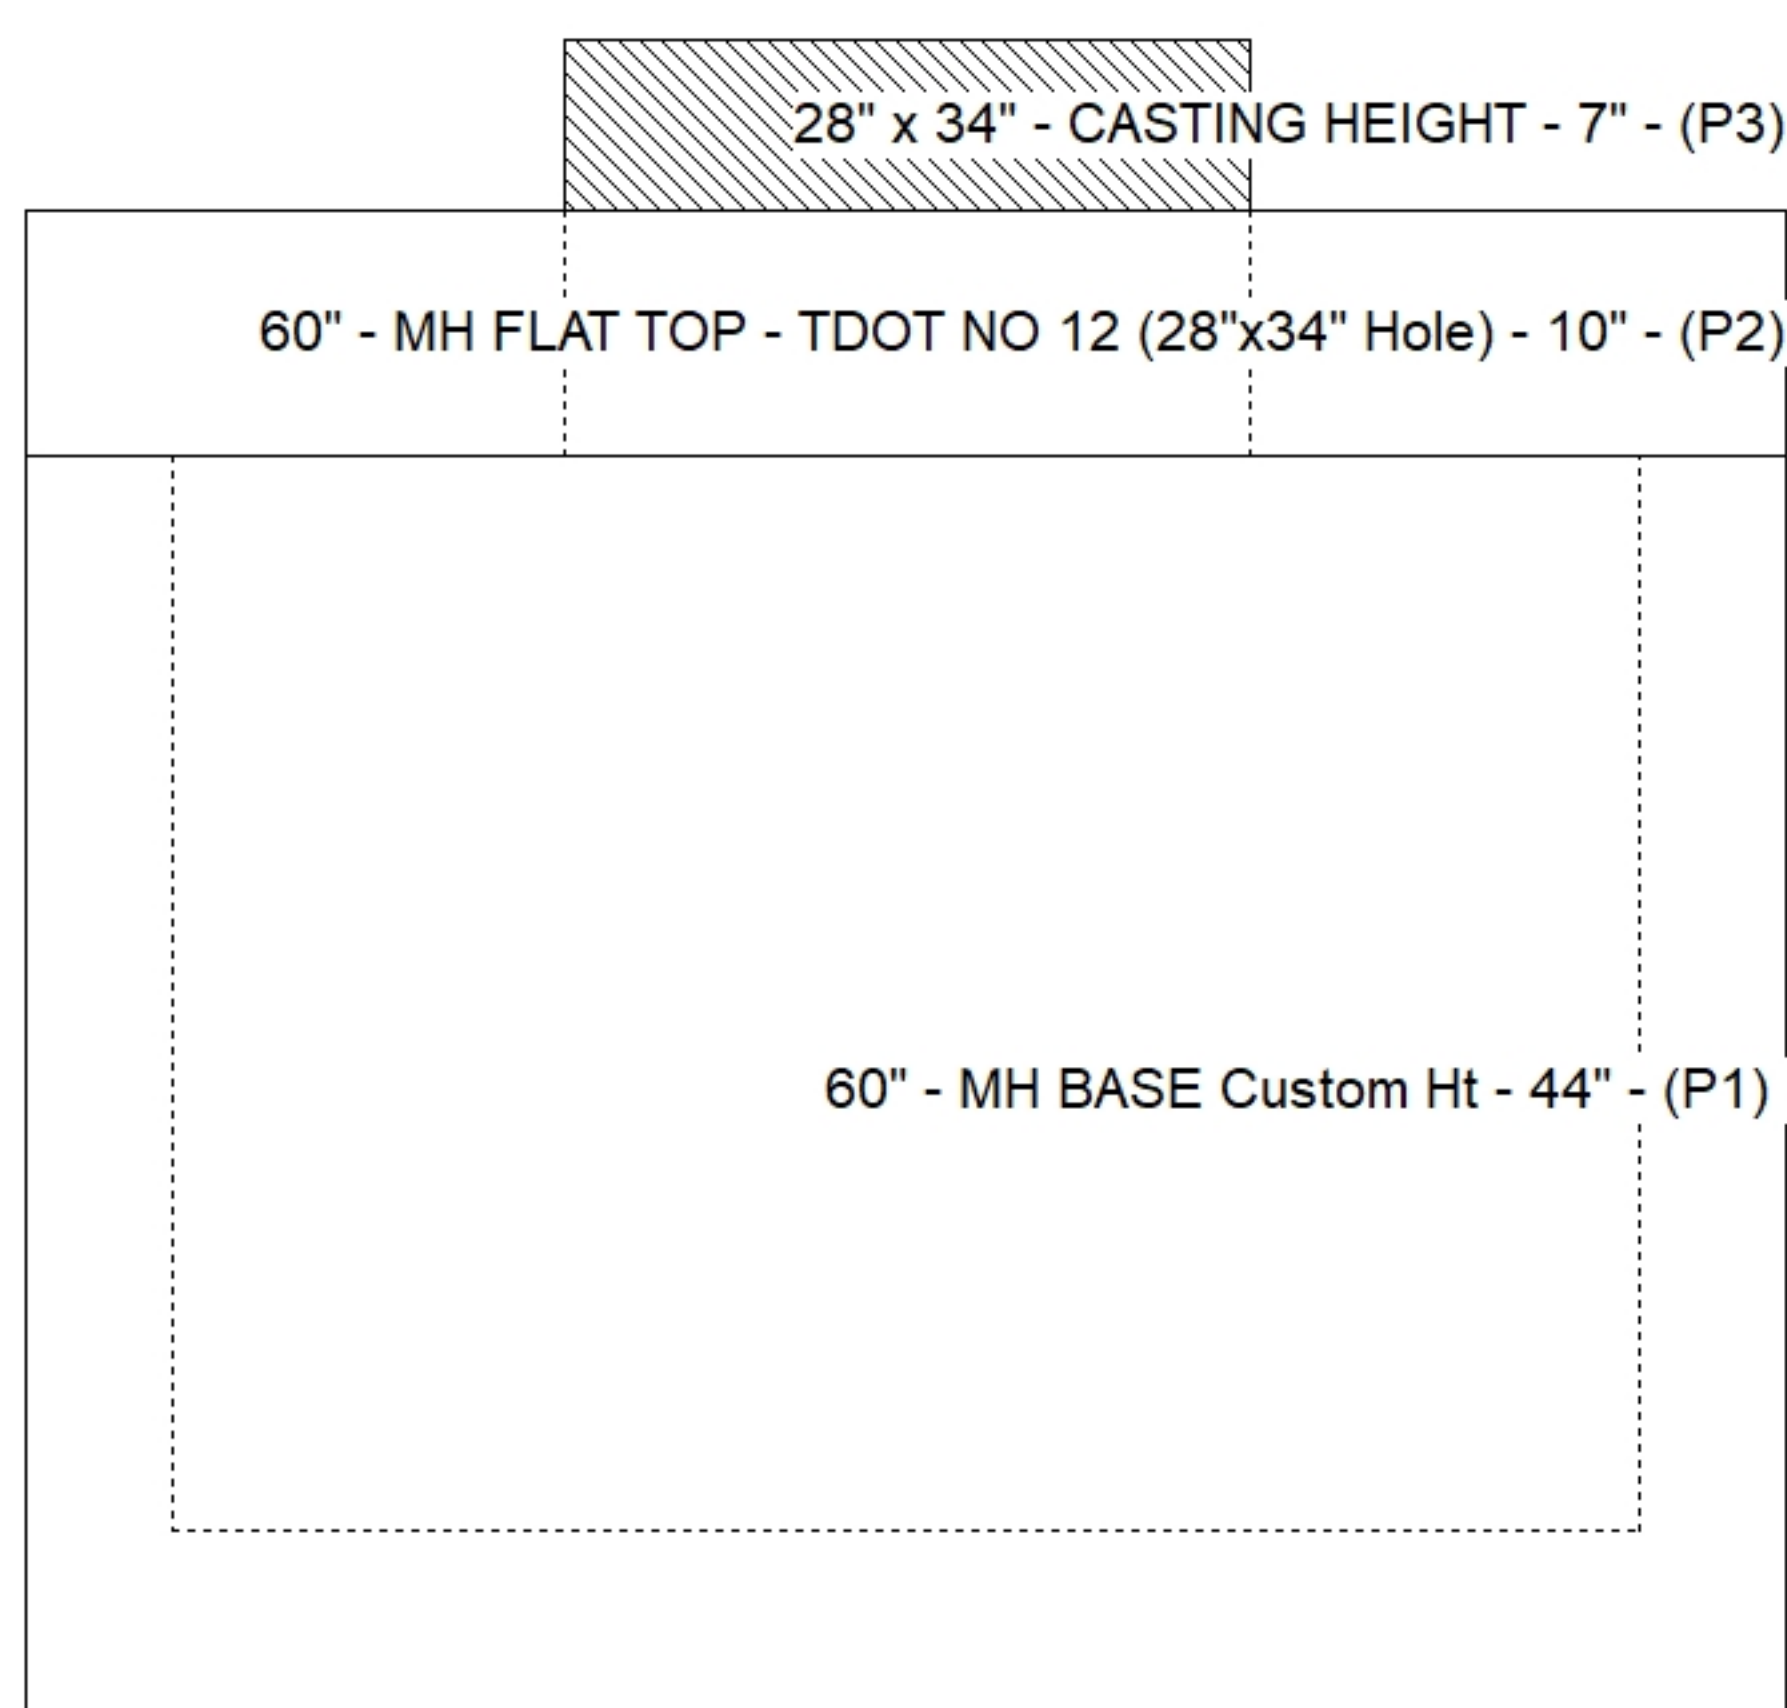

SUBMITTAL
APPROVED BY:
