






Floor (Bot): 706.513'  
Overall Height: 4.833'  
Slack: 0.52"

|                                                  |         |
|--------------------------------------------------|---------|
| P4) 24" - CASTING HEIGHT - 7"                    | 0 lb    |
| P3) 24" - XYPEX GRADE RING - 3"                  | 202 lb  |
| P2) 48" - ECC XYPEX CONE w/ 24" HOLE - 24"       | 1738 lb |
| P1) 48" - MH BASE w/XYPEX - 18"                  | 2492 lb |
| 1) JOINT WRAP - 0.065"x6"x50' CONSEAL CS212      | 0 lb    |
| 1) JOINT WRAP PRIMER - CONSEAL CS-75 (1 gal.)    | 0 lb    |
| 1) 48" - MH INVERT CHANNEL w/XYPEX - FULL HEIGHT | 1440 lb |
| 1) CASTING - JBS 1150 F/C SANITARY               | 250 lb  |
| 1) 48" - Conseal CS-102 1.00" (Double)           | 0 lb    |
| 2) 24" - Conseal CS-102 1.00" (Double)           | 0 lb    |
| 2) PSX - 12-08 NYLO                              | 16 lb   |
| 3) MH Step ML-10-TDS-NCR - 10"                   | 0 lb    |
| Structure Total:                                 | 6139 lb |

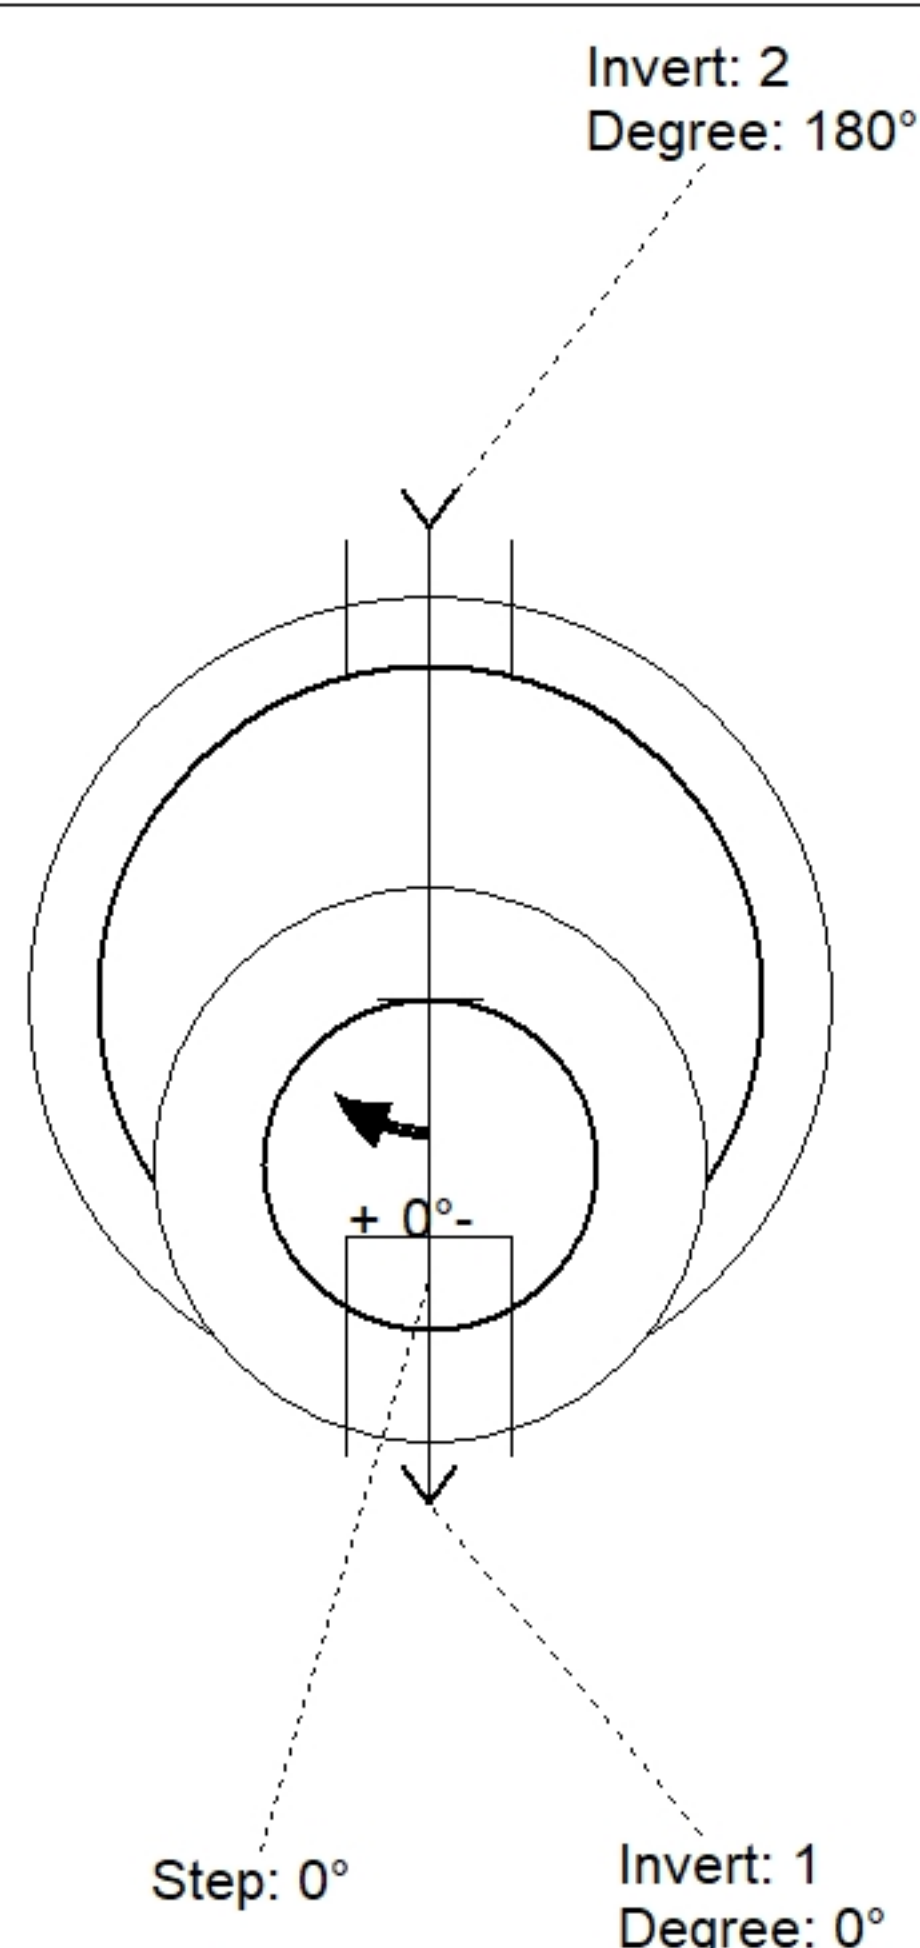

| Position | Elev    | Angle | Pipe         | Pipe OD | Hole | Connector      | Up (⌵) | Ref |
|----------|---------|-------|--------------|---------|------|----------------|--------|-----|
| Rim      | 711.39' |       |              |         |      |                |        |     |
| Reducer  |         |       |              |         |      |                |        |     |
| Invert 1 | 707.18' | 0°    | 8" PVC SDR35 | 8.5"    | 12"  | PSX 12-08 NYLO | 0"     | P1  |
| Invert 2 | 707.28' | 180°  | 8" PVC SDR35 | 8.5"    | 12"  | PSX 12-08 NYLO | 1.2"   | P1  |
| Invert 3 |         |       |              |         |      |                |        |     |
| Invert 4 |         |       |              |         |      |                |        |     |
| Invert 5 |         |       |              |         |      |                |        |     |
| Invert 6 |         |       |              |         |      |                |        |     |
| Invert 7 |         |       |              |         |      |                |        |     |
| Invert 8 |         |       |              |         |      |                |        |     |

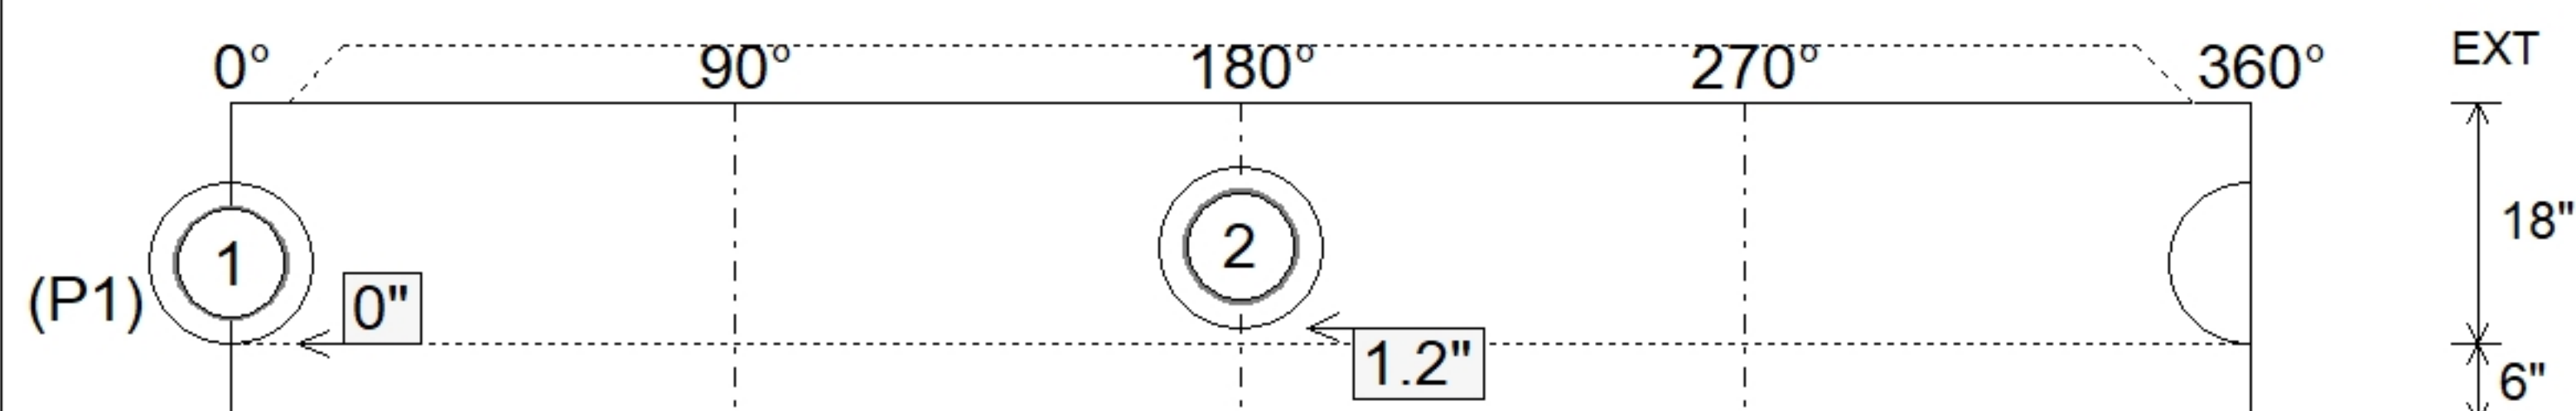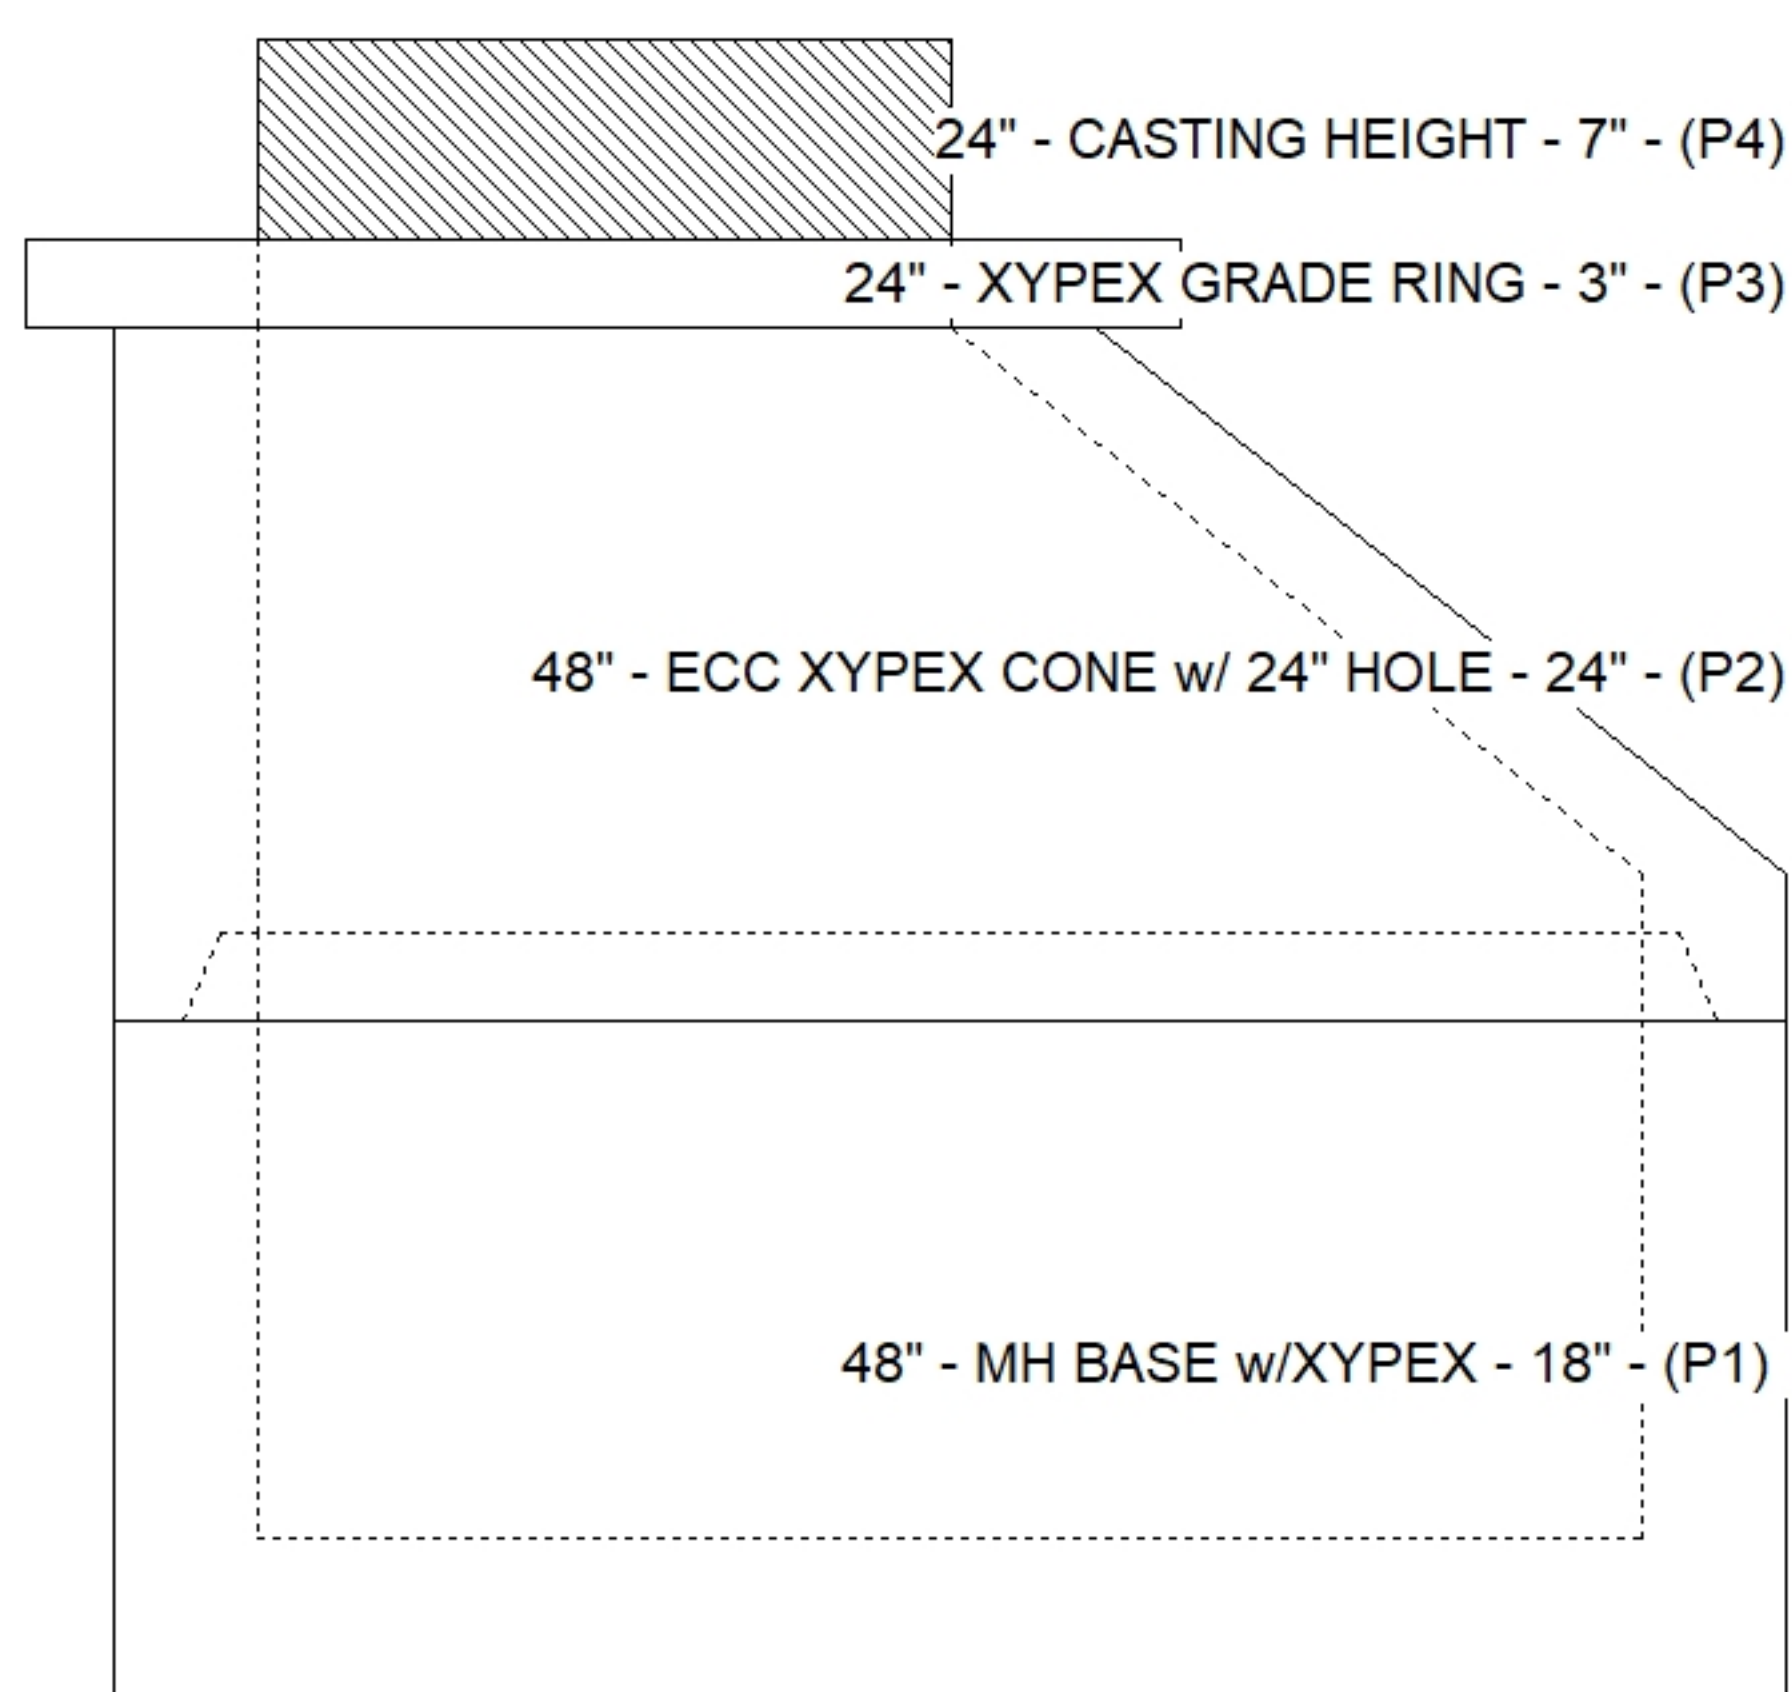

SUBMITTAL  
APPROVED BY:
