



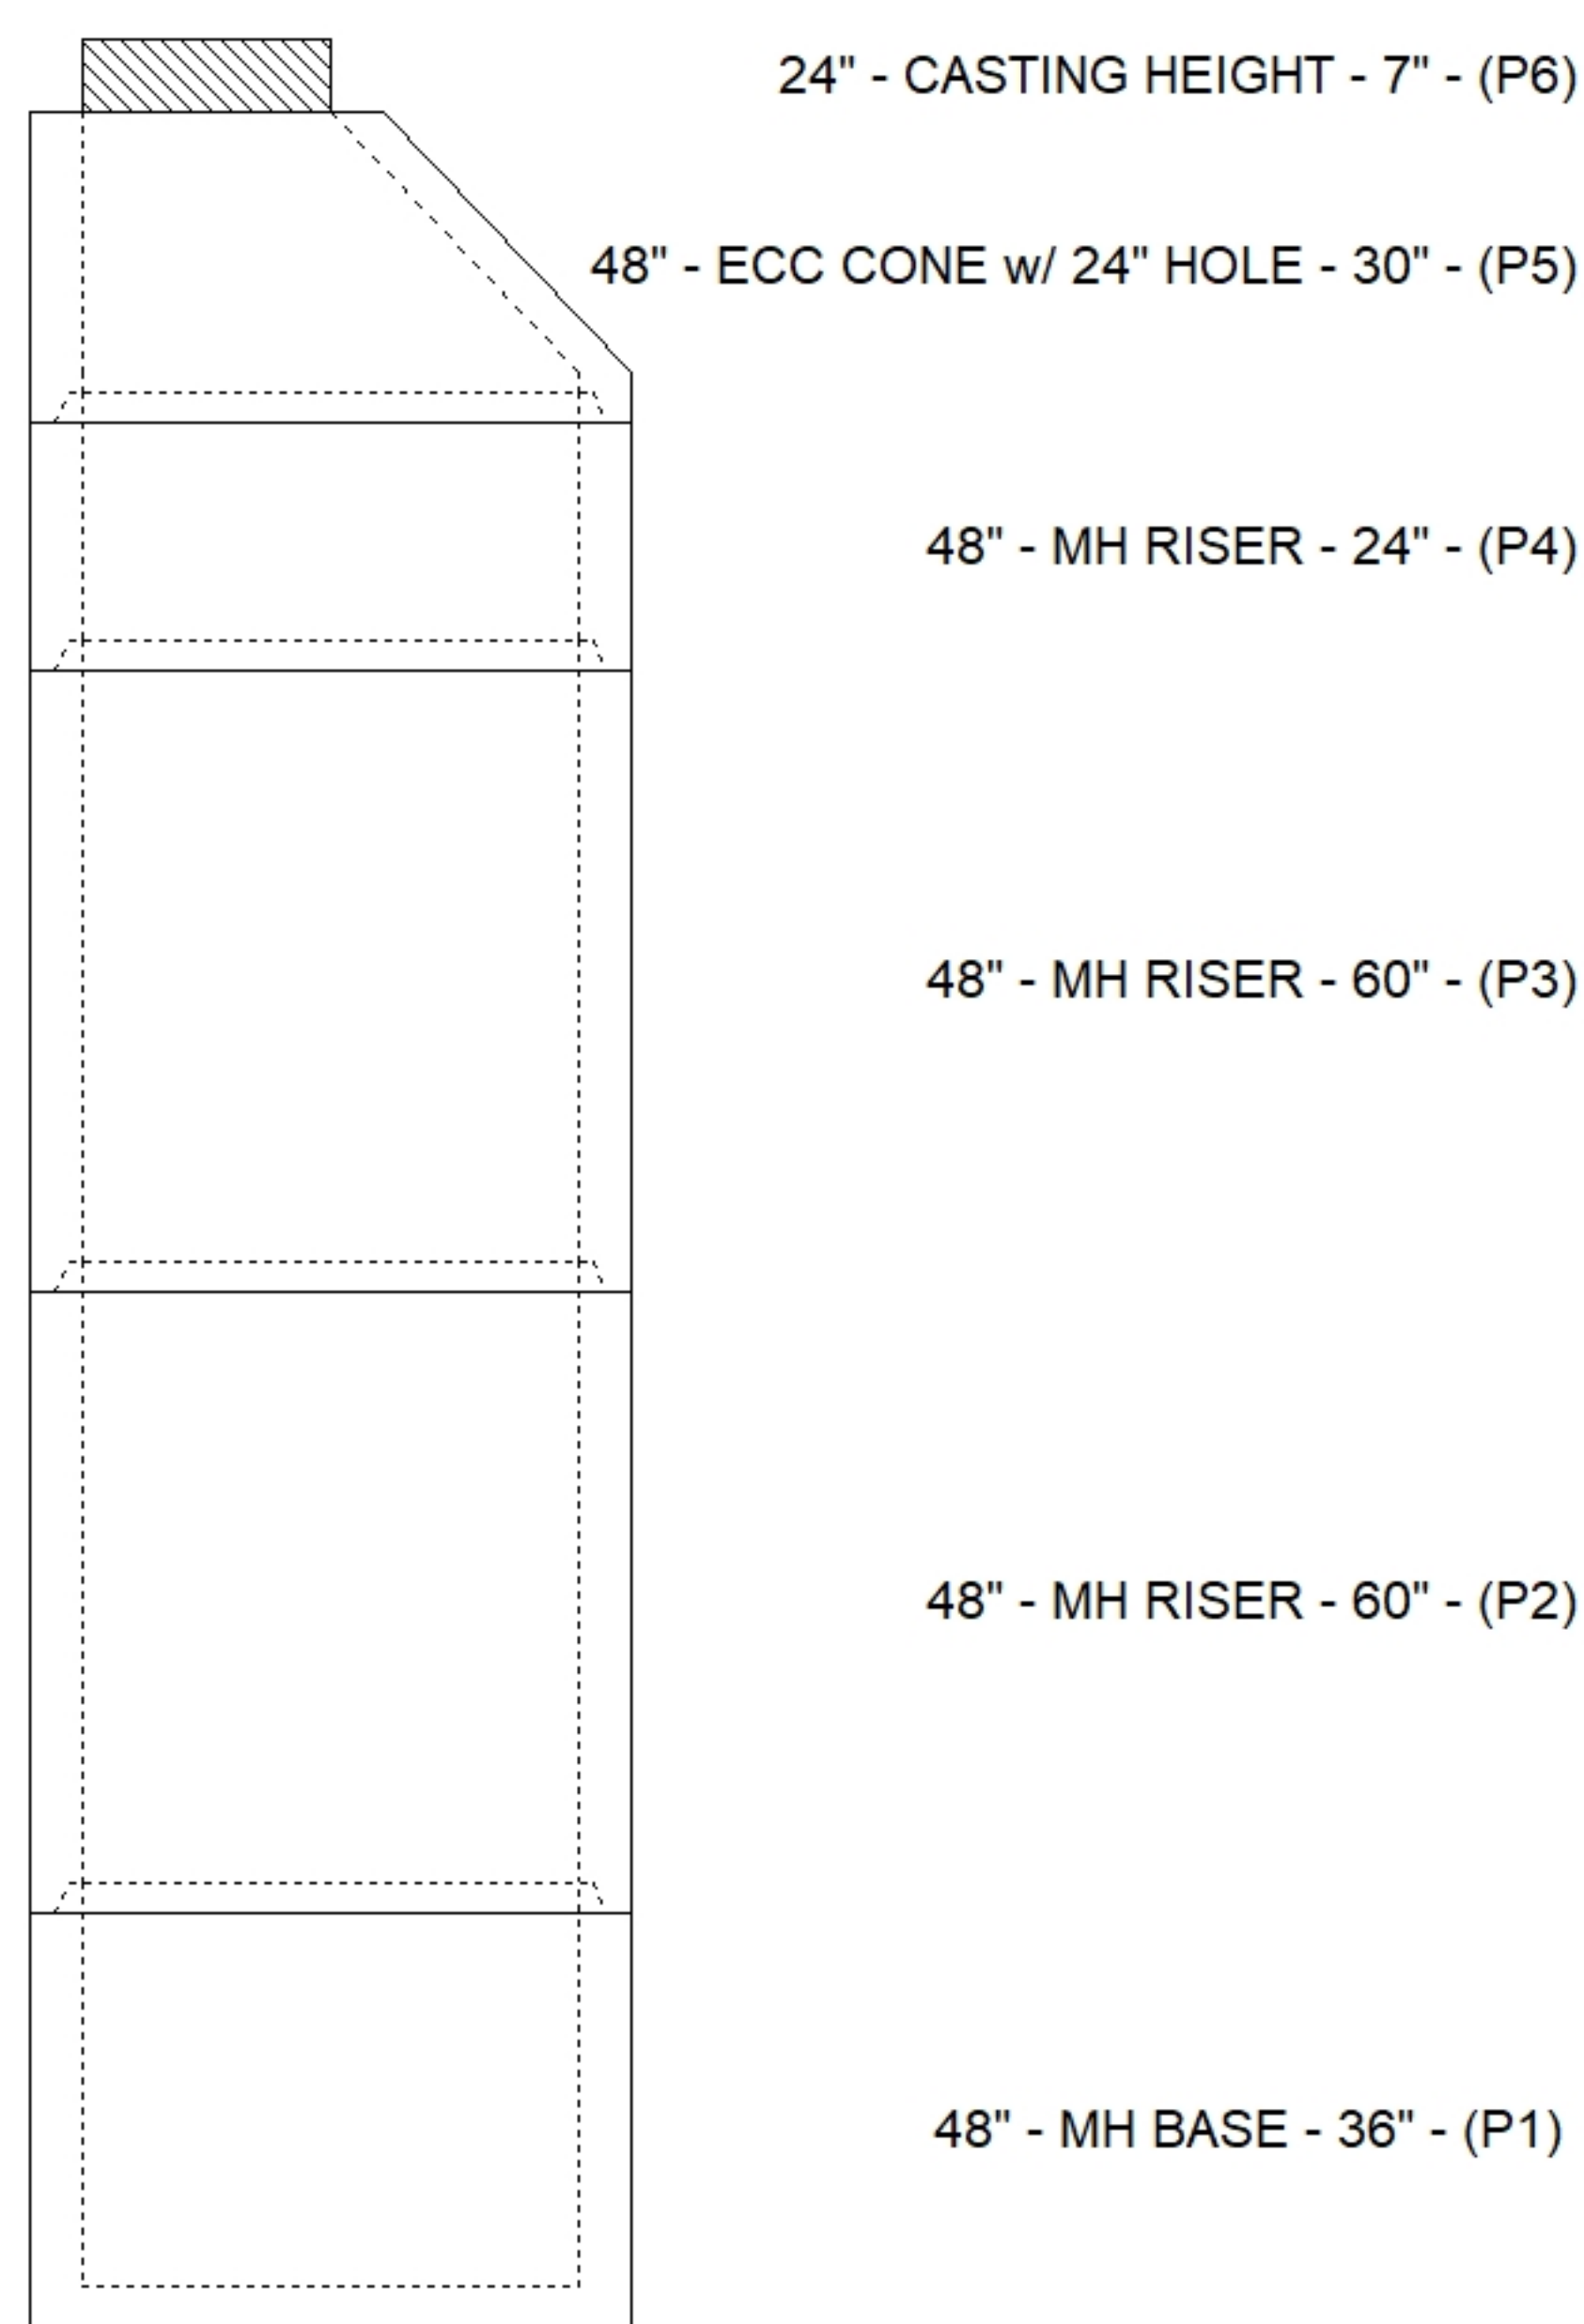

Floor (Bot): 414.463'
Overall Height: 18.583'
Slack: 2.8"


P6) 24" - CASTING HEIGHT - 7"	0 lb
P5) 48" - ECC CONE w/ 24" HOLE - 30"	2050 lb
P4) 48" - MH RISER - 24"	1677 lb
P3) 48" - MH RISER - 60"	4192 lb
P2) 48" - MH RISER - 60"	4192 lb
P1) 48" - MH BASE - 36"	3516 lb
1) Chimney Seal - Cretex Chimney Seal	10 lb
1) JOINT WRAP - 0.065"x6"x50' CONSEAL CS212	0 lb
1) JOINT WRAP PRIMER - CONSEAL CS-75 (1 gal.)	0 lb
1) 48" - MH INVERT CHANNEL - FULL HEIGHT	1440 lb
1) CASTING - HOE MC-375 F/C Sanitary	271 lb
4) 48" - Conseal CS-102 1.00" (Double)	0 lb
1) 24" - Conseal CS-102 1.00" (Double)	0 lb
2) Kor-N-Seal2 - S206-22	13 lb
16) MH Step ML-10-TDS-NCR - 10"	0 lb

Structure Total:	17359 lb

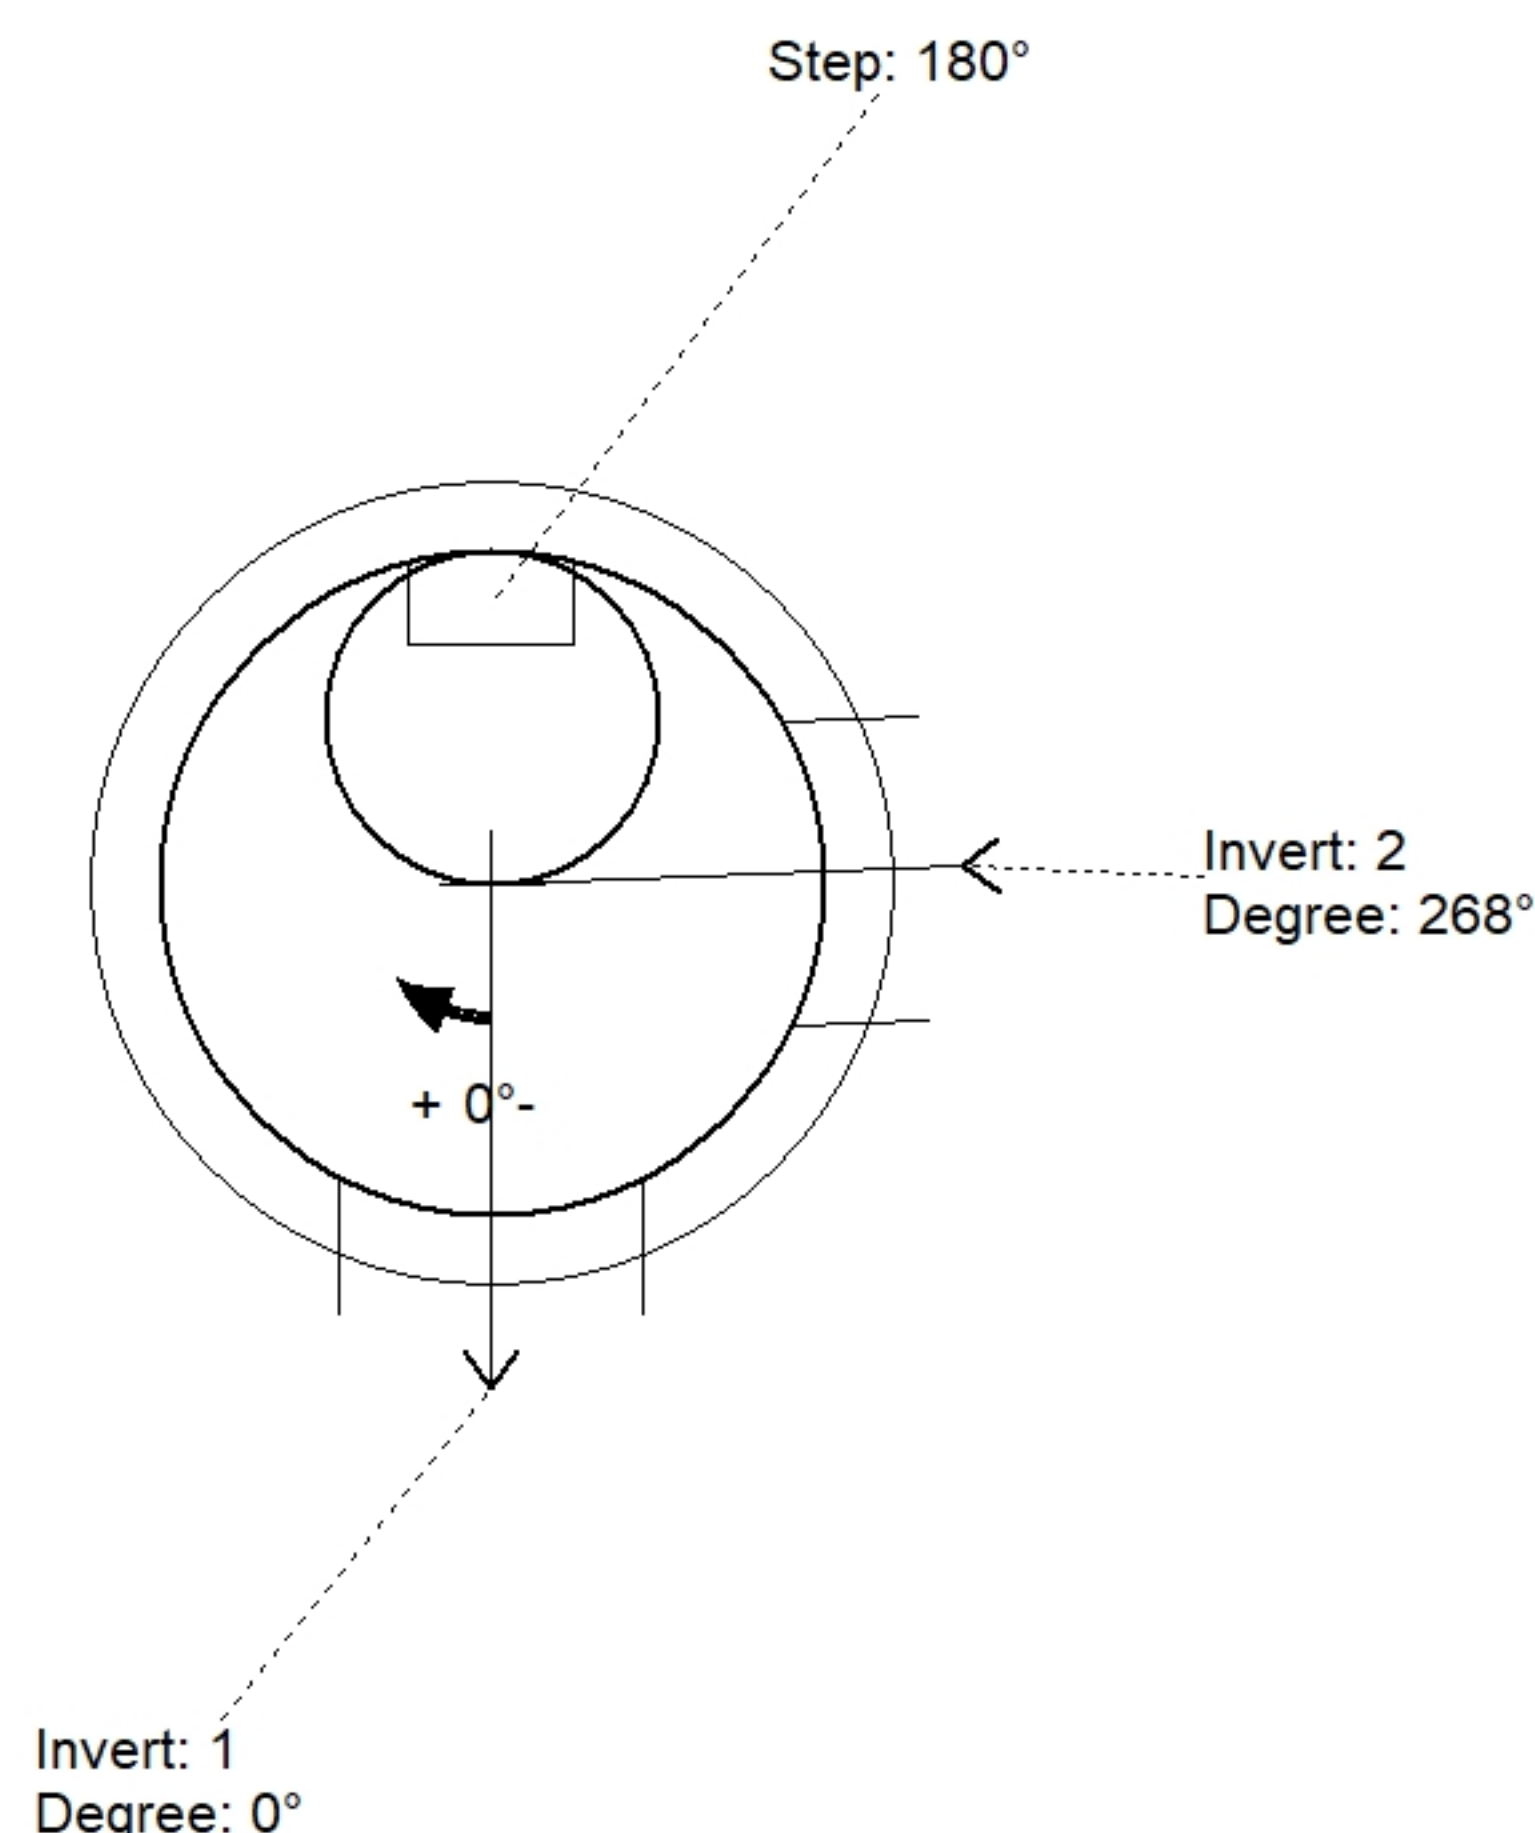

Position	Elev	Angle	Pipe	Pipe OD	Hole	Connector	Up ()	Ref
Rim	433.28'							
Reducer								
Invert 1	415.13'	0°	18" PVC F679	18.701"	22"	Kor-N-Seal2 S206-22	0"	P1
Invert 2	415.23'	268°	18" PVC F679	18.701"	22"	Kor-N-Seal2 S206-22	1.2"	P1
Invert 3								
Invert 4								
Invert 5								
Invert 6								
Invert 7								
Invert 8								

Default - Interior Dimensions

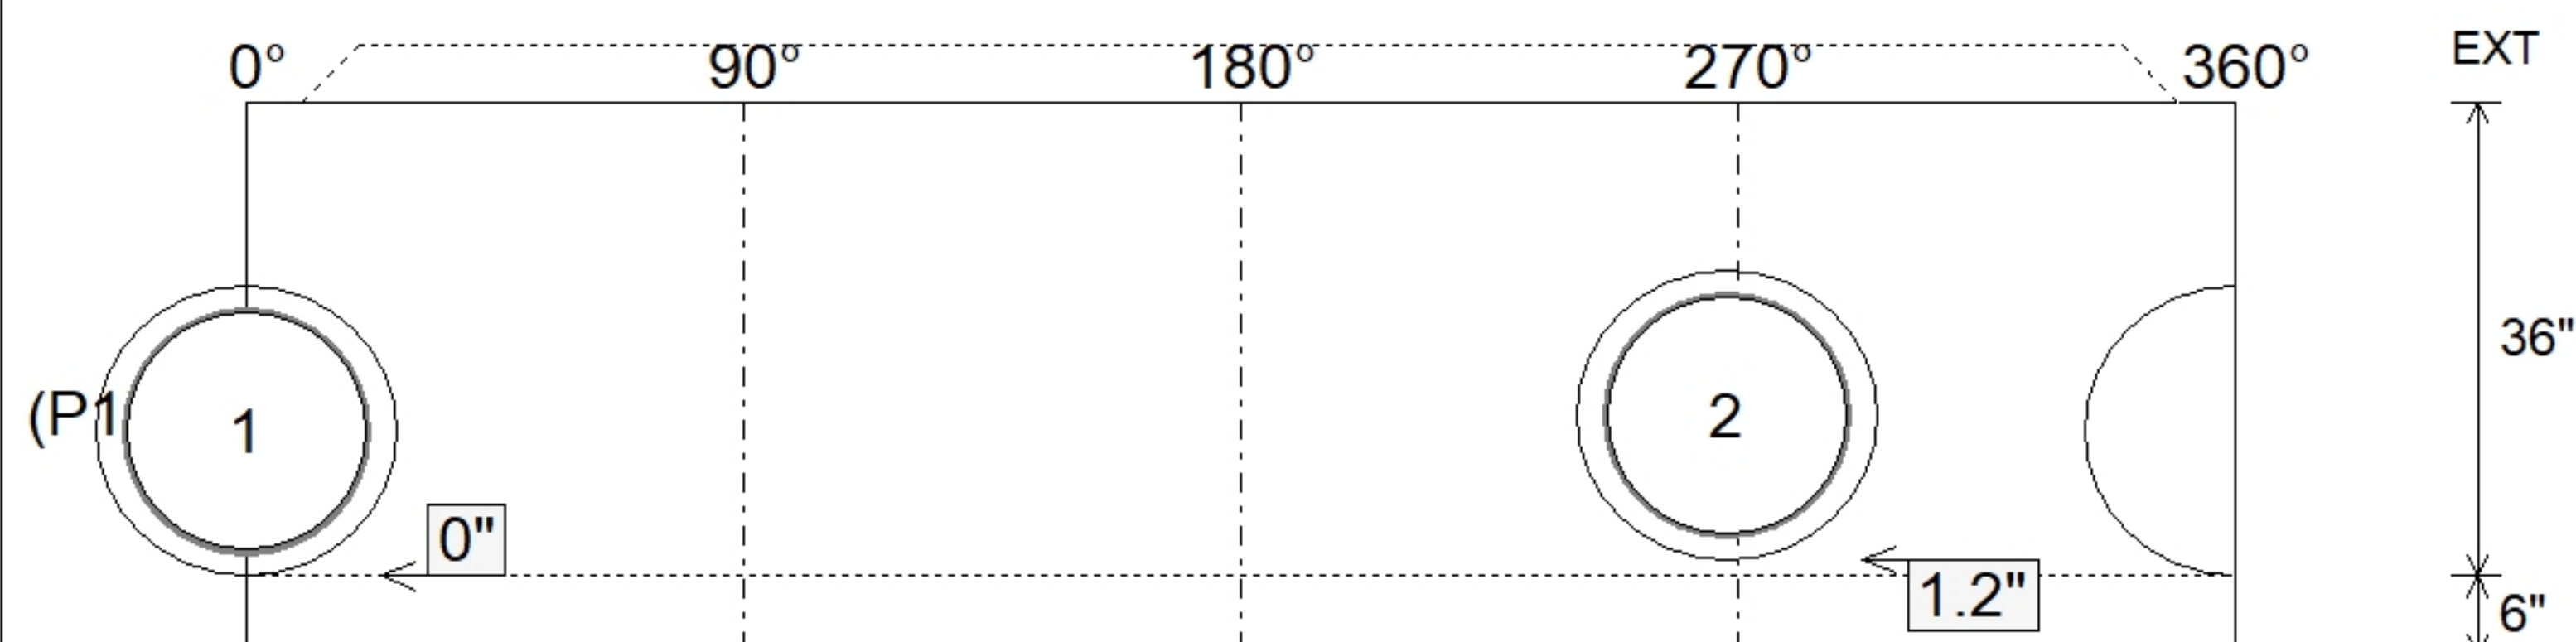

SUBMITTAL
APPROVED BY:
