



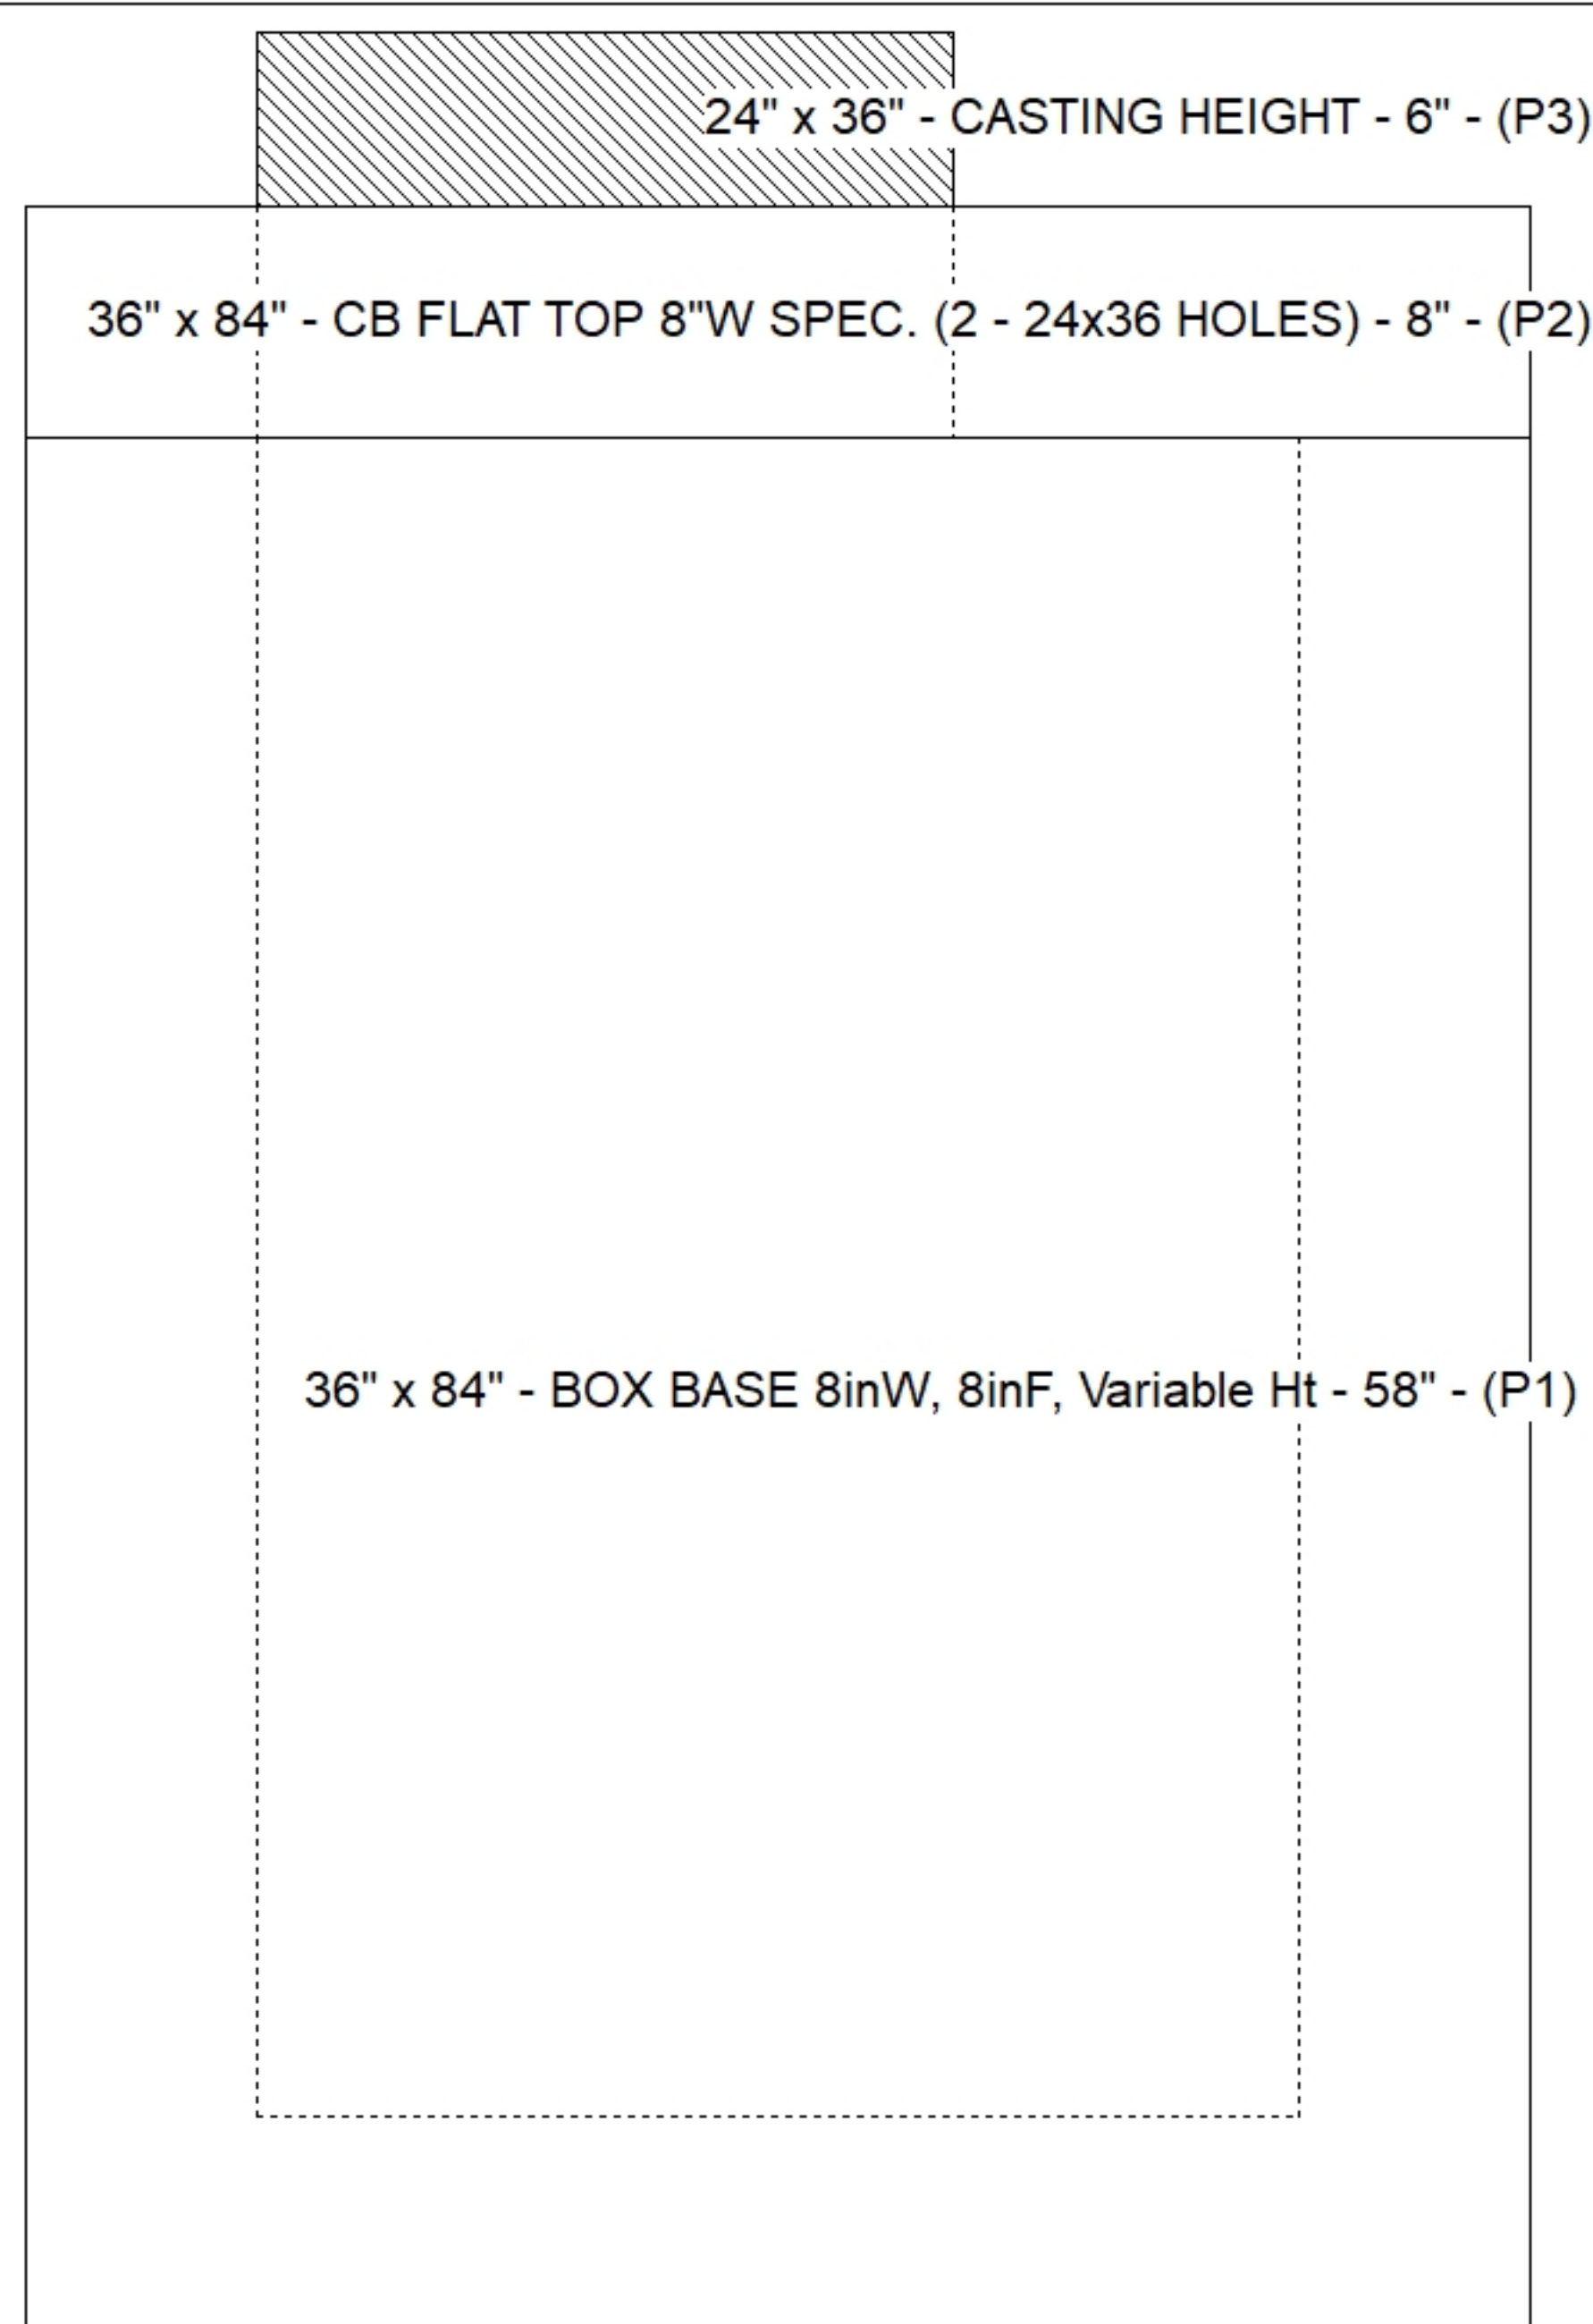


Floor (Bot): 680.523'
Overall Height: 6.667'
Slack: 0"

Structure Total: 14964 lb

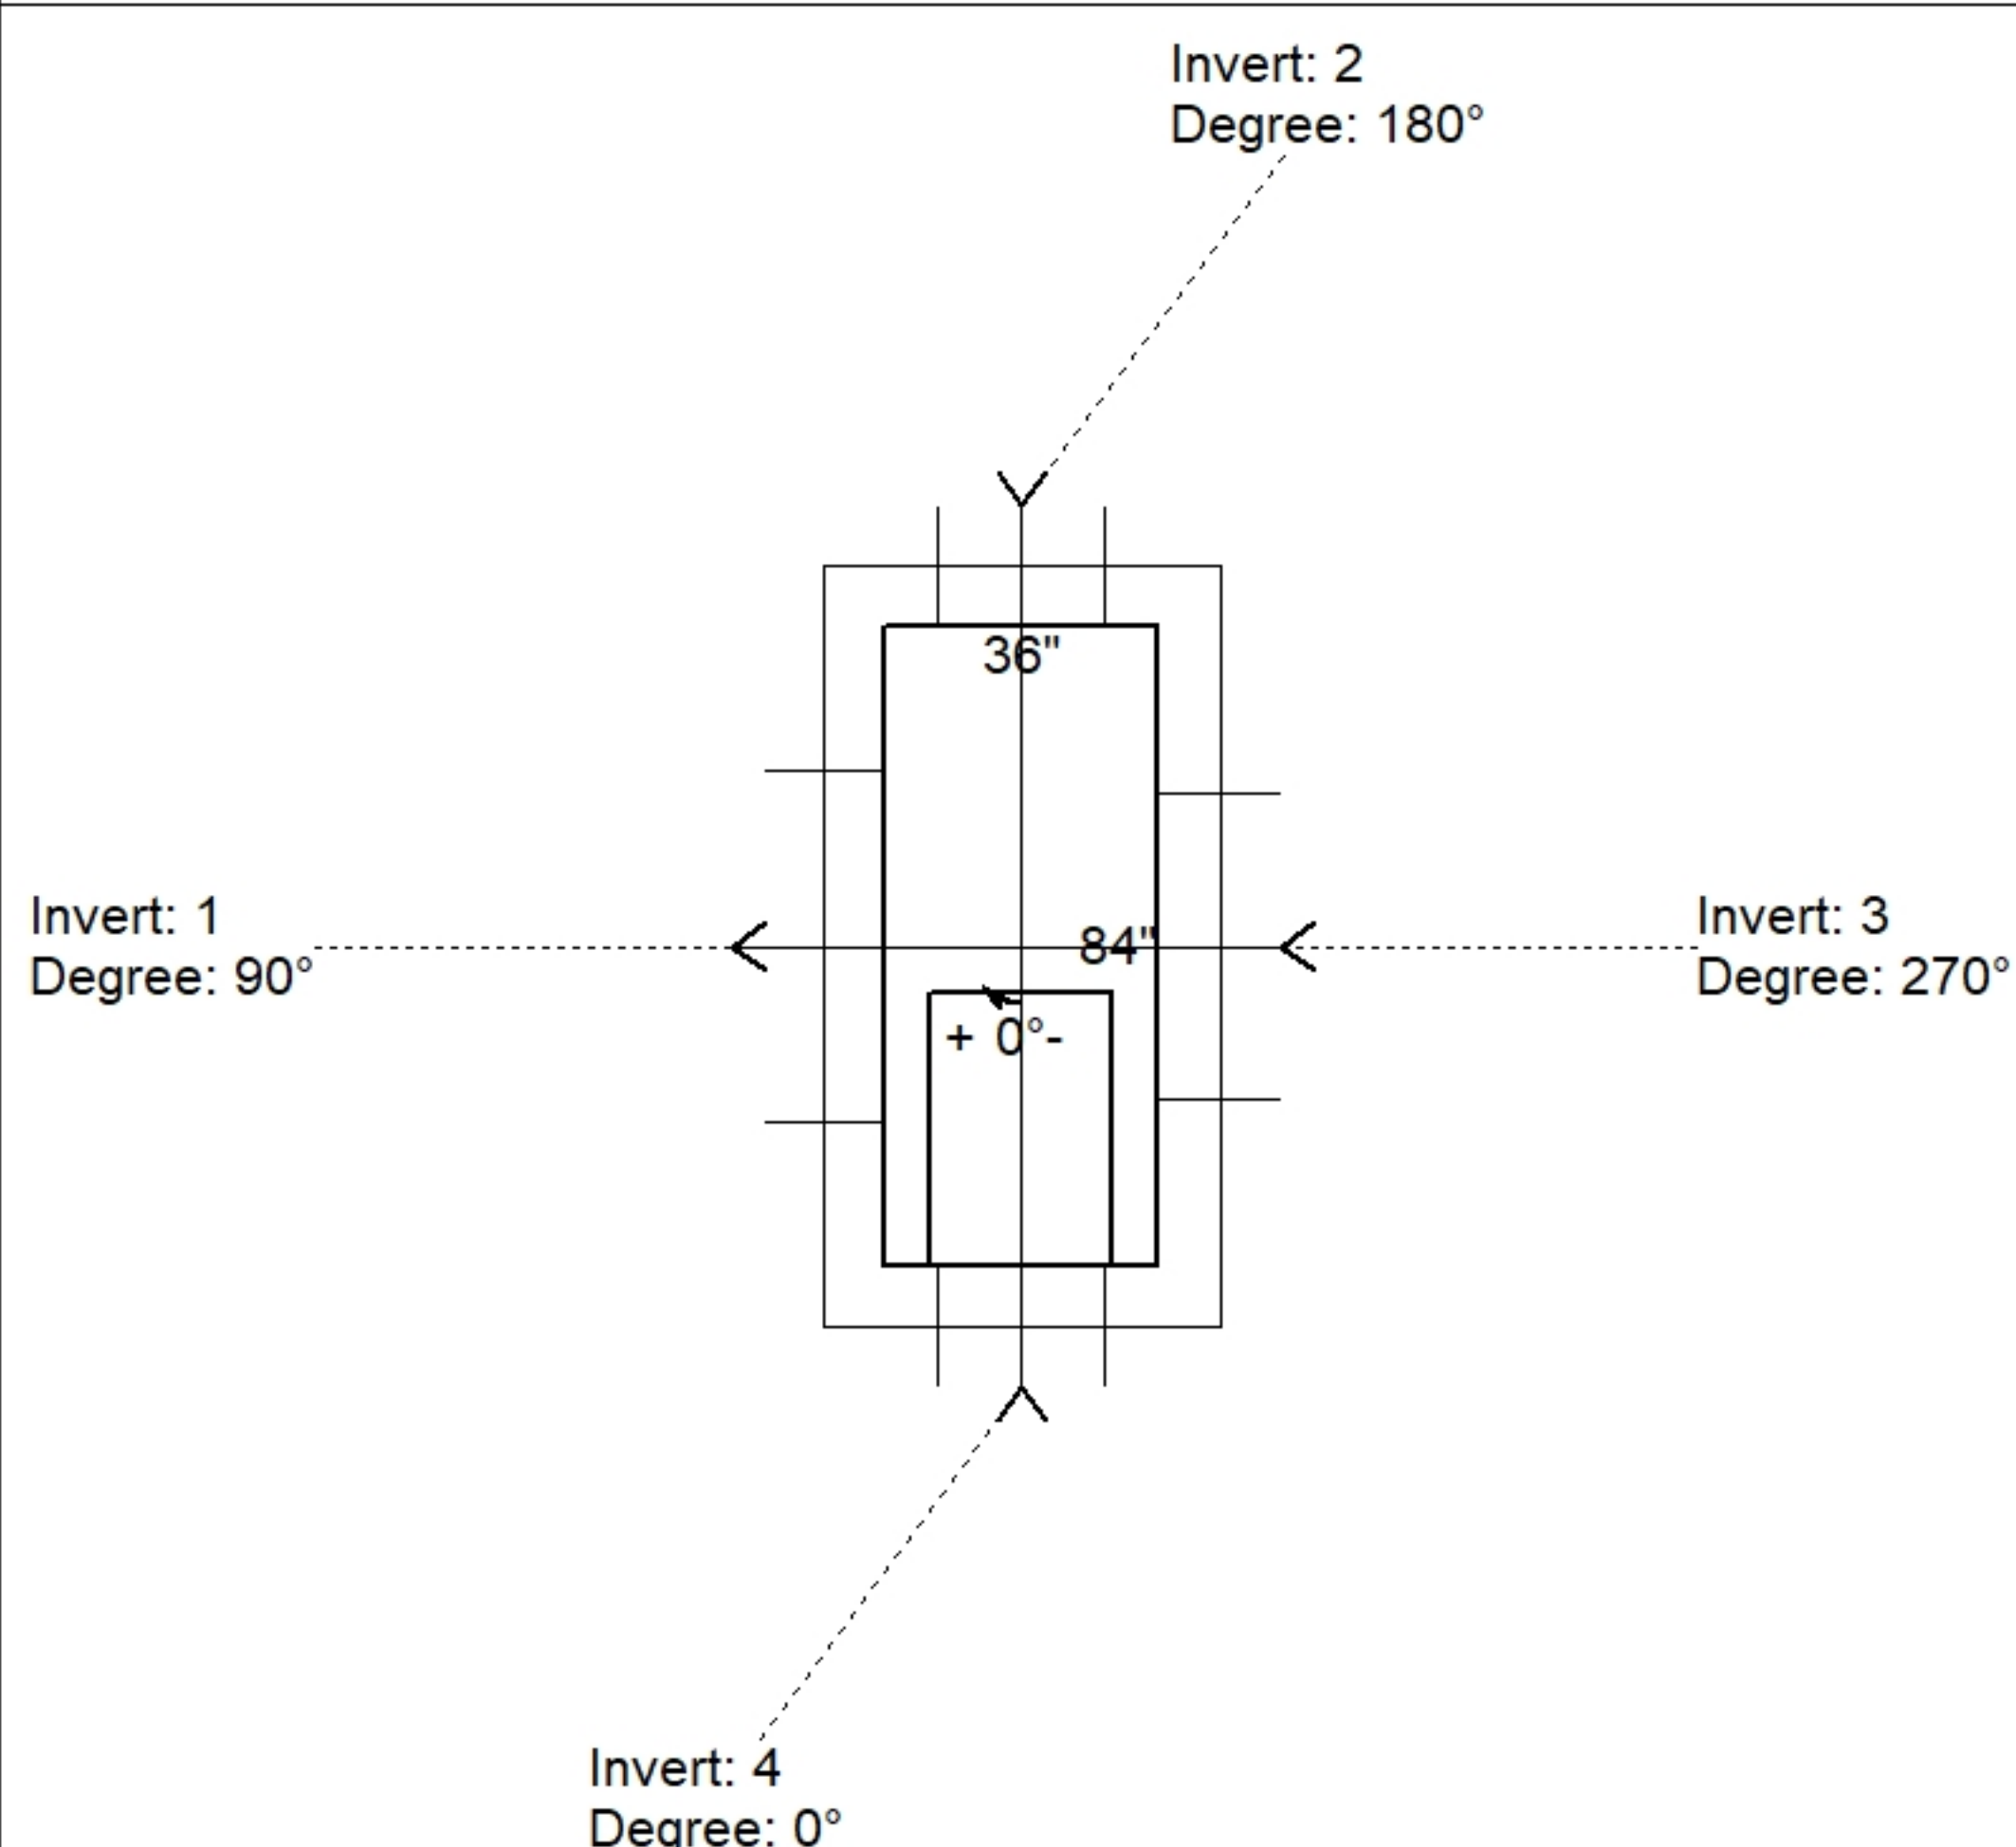

Position	Elev	Angle	Pipe	Pipe OD	Hole	Connector	Up (⌵)	Ref
Rim	687.19'							
Reducer								
Invert 1	681.19'	90°	36" RCP B WALL	44"	46"	Hole 46	-4"	P1
Invert 2	681.19'	180°	15" RCP B WALL	19.5"	22"	Hole 22	-2.25"	P1
Invert 3	681.19'	270°	30" RCP B WALL	37"	40"	Hole 40	-3.5"	P1
Invert 4	681.19'	0°	15" RCP B WALL	19.5"	22"	Hole 22	-2.25"	P1
Invert 5								
Invert 6								
Invert 7								
Invert 8								

(P1)

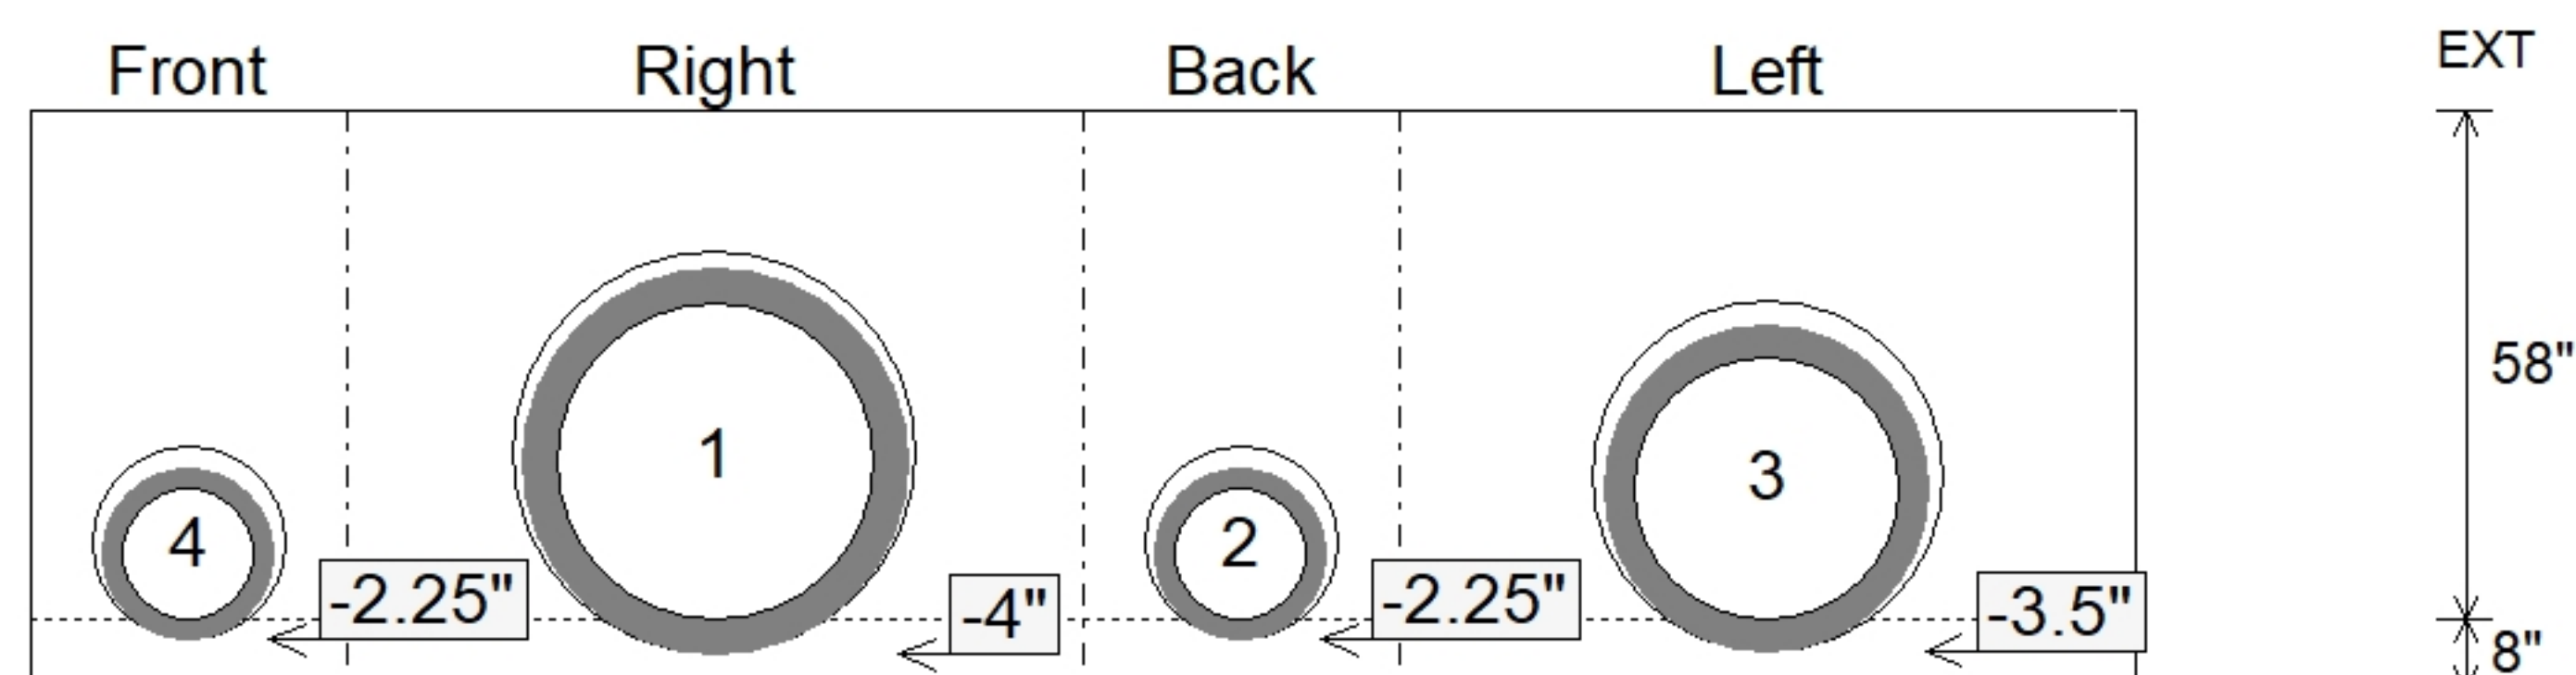

SUBMITTAL
APPROVED BY:
