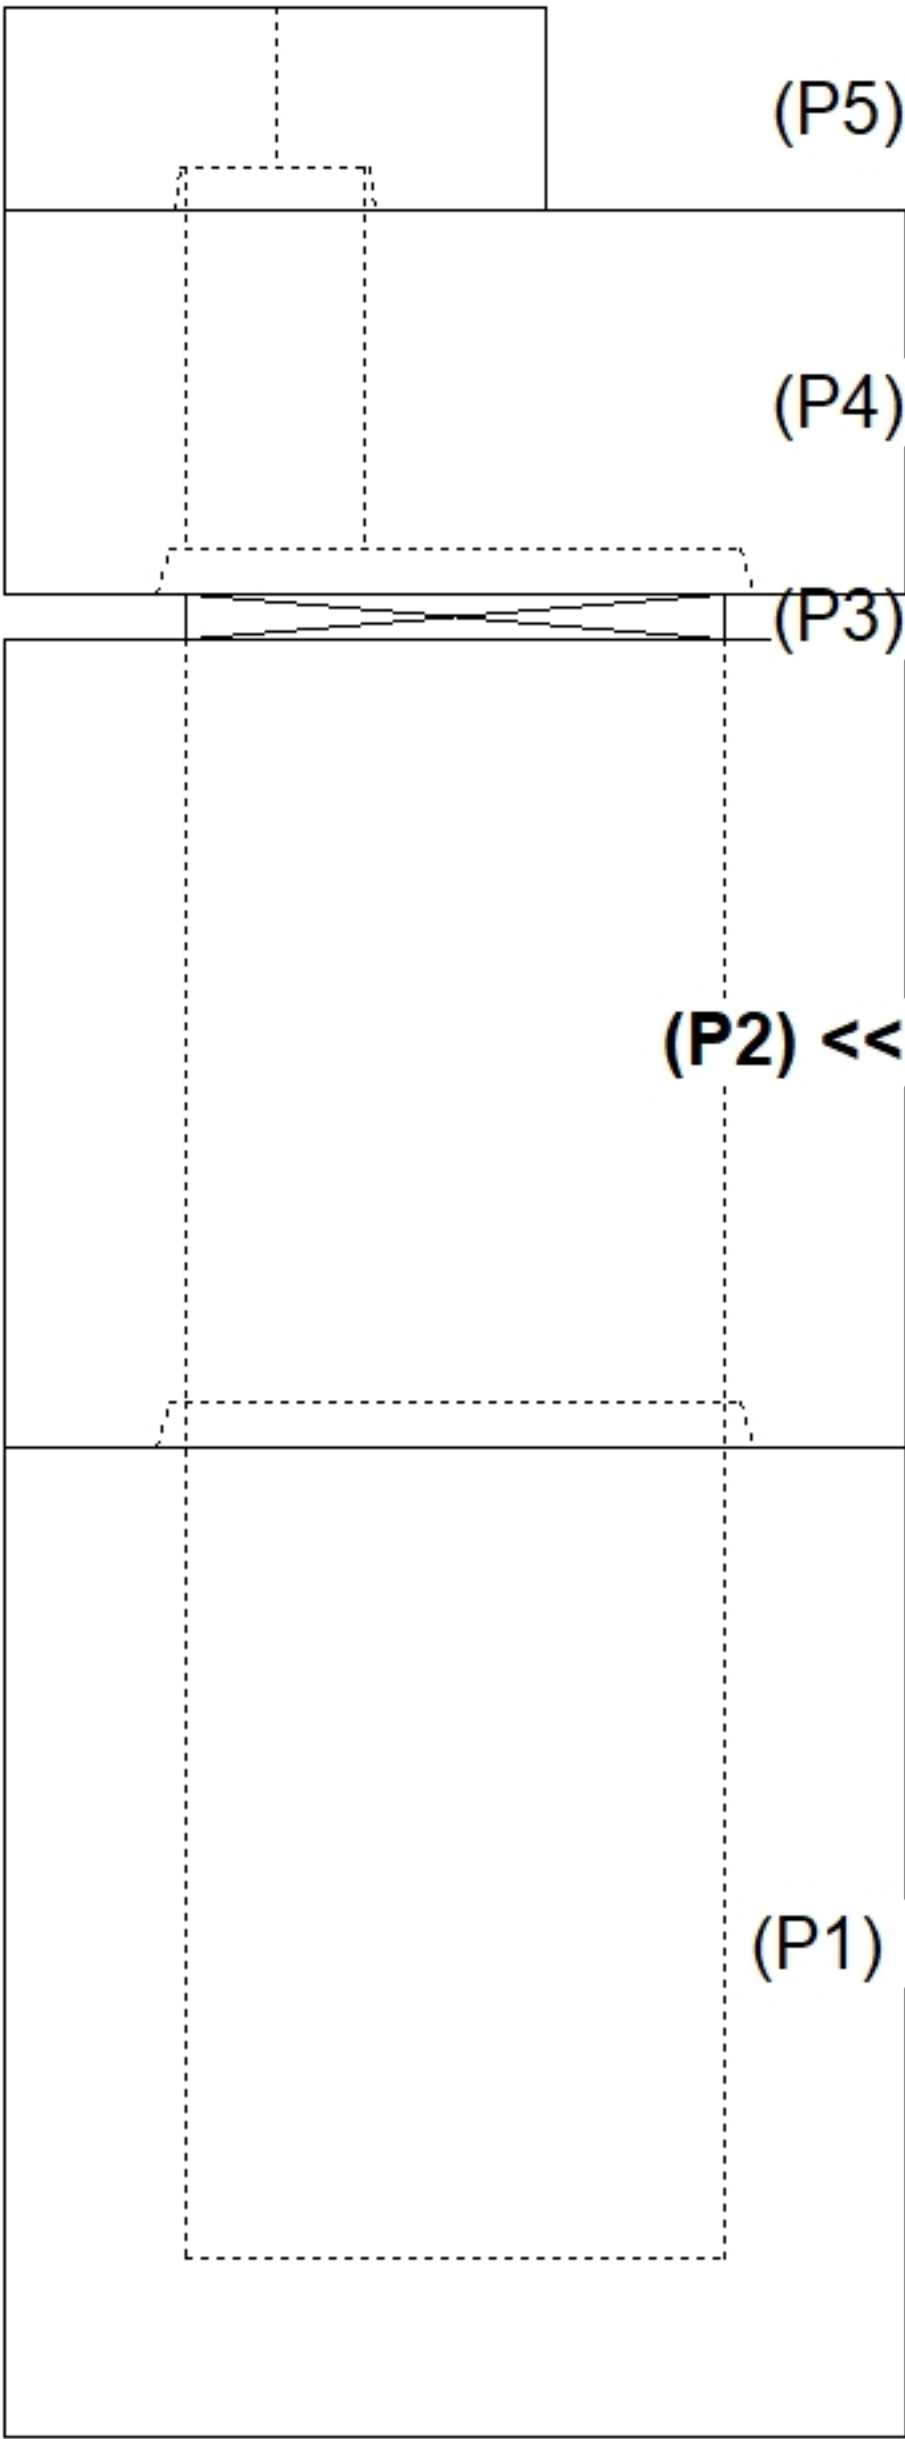
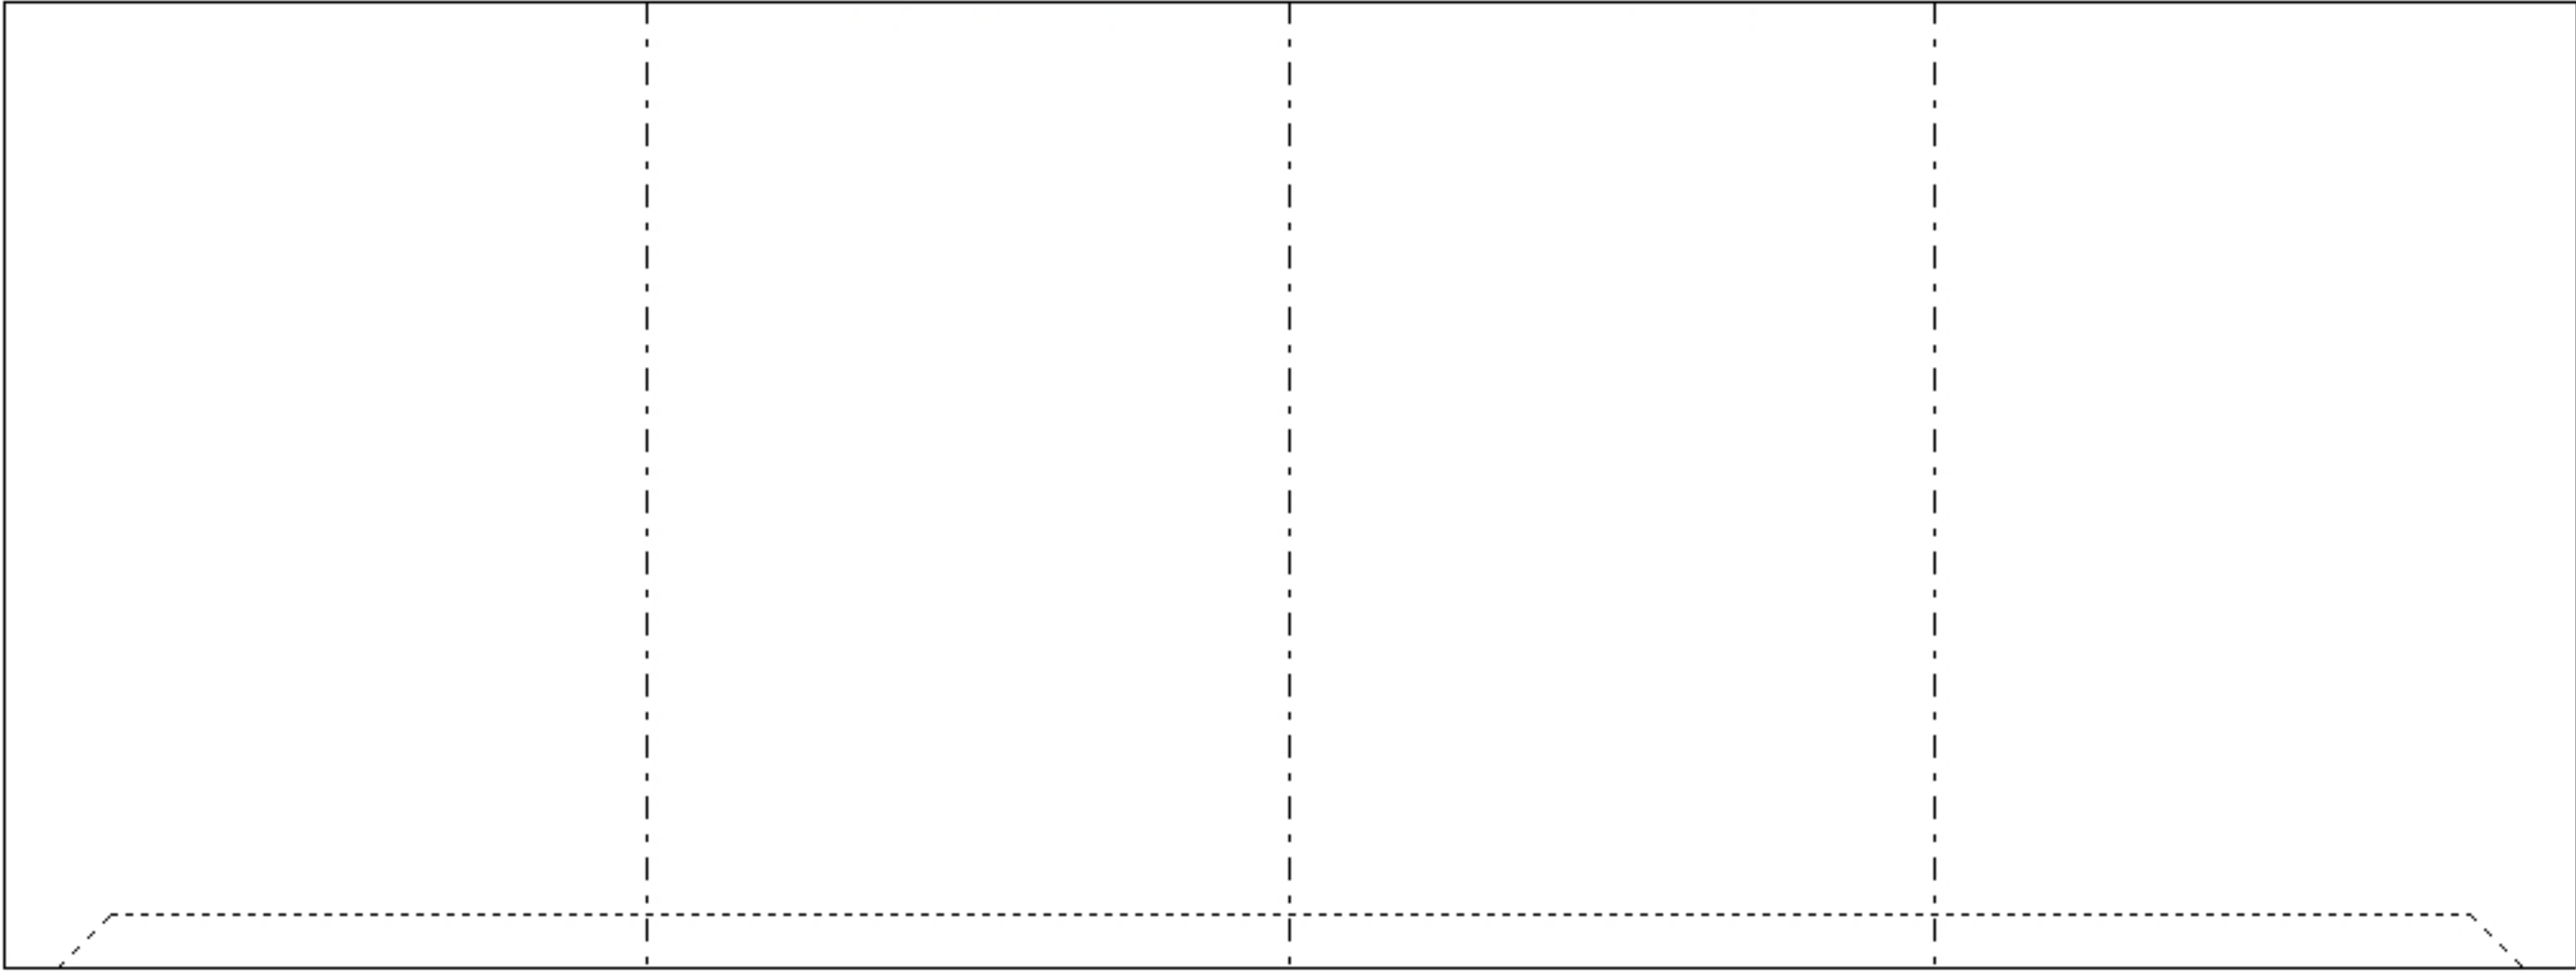
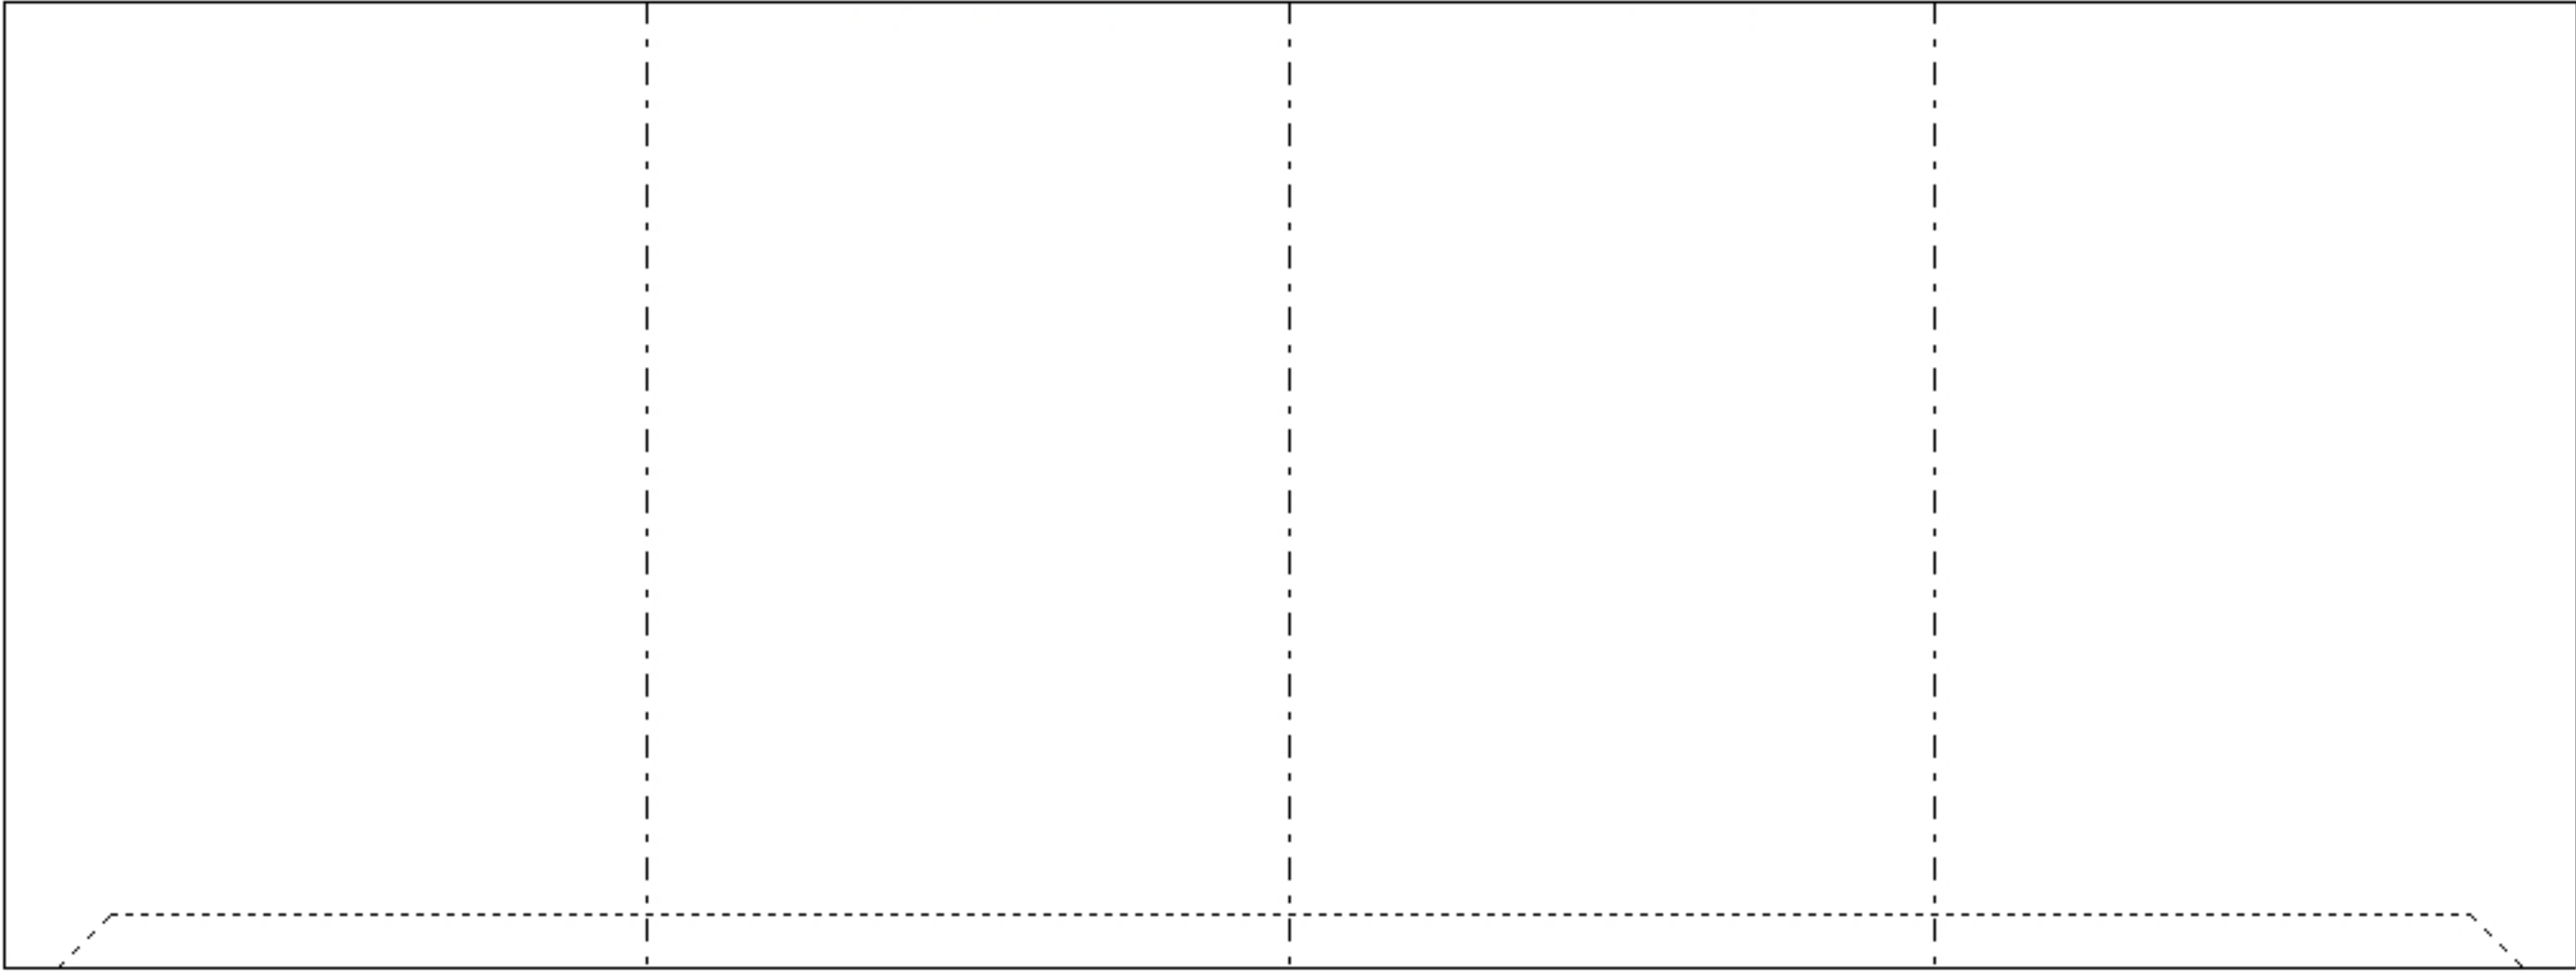
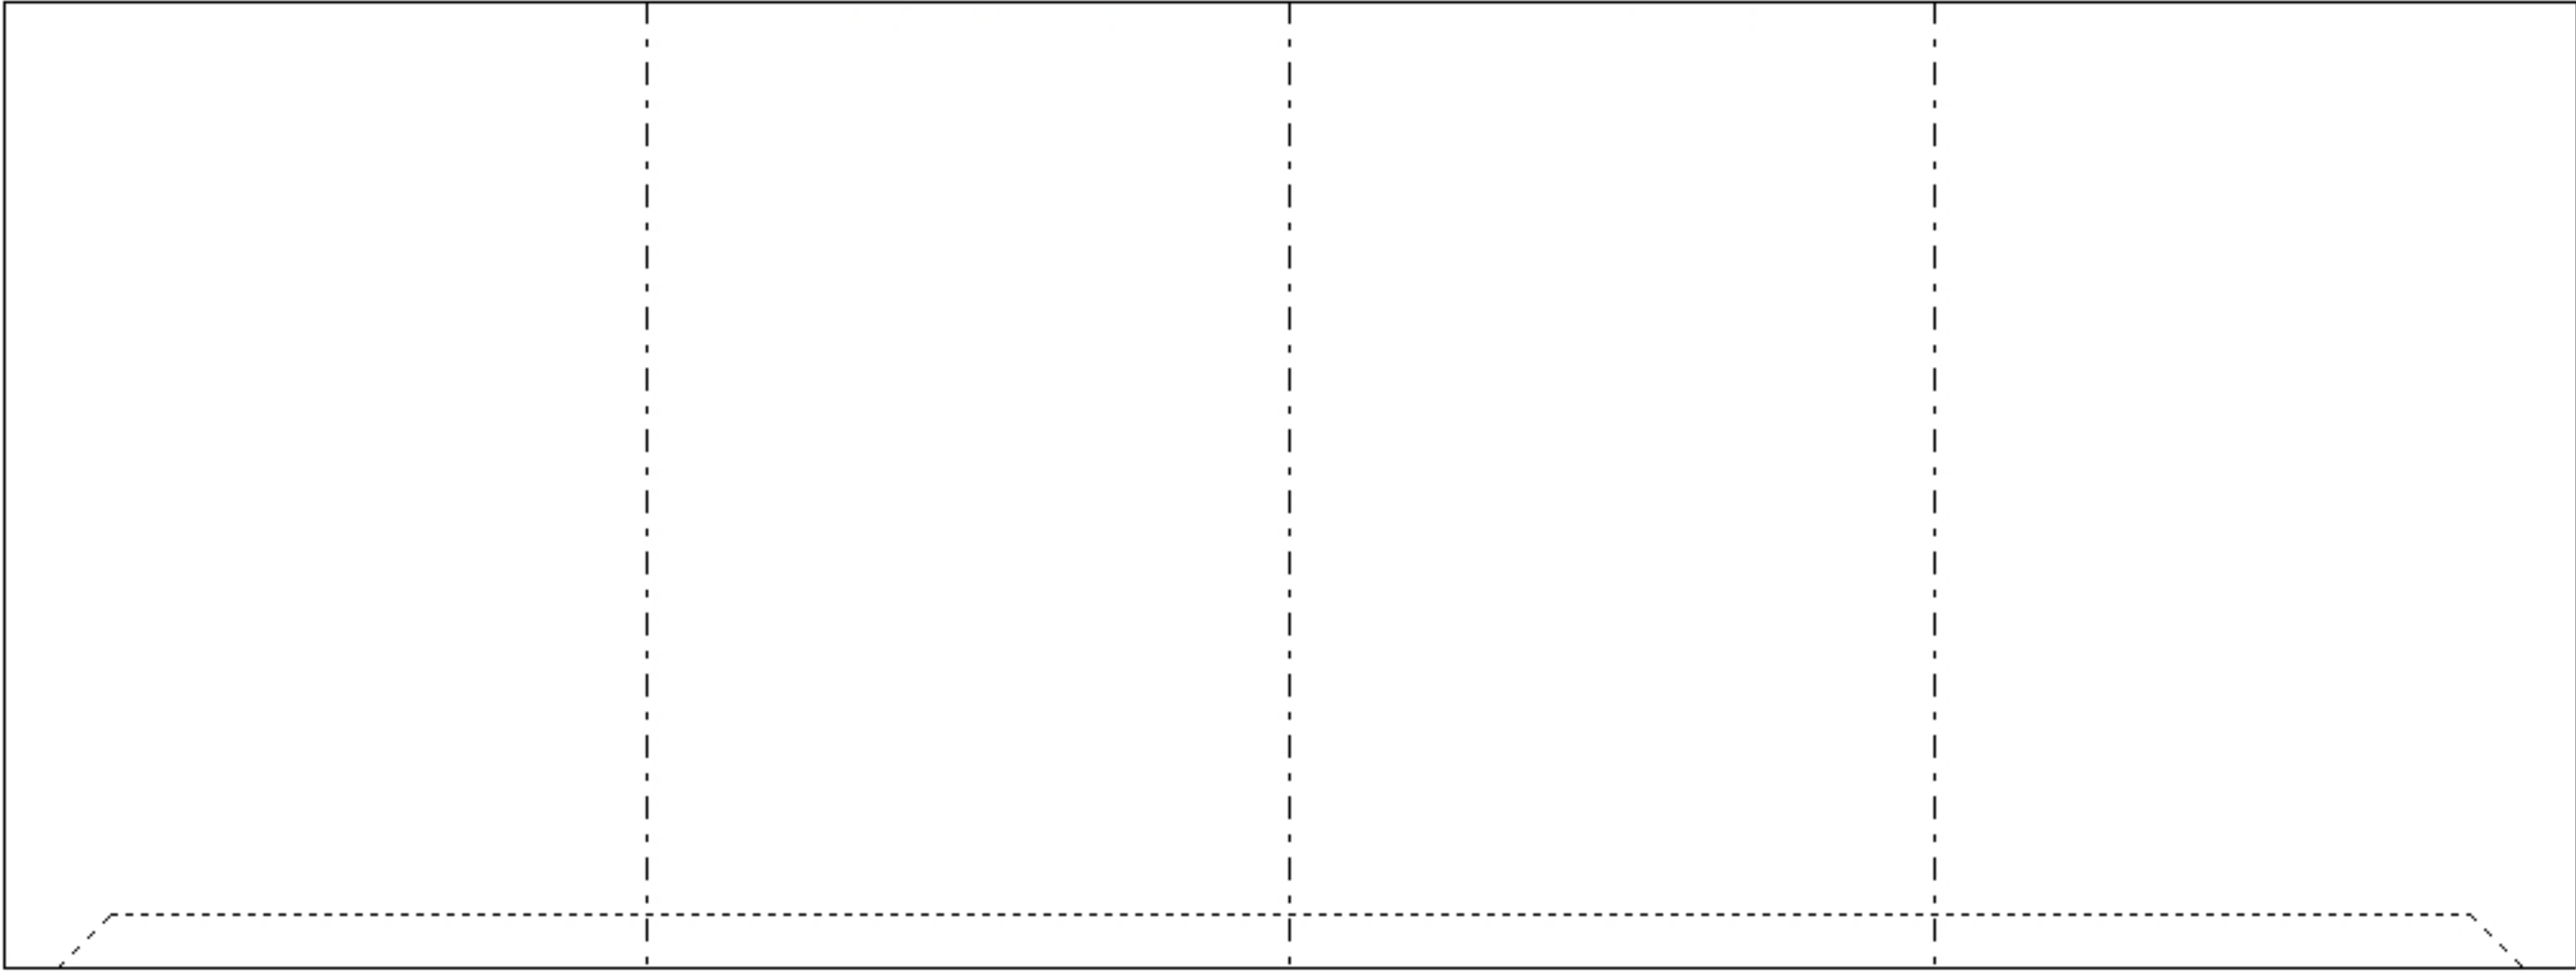


Job Name: 26-2030 - KYTC McCracken Co. Call 111 (ID 264505) Job Location: Paducah, KY Contractor: Jim Smith Contracting Co, LLC				Plant: 100 6/12/2026 7:50:13 AM		Tech: J. Horsley PC: J. Jarvis														
Structure ID: 151+22 RT S-3 CBIB																				
P2 BX2424-08R36				BOX RISER 8inW F/G																
P5) 8" x 120" - CB INLET KY B 10' TOP F/G - 9" P4) 24" x 120" - CB INLET KY B 10' BOTTOM LEFT T/G - 17" P3) 24" x 24" - FIELD ADJUSTMENT - 2" P2) 24" x 24" - BOX RISER 8inW F/G - 36" P1) 24" x 24" - BOX BASE 8inW, 8inF T/n - 36" 1) CASTING - HOE KY-345 SET (CBI B) 2) 24" x 24" - Conseal CS-102 1.00" 2) Hole - 22 1) Hole - 18						1660 lb 2650 lb 0 lb 3093 lb 3486 lb 290 lb 0 lb 0 lb 0 lb ----- Structure Total: 11180 lb		Structure Notes: . ** KYTC STATE PROJECT ** 1. PER KYTC CBI TYPE B / ASTM C913 SPEC'S. 2. CONCRETE = 4,000 PI AT 28 DAYS. 3. CASTING BT ICAST (HOE KY-345 F/G(CBI-B) . REINFORCING PER ASTM A615 (GRADE 60). - TOP PHASE (As .62) #5 BARS AT 6" C.C.E.W. - WALLS (As .31) #5 BARS AT 12" C.C.E.W. - FLOOR (As .31) #5 BARS AT 12" C.C.E.W.												
Rim: 375.16' Rim to Invert: 8.38' Slack: 0.56" Sump: 0" Step Position:																				
Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up ()	Offset										
Invert 1																				
Invert 2																				
Invert 3																				
Invert 4																				
Invert 5																				
Invert 6																				
Invert 7																				
Invert 8																				
RIGHT-SIDE UP VIEW (int. dimensions)  INSIDE WALL DIMENSIONS <table><tr><td>Front</td><td>Right (24")</td><td>Back (24")</td><td>Left</td><td>EXT</td></tr><tr><td colspan="4"></td><td>36"</td></tr></table>											Front	Right (24")	Back (24")	Left	EXT					36"
Front	Right (24")	Back (24")	Left	EXT																
				36"																
Coating (Int): Coating (Ext):				Seam Up: Flat Seam Dn: Groove		Wall Thickness: 8" Floor Height: 0"		Height (Int): 36" Height (Ext): 36"		Weight (Net): 3093 lb Volume (Net): 0.79cu.yd										
