



Slack: 1.6"

Structure Total: 3994 lb


Position	Elev	Angle	Pipe	Pipe OD	Hole	Connector	Up ()	Ref
Rim	604.8'							
Reducer								
Invert 1	601.55'	0°	18" HDPE	21.2"	24"	Hole 24	0"	P1
Invert 2								
Invert 3								
Invert 4								
Invert 5								
Invert 6								
Invert 7								
Invert 8								

24" x 36" - CASTING HEIGHT - 6" - (P3)

48" - MH FLAT TOP w/24"x36" Hole - 7" - (P2)

48" - MH BASE Custom Ht - 26" - (P1)

The diagram illustrates a manhole assembly with three distinct parts. At the top is a hatched rectangular casting, 24 inches wide and 36 inches high, labeled (P3). Below this is a flat top section, 48 inches wide and 7 inches high, featuring a central rectangular hole that matches the casting's dimensions, labeled (P2). The bottom section is the manhole base, 48 inches wide and 26 inches high, shown with a dashed outline, labeled (P1). Vertical dashed lines indicate the alignment of the components.

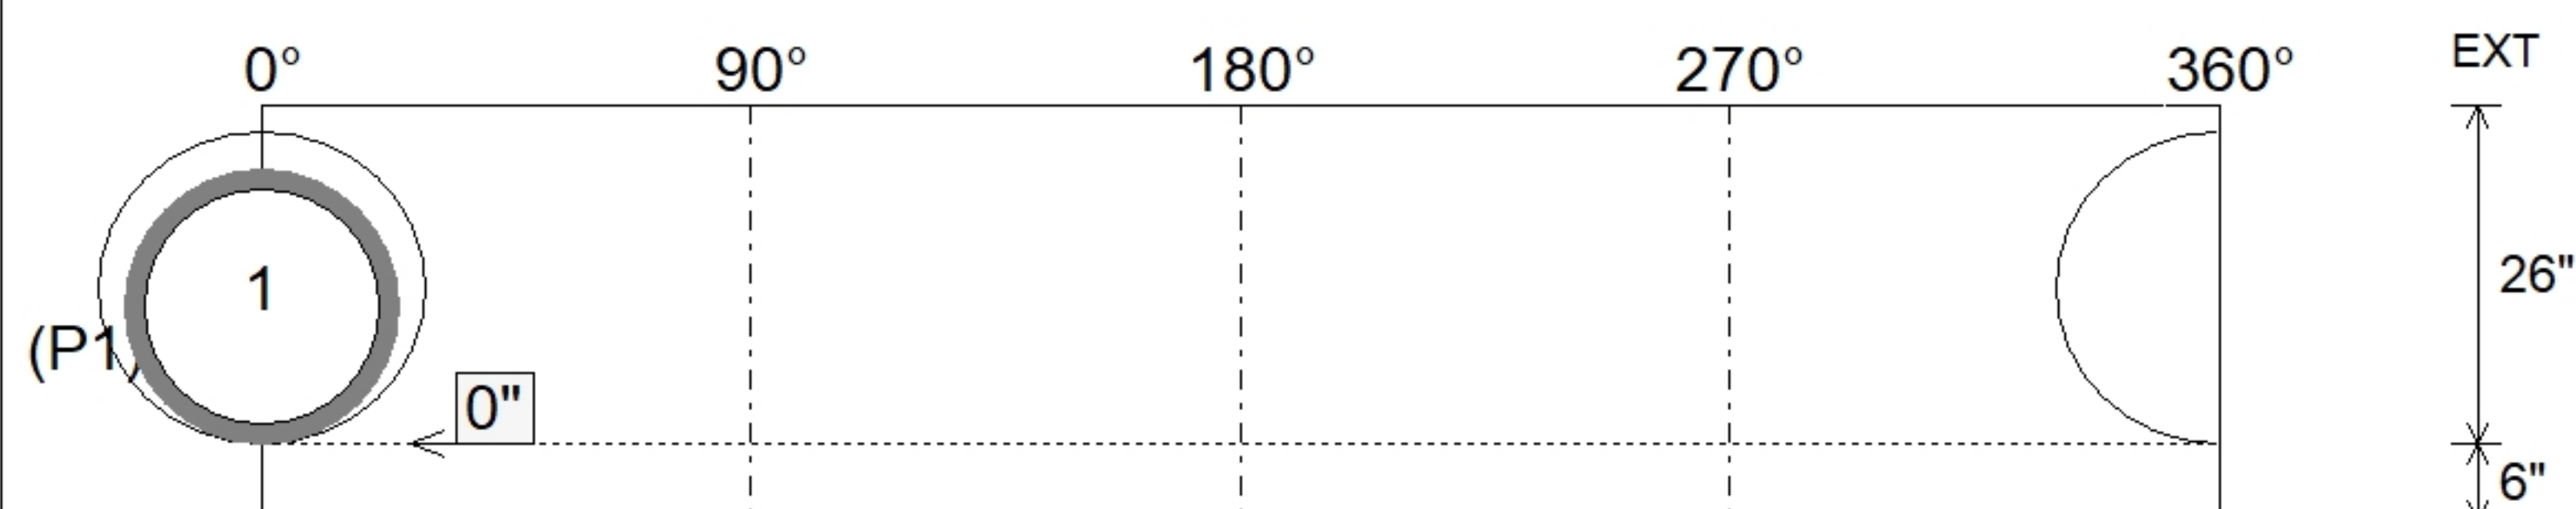

SUBMITTAL
APPROVED BY:
