Job Name: 25-2952 - KYTC Jefferson Co Call 106 (251315)
Job Location: Indiana, KY
Contractor: Louisville Paving and Construction

Plant: 100
5/12/2026 12:59:21 PM

Tech: J. Horsley - A
PC: J. Jarvis

Structure ID: 78

P1 BX24300808VF — BOX BASE 8inW, 8inF, Variable Ht F/n

P3) 15" x 27" - P.I.P. - BY OTHERS - 8"	0 lb
P2) 24" x 30" - CB FLAT TOP 8"W w/15"x27" HOLE F/F - 8"	963 lb
P1) 24" x 30" - BOX BASE 8inW, 8inF, Variable Ht F/n - 38"	4408 lb
1) 24" x 30" - Conseal CS-102 1.00"	0 lb
1) 15" x 27" - Conseal CS-102 1.00"	0 lb
1) Hole - 20	0 lb
1) Hole - 18	0 lb
2) Hole - 4	0 lb
Structure Total:	5371 lb

Structure Notes:
KYTC STATE PROJECT
1. PER KYTC DBI TYPE 13G / ASTM C-913 SPECS
2. CONCRETE: 4,000 PSI AT 28 DAYS
3. REINFORCEMENT: #5 BAR @ 12" C.C. E.W. (GRADE 60) - 2" MIN. REBAR CLEARANCE (TYP)
4. NO STORM INVERT
5. NO STEPS
6. HOE KY-230G FRAME & GRATE SUPPLIED BY OTHERS

Rim: 552.12' Rim to Invert: 4.5' Slack: 0" Sump: 0" Step Position:

Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up (_)	Offset
Invert 1	547.62'	180°	20"	15" HDPE	17.6"	Hole 20	20"	20"	-2.5"	0"
Invert 2	547.62'	270°	23"	12" HDPE	14.5"	Hole 18	18"	18"	-3"	0"
Invert 3	550.12'	90°	23"	4" WEEP HOLE	4"	Hole 4	4"	4"	30"	0"
Invert 4	550.12'	270°	23"	4" WEEP HOLE	4"	Hole 4	4"	4"	30"	0"
Invert 5										
Invert 6										
Invert 7										
Invert 8										

RIGHT-SIDE UP VIEW (int. dimensions)

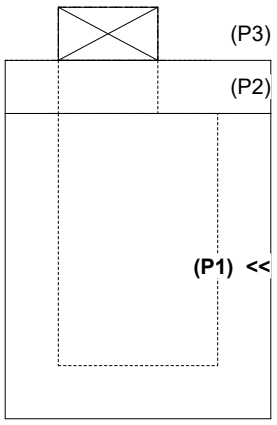

UPSIDE-DOWN VIEW (int. dimenions)

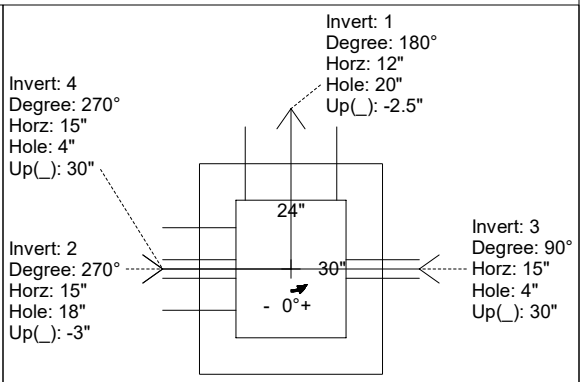

INSIDE WALL DIMENSIONS

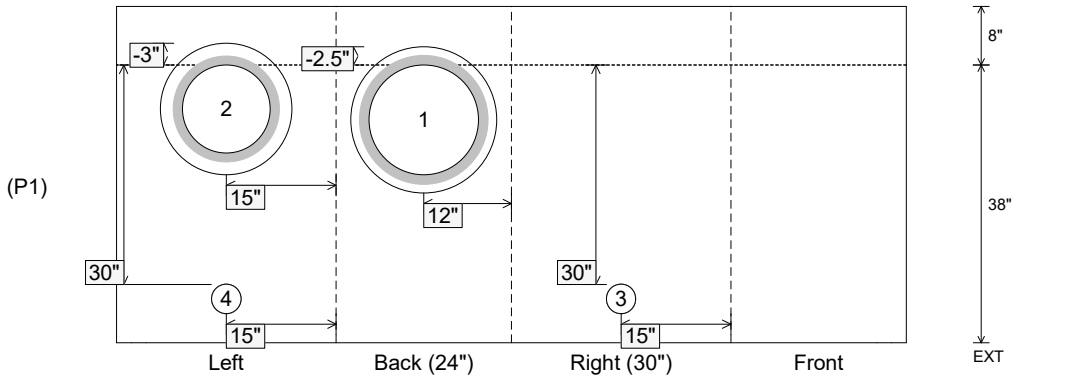

Coating (Int):	Seam Up: Flat	Wall Thickness: 8"	Height (Int): 38"	Weight (Net): 4408 lb
Coating (Ext):	Seam Dn: n/a	Floor Height: 8"	Height (Ext): 46"	Volume (Net): 1.13cu.yd
