Job Name: 23-1914 - KYTC Daviess Couny ID 231032
Job Location: Owensboro, KY 42701
Contractor: Mick-Murf Construction Inc.

Plant: 100
1/13/2026 8:34:09 AM

Tech: J. Horsley
PC: C. Goff

Structure ID: 089 (KY B 10ft)

P1 BX3648-08BA60 BOX BASE 8inW, 8inF F/n

P6) 8" x 120" - CB INLET KY B 10' TOP F/G - 9"	1660 lb
P5) 24" x 120" - CB INLET KY B 10' BOTTOM RIGHT T/G - 17"	2650 lb
P4) 24" x 24" - FIELD ADJUSTMENT - 3"	0 lb
P3) 24" x 24" - BOX RISER 8inW F/G - 24"	2043 lb
P2) 36" x 48" - CB FT REDUCER 24"X24" HOLE T/F - 8"	1847 lb
P1) 36" x 48" - BOX BASE 8inW, 8inF F/n - 60"	8423 lb
1) 36" x 48" - Conseal CS-102 1.00"	0 lb
2) 24" x 24" - Conseal CS-102 1.00"	0 lb
1) Hole - 40	0 lb
1) Hole - 28	0 lb
1) Hole - 34	0 lb
1) Hole - 6	0 lb
Structure Total:	16624 lb

Structure Notes:
** KYTC STATE PROJECT **
1. PER KYTC CBI TYPE B / ASTM C913 SPEC'S.
2. CONCRETE = 4,000 PI AT 28 DAYS.
3. NO STEPS & NO INVERT CHANNEL.
5. CBI KY B F/G - BY OTHERS.

REINFORCING PER ASTM A615 (GRADE 60).
- TOP PHASE (As .62) #5 BARS AT 6" C.C.E.W.
- TRANS SLAB (As .62) #5 BARS AT 6" C.C.E.W. (DBL MAT.)
- WALLS/FLOOR (As .31) #5 BARS AT 12" C.C.E.W.

Rim: 424.73' Rim to Invert: 10.13' Slack: 0.56" Sump: 0" Step Position:

Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up (_)	Offset
Invert 1	414.6'	90°	32"	36" CMP	37"	Hole 40	40"	40"	-0.5"	0"
Invert 2	414.68'	180°	26"	24" CMP	25"	Hole 28	28"	28"	0.5"	0"
Invert 3	414.68'	270°	32"	30" CMP	31"	Hole 34	34"	34"	0.5"	0"
Invert 4										
Invert 5										
Invert 6										
Invert 7										
Invert 8										

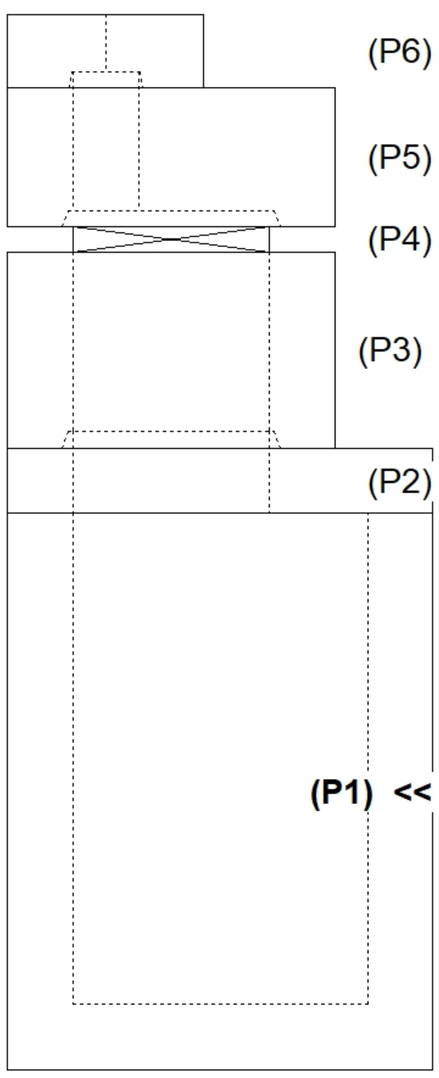

RIGHT-SIDE UP VIEW (int. dimensions)

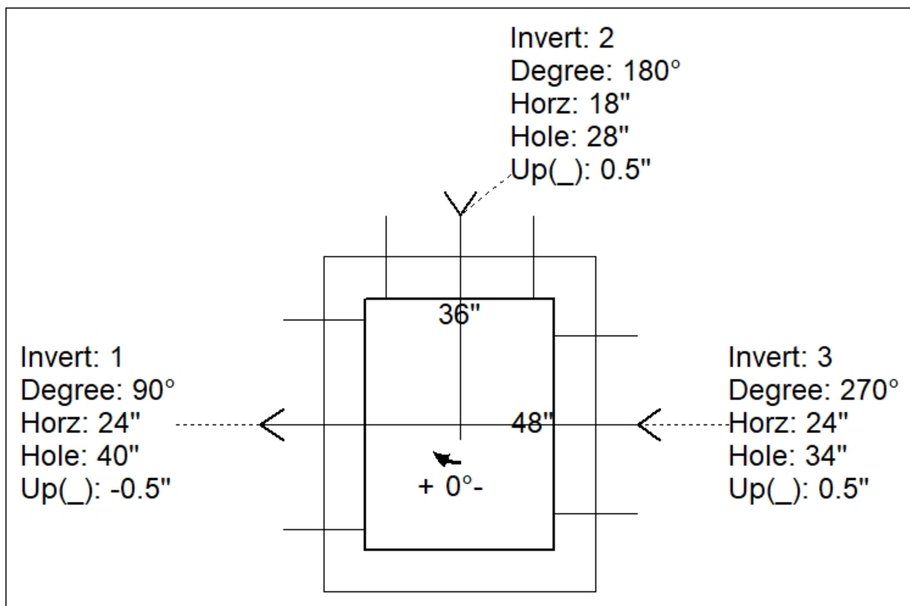

UPSIDE-DOWN VIEW (int. dimenions)

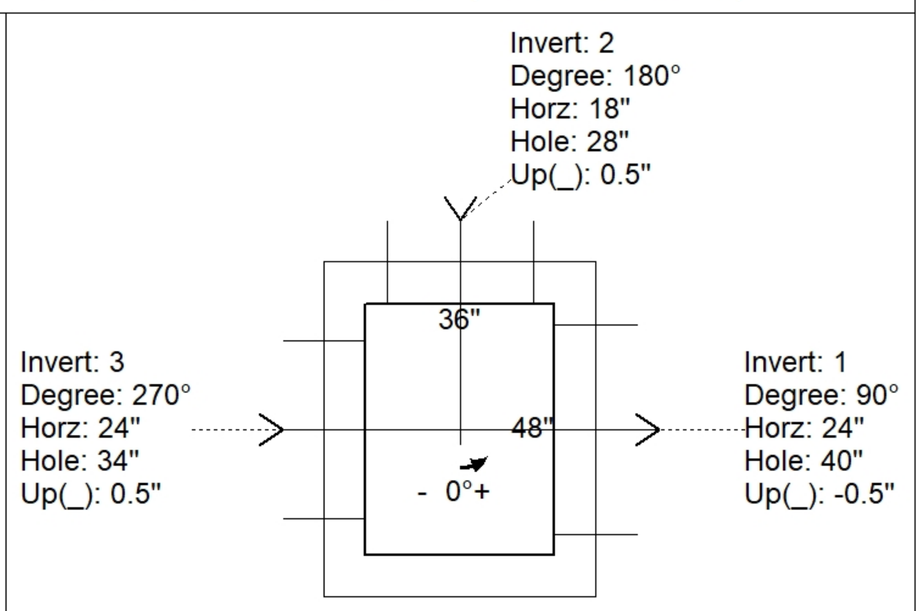

INSIDE WALL DIMENSIONS

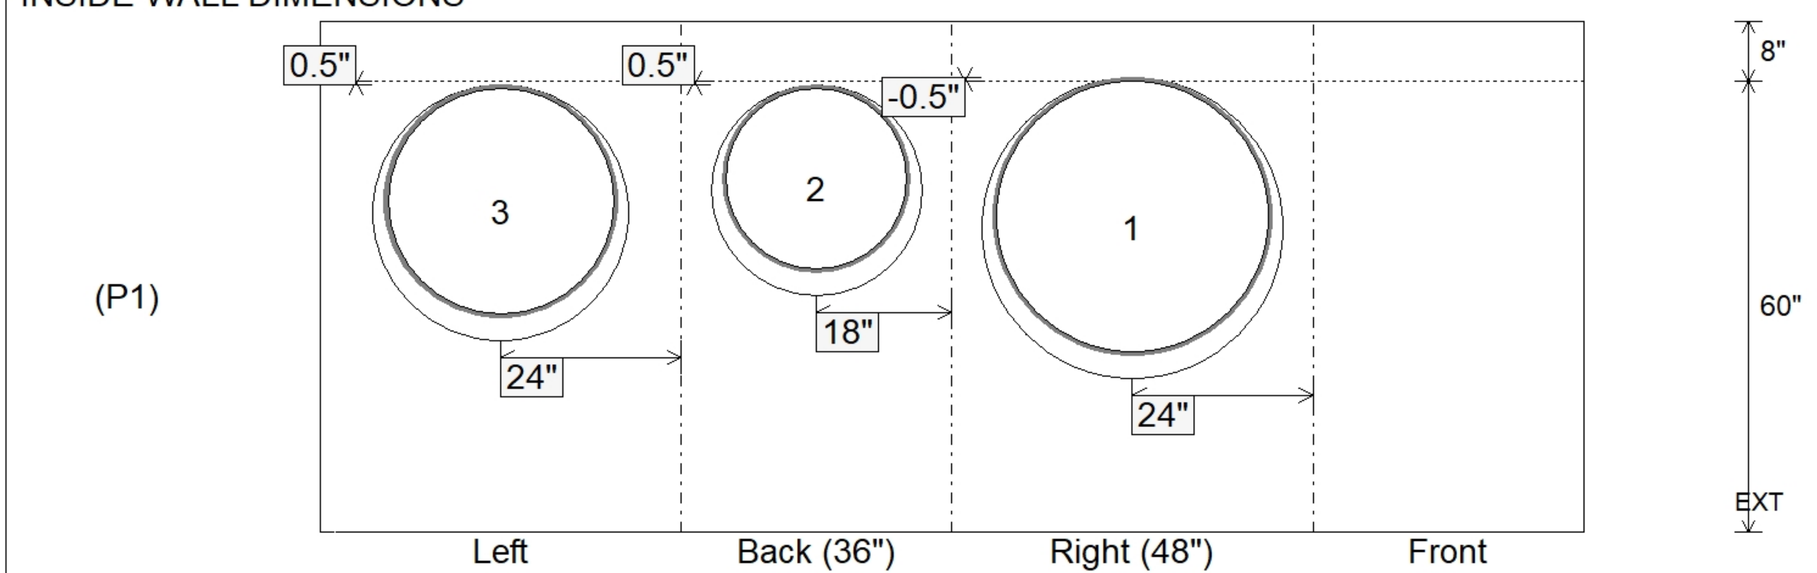

Coating (Int): Coating (Ext):	Seam Up: Flat Seam Dn: n/a	Wall Thickness: 8" Floor Height: 8"	Height (Int): 60" Height (Ext): 68"	Weight (Net): 8423 lb Volume (Net): 2.15cu.yd
