Job Name: 24-4208 - KYTC Christian Co. Call 100 (ID 241018)
Job Location: Hopkinsville, KY
Contractor: Scotty's Contracting & Stone, LLC

PC: C. Goff
TECH: J. Horsley
Plant: Beaver Dam

Structure ID: **201**

Spec: KYTC	Rim: 565.82'	Sump: 0"	Floor (Bot): 559.873'
Type: CBI TYPE A (10') private	Invert: 560.54'	Floor (Top): 560.54'	Overall Height: 5.917'
Size: 24" x 36"	Rim to Invert: 5.28'	Floor Height: 8"	Slack: 0.36"

Structure Notes:
** KYTC STATE PROJECT **
STATION: 410+10 RT
1. PER KYTC CBI TYPE A / ASTM C-913 SPECS
2. CONCRETE: 4,000 PSI AT 28 DAYS
3. REINFORCEMENT:
   - TOP PHASE TOP: #5 BAR @ 6" C.C. E.W. (GRADE 60)
   - TOP PHASE BOTTOM: #5 BAR @ 12" C.C. E.W. (GRADE 60)
   - PIPE CHAMBER: #5 BAR @ 12" C.C. E.W. (GRADE 60)
4. HOE KY-206 FRAME & COVER "STORM" SUPPLIED BY ICAST - FRAME TO BE CAST INTO TOP PHASE TOP FLANGE SIDE UP

STRUCTURE SUMMARY:

P4) 24" x 120" - CB INLET KY A 10' TOP LEFT F/G - 10"	3400 lb
P3) 24" x 120" - CB INLET KY A 10' BOTTOM LEFT T/G - 18"	5270 lb
P2) 24" x 36" - FIELD ADJUSTMENT - 3"	0 lb
P1) 24" x 36" - BOX BASE 8inW, 8inF, Variable Ht F/n - 32"	4058 lb
1) CASTING - HOE KY-206 F/C (KY TY1)	206 lb
1) This Structure Includes a Cast-in Item - KY-206 Frame (Supplied by iCast)	0 lb
2) 24" x 36" - Conseal CS-102 1.00"	0 lb
1) Hole - 24	0 lb
1) Hole - 26	0 lb
1) Hole - 6	0 lb
Structure Total:	12934 lb

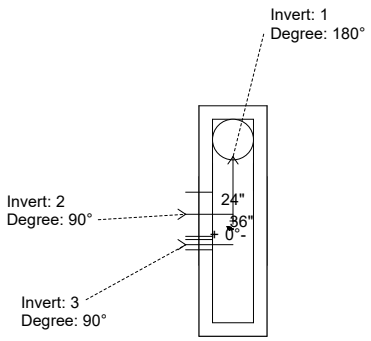

Position	Elev	Angle	Pipe	Pipe OD	Hole	Connector	Up (_)	Ref
Rim	565.82'							
Reducer								
Invert 1	560.54'	180°	18" HDPE	21.2"	24"	Hole 24	-1.625"	P1
Invert 2	560.56'	90°	18" RCP B WALL	23"	26"	Hole 26	-2.25"	P1
Invert 3	562.07'	90°	4" HDPE (perf pipe)	4.8"	6"	Hole 6	18"	P1
Invert 4								
Invert 5								
Invert 6								
Invert 7								
Invert 8								

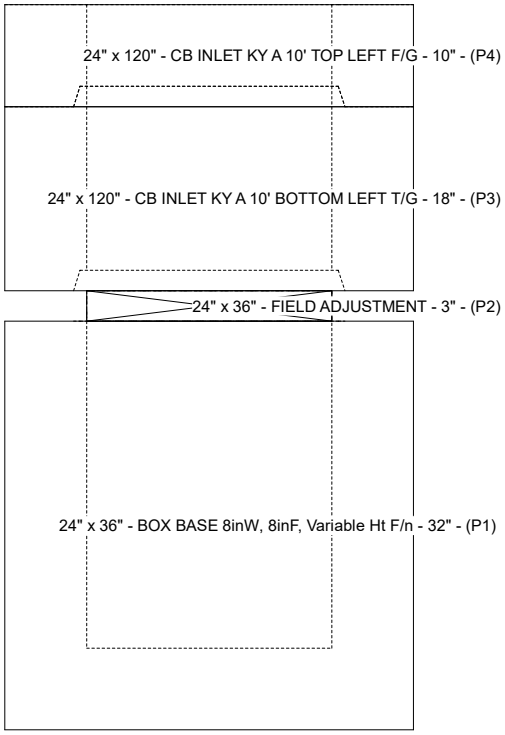

Cast (Int. Dim.) - Interior Dimensions

(P1)



Submittal Drawing
6/26/2026 7:34:00 AM

SUBMITTAL
APPROVED BY:
