Job Name: 25-0209 Garrison Gardens Job Location: Bowling Green, KY Contractor: Scotty's Contracting & Stone, LLC	Plant: 100 1/23/2026 4:36:14 PM	Tech: J. Horsley - A PC: Celina Goff	

Structure ID: CB 3-2

P2 MH060TS13-48ECC — MH Transition Slab 48" Hole T/G

P5) 30" x 30" - CASTING HEIGHT - 4"	0 lb
P4) 48" - MH FLAT TOP w/30"x30" Hole F/G - 12"	1350 lb
P3) 48" - MH RISER SPECIAL T/G - 48"	3341 lb
P2) 60" - MH Transition Slab 48" Hole T/G - 13"	1928 lb
P1) 60" - MH BASE Custom Ht T/n - 68"	8612 lb
1) CASTING - HOE 468 F/G	489 lb
1) 60" - Conseal CS-102 1.00"	0 lb
2) 48" - Conseal CS-102 1.00"	0 lb
1) 30" x 30" - Conseal CS-102 1.00"	0 lb
2) Hole - 38	0 lb
1) Hole - 6	0 lb
9) MH Step ML-10-TDS-NCR - 10"	0 lb
Structure Total:	15720 lb

Structure Notes:
1. PER ASTM C-478 SPECIFICATIONS
2. CONCRETE: 4,000 PSI AT 28 DAYS
3. REINFORCEMENT: #5 BAR @ 6" C.C. E.W. (GRADE 60) - 2" MIN. REBAR CLEARANCE (TYP)
4. HOE 468 FRAME & GRATE SUPPLIED BY ICAST
5. LIFTERS: 3 EA. WRA016 CONAC WIRE ROPE ANCHORS FOR PLANT & FIELD HANDLING
6. TOP SURFACE TO RECEIVE FLOATED FINISH

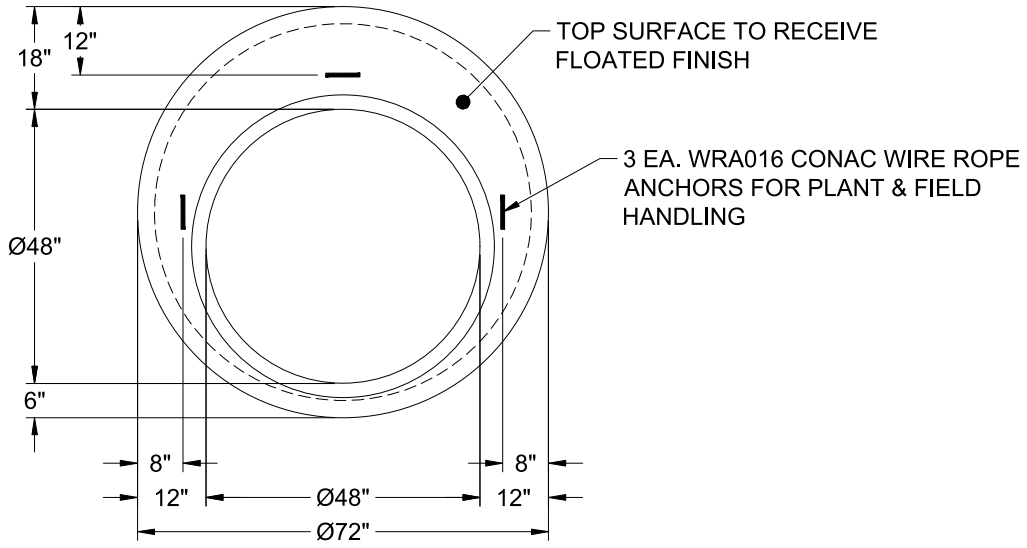

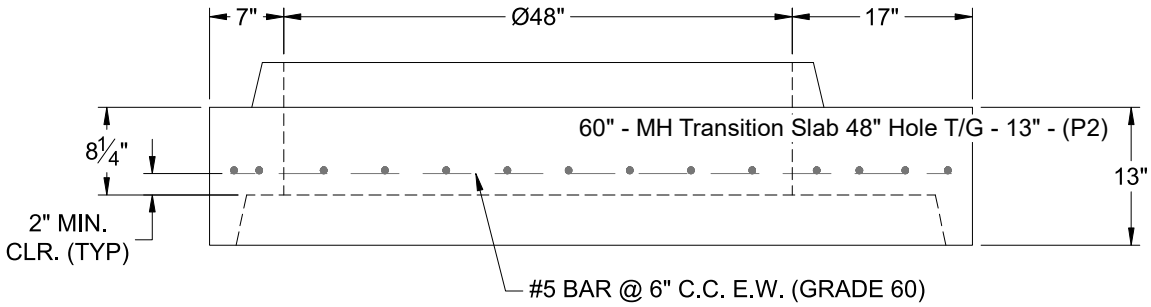

Coating (Int): Coating (Ext):	Seam Up: Tongue Seam Dn: Groove	Wall Thickness: 6"	Height (Ext): 13"	Weight (Net): 1928 lb Volume (Net): 0.49cu.yd
