Job Name: 25-0209 Garrison Gardens Job Location: Bowling Green, KY Contractor: Scotty's Contracting & Stone, LLC	Plant: 100 1/23/2026 4:36:15 PM	Tech: J. Horsley - A PC: Celina Goff	

Structure ID: CB 3-3

P3 MH060LD08-30SQ — MH FLAT TOP w/30"x30" Hole F/F

P4) 30" x 30" - CASTING HEIGHT - 4"	0 lb
P3) 60" - MH FLAT TOP w/30"x30" Hole F/F - 8"	2239 lb
P2) 60" - MH RISER Custom Ht F/G - 43"	4475 lb
P1) 60" - MH BASE T/n - 72"	8869 lb
1) CASTING - HOE 468 F/G	489 lb
2) 60" - Conseal CS-102 1.00"	0 lb
1) 30" x 30" - Conseal CS-102 1.00"	0 lb
2) Hole - 38	0 lb
1) Hole - 20	0 lb
1) Hole - 6	0 lb
6) MH Step ML-10-TDS-NCR - 10"	0 lb
Structure Total:	16072 lb

Structure Notes:
1. PER ASTM C-478 SPECIFICATIONS
2. CONCRETE: 4,000 PSI AT 28 DAYS
3. REINFORCEMENT: #5 BAR @ 6" C.C. E.W. (GRADE 60) - 2" MIN. REBAR CLEARANCE (TYP)
4. HOE 468 FRAME & GRATE SUPPLIED BY ICAST
5. LIFTERS: 4 EA. WRA016 CONAC WIRE ROPE ANCHORS FOR PLANT & FIELD HANDLING
6. TOP SURFACE TO RECEIVE FLOATED FINISH

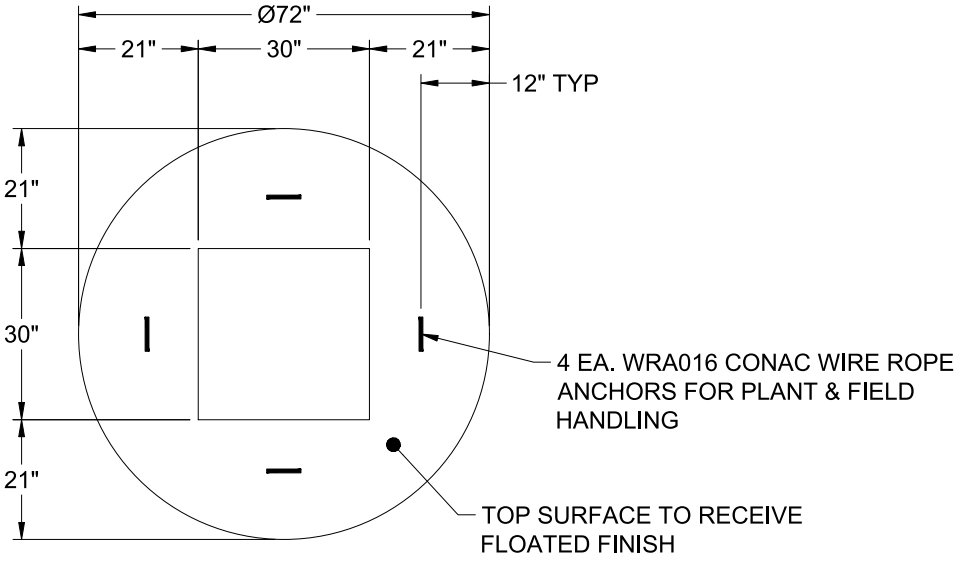



Coating (Int): Coating (Ext):	Seam Up: Flat Seam Dn: Flat	Wall Thickness: 6"	Height (Ext): 8"	Weight (Net): 2239 lb Volume (Net): 0.57cu.yd
