Job Name: 25-2727 - S English Station Storage Job Location: Louisville, KY Contractor: H&W Landwork	Plant: Beaver Dam, KY 2/3/2026 6:41:22 PM	Tech: J. Coppage - F PC: T. Lewis	

Structure ID: 10

P2 MH048LD12ECC — MH FLAT TOP w/ 24" ECC Hole F/G

P3) 24" - CASTING HEIGHT - 7"	0 lb
P2) 48" - MH FLAT TOP w/ 24" ECC Hole F/G - 12"	1561 lb
P1) 48" - MH BASE Custom Ht T/n - 30"	3255 lb
1) CASTING - HOE MC-420 F/C Storm LOU-MSD	340 lb
1) 48" - Conseal CS-102 1.00"	0 lb
2) Hole - 16	0 lb
3) MH Step ML-10-TDS-NCR - 10"	0 lb
Structure Total:	5156 lb

Structure Notes:
1. PER ASTM C-478 SPECIFICATIONS
2. CONCRETE: 4,500 PSI AT 28 DAYS
3. REINFORCEMENT: #4 BAR @ 10" C.C. E.W. (GRADE 60) - 2" MIN. REBAR CLEARANCE (TYP)
4. HOE MC-420 FRAME & COVER "STORM LOU-MSD" SUPPLIED BY ICAST
5. LIFTERS: 3 EA. WRA016 CONAC WIRE ROPE ANCHORS FOR PLANT & FIELD HANDLING
6. TOP SURFACE TO RECEIVE FLOATED FINISH

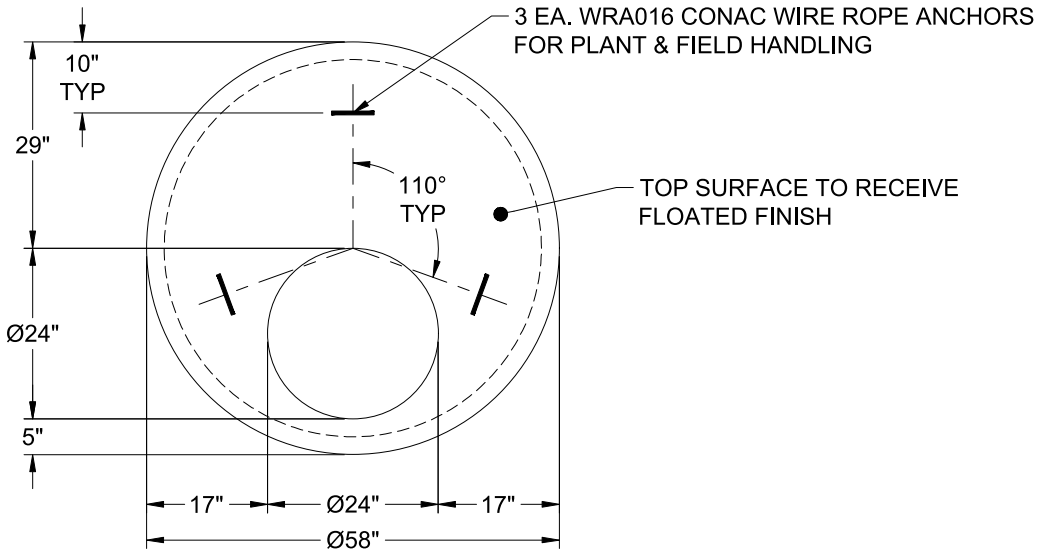



Coating (Int): Coating (Ext):	Seam Up: Flat Seam Dn: Groove	Wall Thickness: 5"	Height (Ext): 12"	Weight (Net): 1561 lb Volume (Net): 0.42cu.yd
